TOWN OF KILLINGLY PERMANENT BUILDING COMMISSION **SPECIAL MEETING**

Tuesday, April 16, 2024

7:00 p.m.

Town Meetin
Killing
172 I
Killing

A
Call of the Meeting and Roll Call **Town Meeting Room (In Person)** Killingly Town Hall 172 Main Street Killingly, CT 06239

AGENDA

2. Citizen Participation

This is an in-person meeting. Public can attend the meeting at the Town Hall. E-mailed public comment will still be accepted and presented at the meeting.

3. Adoption of Minutes:

None

- 4. Unfinished Business:
 - KMS Renovate As New with Addition Project
 - Downes project status update
 - 2. Consideration and Action on the approval of PCO#058 - Provide power to AC-2 units in corridors in an amount totaling \$1,109.00
 - Consideration and Action on the approval of PCO#260 Sitework Revisions -3. PR#14 in an amount totaling \$20,659.00
 - Consideration and Action on the approval of PCO#303 Kitchen Equipment 4. Relocaiton in an amount totaling \$6,556.00
 - 5. Consideration and Action on the approval of PCO#320 - Radon Pit Demolition in an amount totaling \$2,576.94 from a contractor back charge
 - Consideration and Action on the approval of PCO#321 Drop and Cut MEP 6. Systems in Manageable Sections Batch #07 in an amount totaling \$6,331.00 from **CM Contingency**
 - Consideration and Action on the approval of PCO#324 CMU Wall Infill at 7. HVAC Duct Opening in an amount of \$780.00 from CM Contingency
 - 8. Consideration and Concurrence on the award of KMS Move #4 to Meyer, Inc. in the amount totaling \$4,836.25
 - Westfield Avenue/Community Center Renovation Project
 - 1. Consideration and Action on the approval of Guaranteed Maximum Price Amendment #2 in the amount not to exceed \$19,114,721.00
 - 2. Consideration and Action on the approval of Abatement Monitoring for Pennoni in the amount of \$136,100.00

5. New Business: None

6. Other: None

- 7. Correspondence
- 8. Executive Session:

None

- 9. Council Member Reports
- 10. Adjournment

AGENDA ITEM COVER SHEET

ITEM 4(a):

KILLINGLY MEMORIAL SCHOOL RENOVATION/ADDITION PROJECT

PREPARED BY:

Mary Bromm, CD Administrator

ARCHITECT/ENGINEER:

Antinozzi Associates

CONSTRUCTION MANAGER:

Downes Construction

COMMISSIONING AGENT:

Consulting Engineering Services

ITEM SUMMARY:

The Commission will review change order proposals and formally award the bid for move #4 (the proposal was authorized by the Chair due to timing).

ACTION REQUESTED AT THE APRIL 16, 2024 MEETING:

Receive Downes project status update.

Review and if appropriate, approve PCO#058 – Power to AC-2 Units in Corridors

Review and if appropriate, approve PCO#260 - Sitework Revisions - PR#14

Review and if appropriate, approve PCO#303 - Kitchen Equipment Relocation

Review and if appropriate, approve PCO#320 - Radon Pit Demolition

Review and if appropriate, approve PCO#321 - Drop and Cut MEP Systems in Manageable Sections Batch 7

Review and if appropriate, approve PCO#324 - CMU Wall Infill at HVAC Duct Opening

Review and if appropriate, award Move #4 contract to Meyer, Inc.

SUPPORTING DOCUMENTS:

- Downes Project Agenda
- PCO#058
- PCO#260
- PCO#303
- PCO#320
- PCO#321
- PCO#324
- Meyer Proposal



Town of Killingly, CT
Killingly Memorial School Expansion & Renovation

Subject: Downes Construction Permanent Building Commission Agenda

1. Project Update

A. Project Financial Summary

GMP		\$	30,036,781.00	- (As of Amend. #03)
Approved Change Order Requests		\$	703,911.09	- (Thru PCCO #16)
Total Revised GMP @		\$	30,740,692.09	•
Pending/Approximate Change Order Requests			\$121,174.00	
Total Anticipated Final GMP		\$	30,861,866.09	•
Construction Manager's Construction Contingency	\$ 878,661.08			
Approved PCO's	\$ 340,623.53			
Pending PCO's2	\$ 6,331.00			
Approximate PCO's®	\$ (3,769.00)			
Remaining CM Contingency	\$ 535,475.55	w/GN	1P Above	
Owner's Contingency		\$	1,747,114.00	
Approved Changes		\$	703,911.09	
Pending Construction COP's		\$	28,324.00	Approval TBD
Approximate Construction COP's		\$	92,850.00	Approval TBD
Pending Soft Cost COP's		\$	_	
Remaining Owner's Contingency		\$	922,028.91	•
Owner's Soft Cost		\$	2,636,797.00	
Approved Change Order Requests		\$	-	
Pending		\$	-	
Revised Owner's Soft Cost		\$	2,636,797.00	t.)
Total Project Budget		\$	34,420,692.00	



Owner Conting'

Owner Conting'

Owner Conting'

2. Action Items

a. PCO's for review and approval:

PCO #21G - Drop Existing MEP to Floor & Cut into Pieces (\$6,331.00)
 PCO #58 - Supply Power to AC Units in Corridor Not Shown on E-Drawings (\$1,109.00)
 PCO #260 - Sitework Revisions PR#14 (\$20,659.00)
 PCO #320 - Radon Pit Demolition & Excavation (\$0.00)
 PCO #324 - Duct Penetration Infill (\$0.00)

PCO #303 - Kitchen Equipment Relocation - (\$6,556.00)

TOTAL \$28,324.00 Owner Contingency
TOTAL \$6,331.00 CM Contingency

b. PCO's Proceeding on T&M (Not to Exceed)

PCO #095A - Painting of Existing Wood Above Ceilings Part 2
 Owner Conting'

c. Approximate PCO's/Orders of Magnitude

PCO #16B - Eversource Transformer Re-Design (-\$6,779)

PCO #78 - DD Value Management Revisions (-\$26,747.00)

PCO #233- Elevator Card Access (\$5,015.00)

CM Conting'

Owner Conting'

Owner Conting'

PCO #249- Repairs to Existing Retaining Wall (\$36,330.00)

PCO #290 - Phase #2 Demo & Roof Changes (\$18,699.00)
 PCO #319 - Acoustical Ceiling Tiles in Gym (\$56,858.00)
 PCO #036 - Kitchen vendor cost to delay installation for 12 months, (\$7,000.00)
 PCO #95A - Removal / Painting of Wood Above Ceiling Part 2 (\$2,695.00)
 Owner Conting'
 Owner Conting'

PCO #35A - Removal / Painting of wood Above Centing fare 2 (\$2,035)
 PCO #326- Floor Wax Credit (-\$3,990.00)

(3,769.00) CM Contingency

TOTAL \$92,850.00 Owner Contingency

d. Rejected PCO's

TOTAL \$

· None to report at this time



e. Requisitions:

- Total Completed & Stored to Date through March 2024 \$24,031,134.04
- Percentage complete through March 2024, 78.24%
- Retainage held through March 2024, \$1,012,101.18

3. Schedule

a. Work Completed:

- Phase 4 Renovations
- Phase 5 MEP Rough In

b. Work in Progress:

- Phase 5 Flooring
- HVAC Rooftop Equipoment Installation
- Phase 5 Wall Patching

c. Work To Start:

- Kitchen Renovation
- Phase 6 Demolition / Abatement





Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 Phone: (860) 229-3755

Project: 25-01-0447 - Killingly Memorial School Killingly, Connecticut

Prime Contract Potential Change Order #058: CE #058 - Provide power to AC-2 units in corridors

TO:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	058 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM		CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	9/8/2023
REFERENCE:		PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No.	The Program of the Control of the Co	and the state of t
LOCATION:		ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:		PAID IN FULL:	No
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	- Commission - Com
	entitle til som	TOTAL AMOUNT:	\$1,109.00

POTENTIAL CHANGE ORDER TITLE: CE #058 - Provide power to AC-2 units in corridors

CHANGE REASON: Design Development

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract Is Changed As Follows)

CE #058 - Provide power to AC-2 Units in Corridors

Labor and material to provide power to (1) AC-2 unit in corridors 162,177,190,325 not shown on electrical plans.

ATTACHMENTS:

#	Budget Code	Description	Amount
1	001.26-100.S Construction.Electrical & Security System.Subcontractor	Electrical	\$1,062.00
2	001.60-504.M Construction.CM P&P Bonds.Material (Procore)	Bonds	\$7.00
3	001.60-503.M Construction.General Insurance.Material (Procore)	Insurance	\$8.00
4	001.90-001.M Construction.CM Fee.Material (Procore)	Fee	\$32.00
		Grand Total:	\$1,109.00

Antinozzi Associates

271 Fairfield Ave.

Bridgeport, Connecticut 06604

Town of Killingly

172 Main Street

Killingly, Connecticut 06239

Downes Construction-Company

200 Stanley St

New Britain, Connecticut 06051

DocuSigned by:

David Ferris

4/8/2024

DATE

SIGNATURE

DATE

Douglas Triba

DocuSigned by:

4/8/2024

SIGNATURE

DATE



CHANGE ORDER REQUEST SUMMARY

DICIN ELECTRIC COMPANY, INC.

DATE:

3/21/2024

156 Cross Road

DICIN JOB #:

647

Waterford, CT 06385

C.O. REQUEST #:

43

PROJECT: KILLINGLY MEMORIAL SCHOOL STATE PROJECT #069-0069 RNV

SUBCONTRACT NO.: BIS PACKAGE #2.26.1 ELECTRICAL

DESCRIPTION: RFI-97 - INSTALL CONDUIT & CONDUCTORS TO 3RD A/C UNIT;

TERMINATE CONDUCTORS TO UNIT AND SERVICE SWITCHES

SUBMITTED BY: Christopher Hersom

EMAIL: chris@dicinelectric.com

NOTES: Please reference attached backup for details

QUOTES				\$ -
MATERIAL				\$ 164.22
TOTAL MATERIAL				\$ 164.22
LABOR HOURS - FOREMAN - REG.	-	RATE:	\$ 103.69	\$ -
LABOR HOURS - JOURNEYMAN - REG.	8.25	RATE:	\$ 97.15	\$ 801.49
TOTAL LABOR				\$ 801.49
SUB-TOTAL				\$ 965.71
OH/PROFIT - DICIN WORK	·	10%		\$ 96. <u>57</u>
SUBCONTRACTOR WORK				\$ -
OH/PROFIT - SUBCONTRACTOR WORK		5%		\$
GRAND TOTAL				\$ 1,062.28

ADDITIONAL WORK AUTHORIZATION



DICIN ELECTRIC CO., INC.
156 CROSS ROAD
WATERFORD, CT 06385
860-442-0826 | DicinElectric.com

30956

OWNER'S NAME	trection	PHONE		DATE 2-	27-24
STREET	0.02500	JOB NAME	m.s.		JOB NUMBER
CITY STA	ТЕ	STREET	7.3.		
EXISTING CONTRACT NUMBER	DATE OF EXISTING CONTRACT	CITY		STA	TE
You are authorized to perform the following		A			0 0
Install co-				to 3,	-d A.C.
Unit. Tempale	- conducte	3 7	unit		walke
Suitales, RFJ			Ø.	ATERIAL	VERIFICATION
	1 Journey ma		DOWNE	SCONS	TRUCTION
26.24 8- 1/2" growner				MPANY	
Ma G - 3/a" =	+ bookly	532			
1.60 8 - 3/4" Em+	3/3 conn	.,	Downes Cons	truction Com	pany, LLC hereby
13.00 20'- 1/2" Green 29.98 2- 20 Tocale	tield ob	14,99			terials utilized for the decided. This verification of
			work performed	does not relie	eve the subcontractor
	"D 1/2" 3/0			ng with the co	ontract documents.
	eer that bear	y 1000	Upon review, if		beyond the scope of
	al tail (1/11			change order will
			Azol	nitect and/or l	Engineer!
43.96 4 - 3wtoch 8.84 4 - 12" Freen 4	1 lendle	106-7.5	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	-0	Hard Priced
8.16 9- 1/2" Freen	Cal get	Mr G	BY:	(88)	7/302 (1.01)
TUH122 material	troa 10	CO 2-10/ 4*1		199	1234
		MODIC I	DAIL.		1 00 34
ADDITIONAL CHARGE	FOR ABOVE	WORKE	5. 5		Service Control of the Control of th
Payment will be made as follows:					
Above additional work to be performed	under same conditions a	as specified in	original contract	unless other	erwise stipulated.
7/29/2124	g Signature		>		
Date Authorizin	g Signature		OWNER SIGNS HERE		
We hereby agree to furnish labor and m	aterials - complete in ac	cordance with	the above spec	ifications. a	t above stated price.
				, , ,	prince
Authorized Signature	(CONTRACTOR SIGNS HERE)		Date_		
THIS IS CHANGE O	RDER NO				
NOTE: This Revision becomes part of, and in conformance	e with, the existing contract.				





Search by Manufacturer, Part Number or Keyword



of quiest gliners

Stren New

Marriago Littera

Construence Const


Lancar Towns

Abuun

Carrier

Previous > Cooper 7949 Switch Lever Guard W/.25" Padlock Holes

Cooper 7949 Switch Lever Guard W/.25" Padlock Holes



Q Mouse over image to zoom, click to enlarge

Description:

Cooper 7949 Switch Lever Guard W//25" Padlock Holes





COOPER 7949 METAL SWITCH LVR GUARD | Gordon Electric Supply, Inc.

Technical Description.

Lever Guard Type; Flush Tumbler Metal Switch Used on; Finish Nickel Plated; Includes 1/4 Inch Padlock Hole

UPC: 04089304221

Part Number: 7949

Your Price: \$10.99 / ea

Total Available: In Stock

Qty: 1 ea

Production of the second second

Brand Name:

Eaton

Special Features:

Stainless steel

Sub Brand:

Eaton Wiring Devices

Type:

Industrial

CATALOG DESCRIPTION:

EATON SWITCH LEVER GUARD, 0.25 IN PADLOCK HOLES

Category:

Miscellaneous Wiring Devices

Full Size Image

Full Technical Description:

Lever Guard Type; Flush Tumbler Metal Switch Used on; Finish Nickel Plated; Includes

1/4 Inch Padlock Hole

Manufacturer:

Eaton Cooper Wiring-

Manufacturer

Brand:

Eaton Wiring Devices Industrial/Residential

Product _

Description:

Cooper 7949 Switch Lever Guard W/.25" Padlock Holes

Sub-Category:

AC Switch General Accessories

UNSPSC:

39121704

UPC 12 Digit:

040893042213

DocuSign Envelope ID: 23BB7798-6455-4174-BD05-EEC80DE13DD3 3/18/24, 6:49 AM COOPER 7949

COOPER 7949 METAL SWITCH LVR GUARD | Gordon Electric Supply, Inc.

Unique Product

Key:

6347128

comm code enhanced:

51800

Product Spec Sheet

Manufacturer Spec Sheet

Additional Image(s)

El y in @

JOIN OUR MAILING LIST

Email Address

t / 1.1

GORDON

Product Questions? (800) 892Shop All Electrical Box Covers

FREE Shipping on orders over \$50 after you sign in.

\$2.29 Qty: 1 Cart

A Back to top

Q

20ro

Search by keyword or model #

Get SAME-DAY SHIPPING on most orders placed by 4pm local time.

Home / Electrical Supplies / Electrical Boxes & Covers / Electrical Box Covers / Electrical Box Cover, Duplex Receptacle, Square, 2 Gangs, Galvanized Zinc, 1/2 in D, 4 in V Shop All Electrical Box Covers



P Share Product Image Feedback

RACO

Electrical Box Cover, Duplex Receptacle, Square, 2 Gangs, Galvanized Zinc, 1/2 in D, 4 in W, 4 in L

Mfr # 902C Zoro # G0362074

* * * * * 13 reviews | Write a Review

\$2.29_{/ea}









Free Same Day Pickup at 19 Locatio

Shopping Cart (8)

Subtotal	\$99.79
Order Total	\$99.79
THUE ARE	THE HEAT
Some items in your cart are not available and will cause your order to be held. Please r	eview your cart items.
Change All to Pickup	
roduct rice uantity	
Crouse-Hinds HGLL1 Malleable Iron Insulated Grounding Bushing 1/2-Inch	i i
SKU: 73598 3.28°5 / ea Qty (ea)	
- 8 +	Subtotal
	\$26.2
Delivery #	Pickup 🖶
72 on hand for delivery from Middletown, Ct - Estimated Delivery on Tuesday, March 19 th	13 on hand for pickup from New London, Ct - Pickup Monday, March 18 th <u>Change Branch</u>
dd Note	
Crouse-Hinds 451 Zinc Plated Steel Non-Insulated EMT Set Screw Straight Connector	r 3/4-Inch
0.20 ⁸¹ / ea Qty (ea)	
- 8 +	
	Subtota
	\$1.60
Delivery #	Pickup 🖶
- 8 +	\$:

https://www.aw.ct.com/chackgrit/cart/

SKU: 249594

FLEX-1/2-STEEL-UL-500 Liquidtight Flexible Conduit 1/2-Inch x 500-ft Reel

4 / 4

Shopping Cart | Electrical Wholesalers, Inc.

\$0.65⁵²/ea

Qty (ea)

.

Subtotal

\$0.66

Delivery #

0 on hand for delivery from Middletown, Ct - Call for availability

Pickup 🚍

0 on hand for pickup from New London, Ct - Out of stock. Call +1-860-357-6064 to confirm pickup.

Change Branch

This item is not available and will cause your order to be held.

Add Note



Leviton 1222-21 120/277-Volt AC 20-Amp 2-Pole Extra Heavy-Duty Industrial/Specification Grade Toggle AC Quiet Switch Ivory

SKU: 3985

\$14.99 / ea Qty (ea)

- 2 -

Subtotal

\$29.98

Delivery #

25 on hand for delivery from Middletown, Ct - Estimated Delivery on Tuesday, March 19th

Pickup 🖀

0 on hand for pickup from New London, Ct - Estimated Pickup on Tuesday, March 19th <u>Change Branch</u>

Add Note



Crouse-Hinds TP403 Steel Deep Outlet Box 4-Inch x 4-Inch x 2-1/8-Inch 30.3-Cubic-Inch

SKU: 66397

\$1.6110 /ea

Qty (ea)

Subtotal

\$6.44

Delivery @

22270 on hand for delivery from Middletown, Ct - Estimated Delivery on Tuesday, March 19th

Pickup 🚍

413 on hand for pickup from New London, Ct - Pickup Monday, March 18th Change Branch

Add Note



Metallics PT4012 Grounding Pigtail 12-AWG Green

SKU: 68377

Ĥ

\$0.7116 / ea

Qty (ea)

- 25 +

Sold in multiples of 25

Subtotal

\$17.79

Delivery 🚜

175 on hand for delivery from Middletown, Ct - Estimated Delivery on Tuesday, March 19 $^{\rm th}$

Pickup 🚍

0 on hand for pickup from New London, Ct - Estimated Pickup on Tuesday, March 19th Change Branch

Add Note

Arlington 4201 Die Cast Zinc Non-Insulated Throat Straight All-Purpose Greenfield Connector 1/2-Inch SKU: 57040 \$2.2101/ea

Qty (ea)

- 4 +

Subtotal

\$8.84

Delivery 🚚

2355 on hand for delivery from Middletown, Ct - Estimated Delivery on Tuesday, March 19th

Pickup 🚍

49 on hand for pickup from New London, Ct - Pickup Monday, March 18th
Change Branch

Add Note

Crouse-Hinds 736 Malleable Iron Non-Insulated 90-Degree Connector 1/2-Inch SKU: 24581

\$2.04²¹ / ea

Qty (ea)

4 +

Subtotal

\$8.17

Delivery 🚜

16 on hand for delivery from Middletown, Ct - Estimated Delivery on Tuesday, March 19 $^{\rm th}$

Pickup 🗖

0 on hand for pickup from New London, Ct - Estimated Pickup on Tuesday, March 19th

Change Branch

Add Note

COMPANY INFORMATION

About Us

Careers

Find a Branch

Services

Product Categories

Accessibility

ONLINE CUSTOMER SUPPORT

POLICIES & FAQS

CHECK OUT OUR MOBILE APPS!



Killingly MS Project DCC Job #25-01-0474 NOC Letter (PCO#058)

Town of Killingly 172 Main Street Danielson, CT

Building Committee Chairman:

We have received the following documents in association with this NOC letter - PCO# 058:

RFI #097

A review of the information indicates that the revisions (Wiring additional mini split head in (4) corridors – not shown on electrical plans) will result in an increase in the cost of work of approximately \$1,128.00. This estimate represents a not to exceed value for this work. Time and materials will be verified during this work and will determine the final pricing.

Confirming our meeting held today, we are proceeding with this work so as not to delay the project.

Sincerely,

Downes Construction Company

Doug Triba

Project Manager

Approval To Proceed

KMS Bldg. Committee Chairman

Cc: DCC Job File, Town of Killingly (Mary Bromm, Mary Calorio)



PCO #058

Downes Construction Company 200 Stanley St New Britain, Connecticut 06051

Project: 25-01-0447 - Killingly Memorial School Killingly, Connecticut

New Britain, Connecticut 06051 Phone: (860) 229-3755

Prime Contract Potential Change Order #058: CE #058 - Provide power to AC-2 units in corridors

TO:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	058 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM		CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	9/8/2023
REFERENCE:		PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No		
LOCATION:		ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:		PAID IN FULL:	No
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	
		TOTAL AMOUNT:	\$1,128.00

POTENTIAL CHANGE ORDER TITLE: CE #058 - Provide power to AC-2 units in corridors

CHANGE REASON: Design Development

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract Is Changed As Follows)

DATE

CE #058 - Provide power to AC-2 Units in Corridors

Labor and material to provide power to (1) AC-2 unit in corridors 162,177,190,325 not shown on electrical plans.

ATTACHMENTS:

#	Budget Code	Description	Amount
1	001.26-100.S Construction.Electrical & Security System.Subcontractor	Electrical	\$1,079.00
2	001.60-504.M Construction.CM P&P Bonds,Material (Procore)	Bonds	\$8.00
3	001.60-503;M Construction,General Insurance,Material (Procore)	Insurance	\$8.00
4	001.90-001.M Construction.CM Fee.Material (Procore)	Fee	\$33.00
		Grand Total:	\$1,128.00

Antinozzi Associates	Town of Killingly	Downes Construction Company
271 Fairfield Ave.	172 Main Street	200 Stanley St
Bridgeport, Connecticut 06604	Killingly, Connecticut 06239	New Britain, Connecticut 06051

SIGNATURE

SIGNATURE

DATE

SIGNATURE

DATE



Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 P: (860) 229-3755

Project: 25-01-0447 Killingly Memorial School Killingly, Connecticut

RFI #97: AC-2 unit quantity's

Status

Closed on 05/02/23

To

David Ferris (Antinozzi Associates)

Kevin Matis (Antinozzi Associates)

From

Jason Scarano (DICIN Electric Co., Inc.)

Date Initiated

Apr 17, 2023

Due Date

Apr 20, 2023

Location

Project Stage

Cost Impact

Schedule Impact

Spec Section

Cost Code

Drawing Number

E-101.2 M-101.2

Reference

Linked Drawings

Received From

Jason Scarano (DICIN Electric Co., Inc.)

Sub Job

Copies To

Alison Burzdak (P & D Mechanical, Inc.), Cindy Hersom (DICIN Electric Co., Inc.), Eric Fontaine (Downes Construction Company), Chris Hersom (DICIN Electric Co., Inc.), Dominic Madigan (Downes Construction Company), Jason Scarano (DICIN Electric Co., Inc.), David Warzecha (P & D Mechanical, Inc.)

Activity

Question

Question from Jason Scarano DICIN Electric Co., Inc. on Thursday, Apr 13, 2023 at 01:43 PM EDT

On drawing M-101.2 it shows 3 AC-2 units in each of the following corridor's 162,177,190,325. On drawing E-101.2 the same

corridor's only have 2 AC-2 units shown. Will the electric drawings need to be updated with added units?

Official Response

Response from Kevin Matis Antinozzi Associates on Tuesday, May 2, 2023 at 08:17 AM EDT

Proceed as directed by engineer.

Official Response

Response from Sherman Taylor Salamone & Associates, PC on Tuesday, Apr 25, 2023 at 09:44 AM EDT

Connect the third AC-2 to the same circuit as the adjacent ACs. (keep all units in the same corridor together)

All Replies

Response from Kevin Matis Antinozzi Associates on Tuesday, May 2, 2023 at 08:17 AM EDT

Proceed as directed by engineer.

Response from Sherman Taylor Salamone & Associates, PC on Tuesday, Apr 25, 2023 at 09:44 AM EDT Connect the third AC-2 to the same circuit as the adjacent ACs. (keep all units in the same corridor together)



CHANGE ORDER REQUEST SUMMARY

DICIN ELECTRIC COMPANY, INC.

DATE:

6/29/2023

156 Cross Road

DICIN JOB #:

647

Waterford, CT 06385

C.O. REQUEST #:

5

PROJECT: KILLINGLY MEMORIAL SCHOOL STATE PROJECT #069-0069 RNV

SUBCONTRACT NO.: BIS PACKAGE #2.26.1 ELECTRICAL

DESCRIPTION: RFI #97 - CONNECT THIRD AC-2 UNIT (ONLY TWO AC-2 UNITS

SHOWN ON DWG. E-101.2, THREE ARE SHOWN ON DWG. M-101.2)

SUBMITTED BY: Christopher Hersom

EMAIL: chris@dicinelectric.com

NOTES: Please reference attached backup for details

QUOTES		\$	49
MATERIAL		\$	179.40
TOTAL MATERIAL		\$	179.40
LABOR HOURS - JOURNEYMAN - REG.	8.25 RATE: \$	97.15 \$	801.49
TOTAL LABOR		\$	801.49
SUB-TOTAL		\$	980.89
OH/PROFIT - DICIN WORK	10%	\$	98.09
SUBCONTRACTOR WORK		\$	•
OH/PROFIT - SUBCONTRACTOR WORK	5%	\$	-
BOND	0.97%	- 5	10,97
GRAND TOTAL			1,000.44
			\$1,079.00



Summary by Subtotal

JOB-0184 KILLINGLY MEMORIAL SCHOOL

Job ID: Project:

Vendor: TRADE/3-COL	703		Labor Level: UABOR 1	OR 1				29 Jun 2023	14:10:43
			は一番の一番の	The state of	CANCOL STATE				77.
Subtotal 10 - RIGID FITTINGS	FITTINGS								
Mern # Size 40127 1/2	Description GRND BUSHING INSULATED	S Z	Quantity U/M 8.00 EA	Med Unit 6.0900	Mot Result 48.72	Lab Unit 0.2500	Lab Result 2.00	Quo Unit	Ono Result
			Subtotal totals:		48.72		2.00		0.00
Subtotal 11 - EMT FITTINGS	TINGS								
Nem # Size 30624 3/4	Description EMT STEEL 8S CONNECTOR	82	Quantity USI 8.00 EA	Mat Unit 02100	Mad Result 1.68	Lath Unit 0.1000	Leb Resuft 0.80	Que Unit	Quo Result
C. block 144 El Exibit E CONDITI	Figure		Subtotal totals:		1.68	=	0.80		0.00
Henrik Size		ē							
50001 1/2	FLEXIBLE STEEL CONDUIT	2 2	Quentity URI 20.00 FT	0.9800	Met Result 13.20	Leb Unit 0.0400	Lab Result 0.80	Quo Unit 0,0000	Quo Result 0.00
			Subtotal totals:		13.20		0.80		0.00
Subtotal 21 - DEVICES	on un								
Nem # Size 140453 20A	Description 2P TOGGLE SPECIFICATION-GRADE	2	Quantity UM 2.00 EA	Mai Unft 8.5400	Mat Resuft 17.08	Leb Unit 0.3500	Lab Result 0.70	Oxo Unit 0.0000	Quo Result
			Subtotal totals:		17.08		0.70		0.00
SUBTOTAL 23 - SIEEL BOXES	BOXES								
florm \$ Size 150041 2-1/8"D 15009B 1/2"D 7.3-CI	Description 4"SQ CMB-KO NO BPKT 4"SQ 1-8W RAISED CVR	822	Quantity (UN) 4.00 EA 4.00 EA	Mad Unit 1,5800 1,6200	Mot Result 6.24 6.48	Leb Unit 0.3000 0.2000	Lab Result 1.20 0.60	Que Unit 0.0000 0.0000	Quo Result 0.00
Subtotal 24 - THUNTHAM CI	TO NAME.		Subtotal totals:		12.72		2.00		0.00
The state of the s									
from # Size 70033-12	Description THHNTHWN CU (STR)	52	Quantity USS 100.00 FT	Mail Unite 0.1600	Mat Regult 16.00	1.ab Unit 0.0060	Lab Result 0.60	Que Unit 0.0000	Quo Result 0.00
			Subtotal totals:		16.00		0.60		0.00
Subtotal 42 - WIRE TERMINATIONS	ERMINATIONS								
them # Stze 100151 #12 SOL	Description 6-12" PISTAIL WIGRD SCREW	8	Quantity UM 4.00 EA	Offer Unit 0.7100	Mat Result 284	Lab Unit 0.0500	Lab Result 0.24	Cuo Unit 0.000	Quo Regult 0.00
Subtotal 109 - GEAR & DANE! ACCVS	% DACKS		Subtotal totals:		2.84		0.24		0.00
170577	Description BRKR HANDLE LOCK	5≥	Quentity UM 4.00 EA	Mat Unit 11.0000	Mail Result 44.00	Lab Unit 0.0130	Lab Result 0.05	Otto Unit 0.0000	Quo Result 0.00
Dicir Electric Co.	6 1	5	8		0. 5		C-0831		

Page 1 of 2

29 Jun 2023, 14:10:43	0.00	Que Unit Que Result 0.000 0.000 0.000	11	-	
	0.05	Lab Unit Lab Result 0.1440 0.58 0.1200 0.48	1 1	Grand Material, Quote, Equipment, and Subconfract Total:	Phone: 850-442-0826 Web: www.DigmEllectric.gm
	44.00	3.5600 Nat Result 3.5600 14.36 2.2000 8.60	23.16	Grand Material, Quot	
	Subtotal totals:	O/M Quantity U/M M 4:00 EA M 4:00 EA	Subtotal totals: Job totals:		Asb Cross P. 1
Summary by Subtotal: KILLINGLY MEMORIAL SCHOOL	ND FITTINGS	Description FLEX COND ANGLE CONN FLEX COND STRAIGHT CONN			ASE CRO
Summary by Subtotal	Subtotal 112 - FLEX COND FITTINGS	Nern # Size 50030 1/2 50041 1/2		S C C C C C C C C C C C C C C C C C C C	

Page 2 of 7

6/23/23, 8:55 AM

Shopping Cart | Electrical Wholesalers, Inc.









	Carodavillus: Our Commitment to Our Employees
Shopping Cart (10)	
Order Summary	
Subtotal	\$199.01
Order Total	\$199.01
Change All to Pickup	
Product Price Quantity Subtotal	
Crouse-Hinds MGLL1 Malleable Iron Insulated Grounding Bushing 1/2-Inch SKU: 73598	
\$6.09 /ea Qty (ea)	
- 6 +	
	Subtotal
Dallitoni de	\$36.54
Delivery 🚒 88 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26 th Pickup 🚍	
15 on hand for pickup from New London, Ct - Available for immediate pickup <u>Change Bra</u>	nch
Add Note	
Crouse-Hinds 451 Zinc Plated Steel Non-Insulated EMT Set Screw Straight Connector 3/4-Inch	— -
\$0.21/en	
Qty (ea)	
- 8 +	
	Subtotal
	\$1.68_
Delivery ••• — 20241 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26 th Pickup Pickup	
226 on hand for pickup from New London, Ct - Available for immediate pickup Change Br	ench
Add Note	

SKU: CW487

Reduced Wali Flexible Conduit 1/2-Inch

Change Branch

Add Note

11451 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26th

365 on hand for pickup from New London, Ct - Available for immediate pickup

6/23/23, 8:55 AM

Shopping Cart | Electrical Wholesalers, Inc.

Crouse-Hinds TP512 Steel Raised Surface Cover With (1) Toggle Switch Opening 4-Inch x 4-Inch x 1/2-Inch SKU: 56824 \$1.62/63 Qty (ea) Subtotal \$6.48 Delivery 🚚 682 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26th Pickup 🚍 53 on hand for pickup from New London, Ct - Available for immediate pickup Change Branch **Add Note** WCU-THHN-12-CU-STRANDED-WHITE-500 Stranded Copper THHN Cable 12-AWG 500-ft Spool White SKU: 9066 \$0.16 /ea Qty (ea) 500 + Sold in multiples of 500 Subtotal \$80.00 Delivery 🚒 80500 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26th Pickup 🚍 4500 on hand for pickup from New London, Ct - Available for immediate pickup Change Branch Add Note Û Metallics PT4012 Grounding Pigtail 12-AWG Green SKU: 68377 \$0.71 /ea Qty (ea) 25 Sold in multiples of 25 Subtotal \$17.75 Delivery 🚒 965 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26th 0 on hand for pickup from New London, Ct - Estimated Pickup on Monday, June 26th Change Branch Add Note Crouse-Hinds 736 Malleable Iron Non-Insulated 90-Degree Connector 1/2-Inch SKU: 24581

https://www.ew-ct.com/checkout/cart/

\$3.59 / 68

6/23/23, 8:55 AM

Qty (ea)

Shopping Cart | Electrical Wholesalers, Inc.

Subtotal

\$14.36

Delivery #

50 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26th

Pickup 🚍

0 on hand for pickup from New London, Ct - Estimated Pickup on Monday, June 26th

Change Branch

Add Note

Arlington 4201 Die Cast Zinc Non-Insulated Throat Straight All-Purpose Greenfield Connector 1/2-Inch SKU: 57040 Û

\$2.20/ea

Qty (ea)

-- 4 -

Subtotal

\$8.80

Delivery 🚜

345 on hand for delivery from Middletown, Ct - Estimated Delivery on Monday, June 26th

Pickup 🖀

10 on hand for pickup from New London, Ct - Available for Immediate pickup Change Branch

Add Note

COMPANY INFORMATION

About Us

Careers

Find a Branch

Services

Product Categories

Accessibility

ONLINE CUSTOMER SUPPORT

POLICIES & FAQS

CHECK OUT OUR MOBILE APPS!





Our Affiliations







© 2023 Electrical Wholesalers, Inc.



7949 - Switch Lever Guard W/.25" Padlock Holes

Eaton

\$11.00 (Each)

\$11.00 (Each)

\$1,100.00 (Per 100)

Availability: in Stock

QTY: 1

Suy Jan

EES Spec Sheet

Suggest Changes

	A CONTRACTOR OF THE PROPERTY O	
Quick Specs	<u>⊦.</u> ∯ Help Impo	rove Our Da
Catalog Number	7949	
Manufacturer	Eaton	
Manufacturer's F	mber 7949	
Description	Switch Lever Guard W/.25" Padiock Holes Switch Lever Guard, 0 Gang, 1.44 (W) X 4.19 (H) In, Polycarbonate Material, Jack Adapt Sand, Lever Actuator, 0.0005 LB	ter Connec
Slang Terms		
Similar Brands		
Categories	Gen Purpose Wiring Devices - Misc Wiring Devices	
Classification	Residential Switches	
UNSPSC	39121704 - Wallplates	
UPC/GTIN	040893042213 / 00040893042213	
Weight per unit	o	
rice & Packaging		
Minimum Order C	y 1	
Unit	\$11.00 (Each)	
Standard Package	\$1,100.00 (Per 100)	
esources		
Images		
	- 7949 - Small Image	
	₹ 7949 - Large Image 1. The second of the second o	
Altachments		
	7949 - Specification Sheet	
	12 7949 - Specification Sheet	
	1.5.7949 - Specification Sheet	
Specifications She		
	्र. <u>7949</u> - Specification Sheet	
		ve Our Data



7949 - Switch Lever Guard W/.25" Padlock Holes

Eaton

\$11.00 (Each)

\$11.00 (Each)

\$1,100,00 (Per 100)

Availability: In Stock

QTY: 1

Each Stg/ .*s-

上 EES Spec Sheet

Suggest Changes

	Specifications Co	rrent Stock	
Quick Spe	cs		Help Improve Our Da
Ceta	log Number	7949	
Man	ufecturer	Eaton	
Man	ufacturer's Part Number	7949	
Desc	cription	Switch Lever Guard W/.25" Padlock Holes	
		Switch Lever Guard, 0 Gang, 1.44 (W) X 4.19 (H) In. Polyce Sand, Lever Actuator, 0.0005 LB	arbonate Material, Jack Adapter Connec
Stang	g Terms		
Simil	ar Brands		
Cate	gories	Gen Purpose Wiring Devices - Misc Wiring Devices	
Class	sification	Residential Switches	
UNS	PSC	39121704 - Wallpfates	
UPC/	GTIN	040893042213 / 00040893042213	
Weigl	ht per unit	0	
rice & Pac	kaging		
Minin	ium Order Quantity	1	
Unit		\$11.00 (Each)	
Stand	lard Packaging	\$1,100.00 (Per 100)	
esources			
lmage	25		
		7949 - Small Image	
		○ 7949 - Large Image	
Altach	nments		
		14 7949 - Specification Sheet	-
		2: 7949 - Specification Sheet	
		7949 - Specification Sheet	
Specil	ications Sheets	-	
		4.7949 - Specification Sheet	

Help Improve Our Date





Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 Phone: (860) 229-3755

Project: 25-01-0447 - Killingly Memorial School Killingly, Connecticut

Prime Contract Potential Change Order #260: CE #260 - Sitework Revisions - PR#14

то:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	260 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM		CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	1/25/2024
REFERENCE:		PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No		Notes-par-apphinate-parameters and the second state of the second
LOCATION:		ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:	-phorestia	PAID IN FULL:	No .
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	an hitiga atau atau da
	engleight little de un na mar eann eangleight little de little general pair de little getaleg jub mei war septon uit	TOTAL AMOUNT:	\$20,659.00

POTENTIAL CHANGE ORDER TITLE: CE #260 - Sitework Revisions - PR#14

CHANGE REASON: Design Development

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract is Changed As Follows)

CE #260 - Sitework Revisions - PR#14

Labor and material to perform revisions to the site as shown in PR #14. Scope includes:

- Prepare subgrade, form & pour sidewalk at west field access point with ADA ramp and detectable tile.
- Installation of (2) 4ft wide pedestrian gates.
- Line striping cross walk and area around catch basin adjacent to west field access.
- Saw cut & removal of existing pavement areas at outbuilding on east side of property. Preparation of subgrades and paving as shown at (2) locations.
- Installation of (3) "Reserved for Admin Staff" signs in front of building parking spots.

Current plan is to pour the sidewalk for west field access in early spring so grading can be completed and seeding during planting season.

ATTACHMENTS:

#	Budget Code	Description	Amount
1	001.31-100.S Construction.Sitework.Subcontractor	Sitework	\$19,770.00
2	001.60-504.M Construction.CM P&P Bonds.Material (Procore)	Bonds	\$138.00
3	001.60-503.M Construction.General Insurance.Material (Procore)	Insurance	\$149.00
4	001.90-001.M Construction.CM Fee.Material (Procore)	Fee	\$602.00
		Grand Total:	\$20,659.00

Antinozzi Associates	Town of Killingly	Downes Construction Company
271 Fairfield Ave.	172 Main Street	200 Stanley St
Bridgeport, Connecticut 06604	Killingly, Connecticut 06239	New Britain, Connecticut 06051

DocuSigned by:

SIGNATURE

David Terris

4/8/2024

DATE

SIGNATURE

DATE SIGNA

DocuSigned by:

4/8/2024

DATE



Proposal Request

PROJECT: (name and address)

Killingly Memorial School

Expansion and Renovation Project

339 Main Street

Danielson, CT 06239

Town of Killingly

Danielson, CT 06239

OWNER: (name and address) 172 Main Street

Bridgeport, CT 06604

ARCHITECT: (name and address) Antinozzi Associates, P. C. 271 Fairfield Avenue

CONTRACT INFORMATION:

Constructor with a GMP

Date: July 06, 2022

Contract For: Construction Manager as

New Britain, CT 06051

200 Stanley Street

2023

Architect's Project Number: 21025

Proposal Request Number: 014R1

Proposal Request Date: November 20,

CONTRACTOR: (name and address)

Downes Construction Company

The Owner requests an itemized proposal for changes to the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. The Contractor shall submit this proposal within seven (7) days or notify the Architect in writing of the anticipated date of submission.

(Insert a detailed description of the proposed modifications to the Contract Documents and, if applicable, attach or reference specific exhibits.)

Provide a proposal for the following Site related changes requested by the Owner:

- 1. Curb Ramp at Northwest Corner of building.
- 2. New Gate, paved access, and striped crosswalk to exisiting West Playfields
- 3. Asphalt pavement access to adjacent site Building
- 4. Administrative Parking Signs at front Parking Lot

Please provide a proposal enumerating the changes to your contract as a result of this proposal.

ATTACHMENTS:

Drawings

104 C-104 - SITE MATERIALS PLAN Rev 5 -

105_C-105 - SITE GRADING AND DRAINAGE PLAN Rev 5

Specifications

NONE

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE, OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

REQUESTED BY THE ARCHITECT:

Michael LoSasso, AIA, LEED AP, BD+C, Principal


PRINTED NAME AND TITLE

AIA Document G709 - 2018. Copyright @ 1993, 2001 and 2018. All rights reserved. "The American Institute of Architects," "American Institute of Architects." "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:45:41 ET on 11/20/2023 under Order No.4104244980 which expires on 09/01/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@alacontracts.com. (3B9ADA4D)

PHASE 2 OF 3 339 MAIN STREET DANIELSON, CT 06239 STATE PROJECT NO.: 069-0069 RNV

EXPANSION AND RENOVATION KITINCIA MEMOBIAT SCHOOF

C-104 took the took

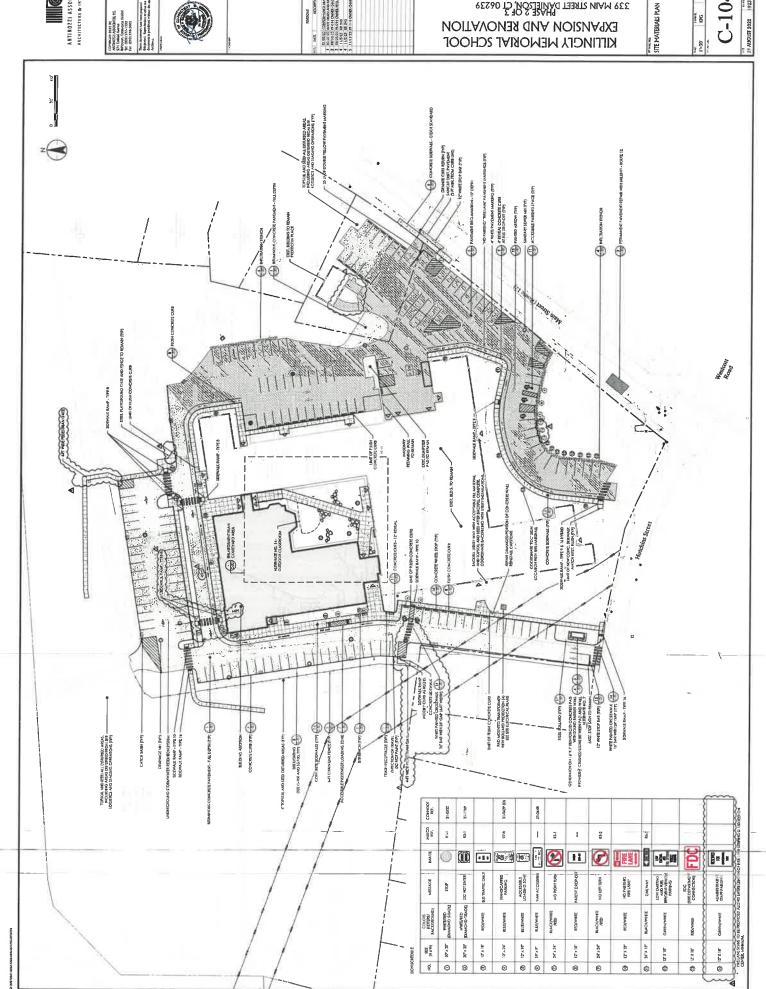


ANTINOZI ASSOCIATES
ACANTECTURE DITERIORA

STATEMENTO SOCIATE
ANTINOSI MASSOCIATE
ANTI

HASE 2 OF 3 339 MAIN STREET DAVIELSON, CT 06239 STATE PROJECT NO.: 069-0069 RNV

EXPANSION AND RENOVATION KILLINGLY MEMORIAL SCHOOL

SITE CAUGHG AND DEVINAGE PLAN IN THE PLAN

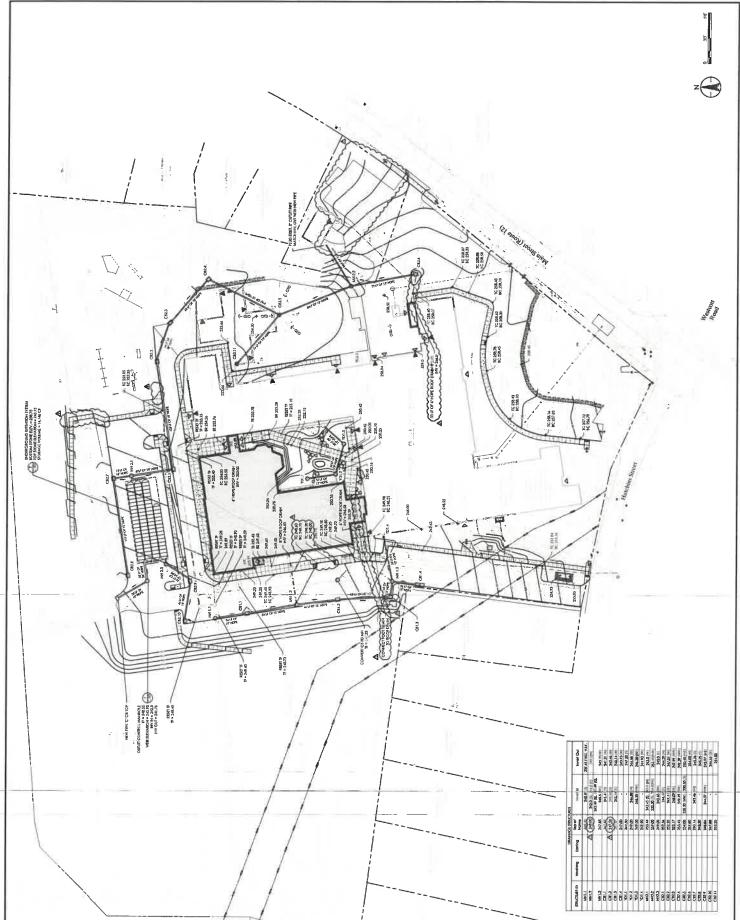

REVISED CHANGE ORDER PROPOSAL WORKSHEET

To: Douglas Triba From: Mather Corporation

Project: Killingly Memorial School Phase 2 Date: 2/22/2024

Killingly, CT 06239 Ref. Doc.: PR #14 Rev. Site Plans 11/13/2023 C-104/105

Description: PR #14 Site Changes - New pavement at the east existing out building, added signs at staff parking, added line striping for crosswalks/hatching, added two gates in existing and new fencing, added

sidewalk and handicap ramp at west field entrance.

Quant. Unit		Description of Material and Equipment	U	nit Cost	Total	
					\$	-
		Materials			\$	-
2	ton	Bituminous Concrete	\$	79.00	\$	158.00
24	ton	Processed base	\$	19.00	\$	456.00
3	су	Concrete for sidewalks	\$	170.00	\$	510.00
1	ea	Short Load Charge for concrete	\$	200.00	\$	200.00
1	ea	2' x 4' ADA domes tiles brick red.	\$	350.00	\$	350.00
24	ton	tipping fees for bituminous concrete and box out material	\$	10.00	\$	240.00
150	sf	wire mesh	\$	0.25	\$	37.50
			\$	_	\$	-
0		Equipment			\$	-
8	hr	Cat M322 Rubber tire excavator	\$	130.00	\$	1,040.00
8	hr	Triaxle dump truck	\$	115.00	\$	920.00
4	hr	earth roller	\$	75.00	\$	300.00
					\$	_
ine #1	Mate	rial and Equipment Subtotal			\$	4,211.50

Crew	Labor Classification	Hours	Base Rate	Tax	Fringe	Pension	Wrkrs Comp.	Total Rate	Total
1	Foreman	8						98.67	\$ 789.36
2	Laborer	16						72.95	\$ 1,167.20
1	Operator	8						94.90	\$ 759.20
									\$ _
Line #2	Labor Subtotal								\$ 2,715.76


Line #3 Total Labor, Materials and Equipment \$ 6,927.26

	-	Allow		
Line #3 Amt	Overhead and Profit % Mark-up on Own Work	%	Applicable %	Total
		10%	N/A	\$ 692.73
Line #4 Total	Mark-up on Contractor's Own Work			\$ 692.73

Subcontractor	Cost	
Trade	Name of Subcontractor	Total
Paving	Advanced Resources - fine grading and paving.	\$ 3,001.05
Concrete walk	Apontes Construction Resources - concrete sidewalks and curbing.	\$ 1,070.00
Line striping	Onsite Services line striping and signage.	\$ 3,400.00
Fencing	Eagle Fence for gate installation at new and existing fence.	\$ 3,250.00
Sawcutting	Pro-Cut for cutting bituminous parking lot	\$ 850.00
Line #5 Subo	contractor Total	\$ 11,571.05

Line #6	Contractor's Mark-up on Subcontractor Work (see note below)	5%	\$ 578.55

Line #7	Total Proposed Change Order Amount	\$ 19,769.59





Jolley Concrete Inc. & Brooklyn Sand and Gravel LLC.

42 Junior Ave.

Danielson Ct. 06239

860-779-3980, 860-774-3872 Fax

moe@jolleyconcrete.net

QUOTE DATE

8/29/23

DATE PRINTED

CUSTOMER ID

QUOTE EXPIRATION DATE Thursday, September 28, 2023

Mather Corporation 21 West Dudley Town Road Bloomfield, Connecticut 06002 860-761-2209 Direct line

Project name:

Phase 2

Killingly Memorial School







Job Contact	phone	email	revised date	
Mike Lawson	860-250-6398	mikelawson@mathercorp.com		2022
QTY	UNIT	DESCRIPTION	UNIT PRICE	LINE TOTAL
22.00	Ton	1 1/4" Processed gravel M.02.06 A	\$19.00	\$418.00
-	A 3-99988			
		etrologistation photosistic production of the second descriptions and	-	elellitetumentellit smeldentelenin
in a riber videate		Annual production by the state of the state		Value bille de l'immer ve bille de l'en e
oman-night fligh yellingiglishi quagetti. All hillingin. Brown-planned (III d. pp)	****			helin
		etano/		
		To a service and the service a	-	and the same of th
		pperantement		half-princes (Maybrown Sylve Shing)
		den er en defende for som degelde for som degelde for former degelde for som d	The state of the s	shifted and the contract
		AL CHARLE		
			1	

Quotation prepared by: Moe LaPierre General Manager

sales tax & pallets not included

TOTAL

418.00

If required:

To accept this quotation, sign here and return:

Ready Mix Concrete Conrete Block, Bag cements Pavers and Aggregates!!

Service Sells!

Versa-Lok

Segmental Walls

Sand & Stone

Wire products





Jolley Concrete, Inc.

42 Junior Ave

Danielson, CT. 06239

860-774-5000, 860-774-3872 fx tjolleyconcrete@gmail.com

Mather Corporation 21 West Dudley Town Rd Bloomfield CT 06002 P: 860 761 2209

F: 860 242 1493

QUOTE DATE 1/16/24 **DATE PRINTED** 1/16/24

CUSTOMER ID

Project name:

QUOTE EXPIRATION DATE

Killingly Memorial School





\$ [C

		'MARKATON COLOR OF THE COLOR OF				
Job Contact	phone	email	revised	sales	start date	
Mike		mikelawson@mathercorp.com			2023	

QTY			UNIT PRICE		LINE TOTA
3	CYD	4400 PSI Class F PCC04460	\$170.00	historia di Barathina di Gili	\$510.00
	an-vyddddynmaddilae;	The indifference of the contract of the contra	and the second dependence is a substitution of the second		
	CYD	Super Plasticizer (Glenium 7500)	at request	1.	
MARKET	100000000000000000000000000000000000000	> 3oz. To 5oz./cwt	\$4.00	ple control (Ching) of pri (China	
		> 5oz. To 8oz. / cwt			
		> 8oz. To 12oz. /cwt	\$8.00	ye hine djardjardjardjardjardj	
unione adv	Per	Fuel Surcharge per mile to job subject to change in fuel cost	\$2.50		projekt-rhu
	CYD	Nycon Fiber Reinforcement	\$8.00	ti englishimata mindi et	
	CYD	Non-chloride-accelerator-1%	\$5.80		***************************************
	CYD	Non-chloride accelerator 2%	\$11.60		and the second of the second
	CYD	HOT WATER	\$6.00	pur quipuritipus	
		DELIVERY CHARGES/ SHORT LOAD		Allega a selfundo digeno a mano	
1	CYD	1 - <2	\$280.00		\$200.00
				the reduct	
I time allowed is	6 minutes per	vard on the truck			NAMED AND ASSESSED OF THE SECOND OF THE SECO
ation prepared by	: Tom	sale	es tax & pallets no	SUBTOTAL t included	\$710.00
uired:		and return:		TOTAL	\$710.00

Ready Mix Concrete
Concrete Block, Bag cements
Pavers

Versa-Lok

Segmental Walls
Sand & Stone
Wire products



Detectable Warning Products, Inc 4600 Summerlin Rd C-2 / 421 Fort Myers, FL 33919 (401)473-5584 http://www.dwpnow.com

Ship To Name Mather Corporation

Address/Ship To

Bill To Name Mather Corporation 21 West Dudley Town Road Bloomfield, Connecticut 06002

United States
Ship To United States

Contact Name Mike Lawson

Other Information

Quote Number 00019969 Quote Date 1/10/2024

Composite WET SET Detectable Warning ADA Solutions 2x4 / Safety Brick Red \$350.00 Each X 1 each.

Subtotal \$350.00
Discount 0.00%
Total Price \$350.00
Tax \$0.00
Shipping and handling \$0.00
Grand Total \$350.00

Thank you for Considering our Company.
Remember: We will BEAT ANY PRICE while still Providing FREE DELIVERY
and the BEST CREDIT TERMS IN THE INDUSTRY!!!

Accepted by & Date



An equal opportunity, affirmative action employer. (DAS CERTIFIED MBE) 305 BUTLERTOWN RD OAKDALE, CT 06371

PROPOSAL-CONTRACT

COMPANY: MATHER CORP.	EMAIL: mikelawson@mathercorp.com
CONTACT: MIKE LAWSON	PROJECT: KILLINGLY MEMORIAL SCHOOL
ADDRESS: 21 West Dudley Town Rd., Bloomfield	LOCATION: KILLINGLY, CT
PHONE: 860-250-6398	DATE: 1/15/2024

ADVANCE RESOURCES CONTACT: BILL CHAMPAGNE

1). FINE GRADE BASED ON 600 SF	\$ 1.30 P/SF - \$780.00
2). 2" HMA S0.5 BINDER	\$16.25 P/SY - \$1,088.75
3). 2" S0.375 WEARING SURFACE	\$16.90 P/SY - \$ 1,132.30
TOTAL	\$3,001.05

- A), ASPHALT ESCALATION BASED ON CURRENT \$585.00
- B), PRICES GOOD THROUGH 10/30/24.
- C). NIGHT AND WEEKEND PLANT OPENINGS WILL BE BILLED ADDITIONALLY @ \$2,000.00 EACH.

THIS SIGNED PROPOSAL / CONTRACT MUST BE MADE AN ADDENDUM TO ANY SUBCONTRACTOR AGREEMENT.

- THIS CONTRACT CONSTITUTES THE ENTIRE AGREEMENT BETWEEN PURCHASER AND ADVANCE RESOURCES LLC.
- ADVANCE RESOURCES LLC IS NOT RESPONSIBLE FOR ANY DELAYS BEYOND OUR CONTROL, I.E. FIRE, FLOODS, WEATHER, ACCIDENTS, STRIKES, WAR AND OTHER SIMILAR CAUSES.
- WHEN EXTRA WORK IS REQUIRED, OUTSIDE OF THE SCOPE OF THE CONTRACT, REASONABLE COMPENSATION IS NECESSARY AND UNDERSTOOD. THIS WILL BE DISCUSSED WITH OWNER OR GENERAL CONTRACTOR IF THE SITUATION ARISES.
- IF ADVANCE RESOURCES LLC DOES NOT GRADE THE BASE, WE RESERVE THE RIGHT TO INSPECT SAID

 BASE AND DECLARE IT UNSUITABLE FOR ASPHALT. THE PURCHASER AND ADVANCE RESOURCES LLC

 WILL DISCUSS THE SITUATION AND DECIDE HOW IT CAN BEST BE REMEDIED. IE AR DOES ADDITIONAL

 WORK TO BASE, NOT INCLUDED IN CONTRACT, AN ADDITIONAL CHARGE WILL BE INCURRED.
- AR IS NOT RESPONSIBLE FOR DRAINAGE ISSUES OF GRADES LESS THAN 1.5%

- ANY CLAIMS FOR DEFECTIVE MATERIALS OR IMPROPER WORKMANSHIP SHALL BE WAIVED UNLESS NOTICE IS GIVEN WITHIN 10 BUSINESS DAYS.
- A COLD WEATHER SIGNED BY THE OWNER / GENERAL CONTRACTOR MUST BE PROVIDED FOR PAVING PRIOR TO MAY 1ST AND AFTER OCTOBER 15th.
- FAILURE OF PURCHASER TO MAKE PAYMENTS AS AGREED WILL RELEASE AR FROM ANY FURTHER PERFORMANCE UNDER THIS CONTRACT UNTIL SITUATION IS REMEDIED TO THE SATISFACTION OF AR.
- WORK WILL BE PERFORMED DURING PERIODS OF PREMIUM OR OVERTIME WAGES, SUCH AS SATURDAYS, SUNDAYS AND HOLIDAYS, ONLY AT AR'S OPTION. IF SUCH WORK IS REQUESTED BY PURCHASER, REASONABLE COMPENSATION WILL BE REQUED FOR THE EXTRA INCURRED COST.
 - FINE GRADING IS + OR ONE INCH FROM REQUIRED GRADE ON AGGREGATE BASE BY OTHERS. AR WILL NOT BE RESPONSIBLE FOR DEFECTS IN PAVING RESULTING FROM ADVERSE WEATHER CONDITIONS, OR FROM INADEQUATE BASE PREPARATION (IF NOT DONE BY AR). AR RESERVES THE RIGHT TO REFRAIN FROM PAVING DURING WHAT IT CONSIDERS TO BE ADVERSE WEATHER CONDITIONS.
- CONDITIONS IN THIS CONTRACT WILL SUPERCEDE ANY LANGUAGE IN THE CUSTOMERS CONTRACT WITH THE OWNER OF THE PROJECT.
- EXEMPTION CERTIFICATE MUST BE PROVIDED BY PURCHASER OR SALES TAX MUST BE PAID. SWEEPING PRIOR TO PAVING BY OTHERS.
- THREE PAVING MOBILIZATIONS ARE INCLUDED UNLESS NOTED OTHERWISE, ADDITIONAL MOBILIZATIONS WILL BE BILLED AT \$6500.00 EACH. THERE WILL BE NO CREDIT GIVEN FOR UNUSED MOBILIZATIONS.
- TWO RECLAIMING MOBILIZATIONS ARE INCLUDED UNLESS NOTED OTHERWISE, ADDITIONAL MOBILIZATIONS WILL BE BILLED AT \$5,000.00 EACH. THERE WILL BE NO CREDIT GIVEN FOR UNUSED MOBILIZATIONS.
- THREE FINE GRADING MOBILIZATIONS ARE INCLUDED UNLESS NOTED OTHERWISE, ADDITIONAL MOBILIZATIONS WILL BE BILLED AT \$2,000.00 EACH. THERE WILL BE NO CREDIT GIVEN FOR UNUSED MOBILIZATIONS.
- ASPHALT DENSITY AND CORE TESTING ARE NOT INCLUDED IN UNIT PRICES.
- THE FOLLOWING ARE EXCLUDED FROM THE PROPOSED PRICES: ALL TAXES, M&P, PERMITS, BONDS, SAWCUTTING, ENGINEERING, SURVEY, LAYOUT, SWEEPING PRIOR TO PAVING, PREMIUM OR WEEKEND WORK, PLANT OPENING CHARGES, TEMPORARY TRENCH PAVING, PATCHING IN FRONT OF CURB, SAW & SEAL-JOINTS, FEES, PERMITS.

ALL PRICES SUBJECT TO 6.35% SALES TAX UNLESS EXEMPTION CERTIFICATE PROVIDED

NOTE:

UNLESS OTHERWISE SPECIFIED IN ABOVE SCOPE OF WORK, PRICE DOES NOT INCLUDE TRAFFIC CONTROL, FEES, PERMITS, OR ENGINEERING. ANY FEES INCURRED TRYING TO COLLECT THIS DEBT WILL BE THE RESPONSIBILITY OF CUSTOMER.

NAME:	
TITLE:	
COMPANY:	entitioner i traverir annu engglete
DATE:	



11 STONY RIDGE RD NORTH WINDHAM, CT 06256 WWW.APONTESCONSTRUCTIONRESOURCES.COM

APONTESCONSTRUCTIONRESOURCES@GMAIL.COM

OFFICE: 860.268.5862



PROPOSAL

February 20, 2024

RE: Killingly Memorial School - SPN 069-0069 RNV

Please accept our proposal to perform the concrete work at the above referenced project. This proposal includes all **Labor Only**, supervision, and insurance to complete our scope of work.

Project #	Project Name	Owner	Bid Date
-----------	--------------	-------	----------

069-0069RNV **Sidewalks Sub** Killingly Memorial School Invitation To Bid #2 - SPN 069-0069 RNV

Client #	Description	Quantity	Units	Unit Price	Extended Price
Add	5" CONCRETE SIDEWALK	88	SF	\$ 5.00	\$440.00
Add	Install ADA TILES 2' X 4'	1	EA	\$ 225.00	\$ 225.00
Add Handicap ramps	SIDEWALK RAMP 16	27	SF	\$ 15.00	\$ 405.00

				TOTAL ADD	\$1,070.00
--	--	--	--	-----------	------------

OnSite Services, Inc.

23 Meadow Road Clinton, CT 06413 (860) 669-3988 Fax (860) 664-9195

DATE: 01/16/2024 QUOTE TO: ATTN: Estimating

FAX:

PROJ: Killingly Memorial School Expansion & Renovation Phase 1 of 3- Killingly (Extra Work)

ITEM NO	DESCRIPTION	APPROX	UNUT	UNIT PRICE
I EIVI INO	DESCRIPTION DESCRIPTION	QUANTITY	UNIT	
	SHEET ALUMINUM SIGNS (Extra Work)		LS	1,650.00
	CONDITIONS:			
	Price based on furnishing and installing sheet aluminum			
	signs on plan sheet C-104 dated 11/13/23.			
	3ea. Reserved for Admin Staff			
	2. Price based on all signs to be installed on U-channel			
	post with breakaway system.			
	3. Price does not include core drilling into sidewalk. Add			
	\$85.00/ea if drilling is performed.			
	Sales tax not included.			
	PAINTED PAVEMENT MARKINGS		LS	1,750.00
	CONDITIONS:		1 - 1	.,
	Price based on Plan Sheet C-104 11/13/23			
	Price based on Waterborne Traffic Paint.			
	Price based on one coat of paint.			
	Painting to be performed when temperatures are at or			
	above 50 degrees, unless directed otherwise. OnSite			
	cannot be responsible for performance of paint at			
	temperatures of less than 50 degrees.			
	Pavement to be dry, clean, and free of obstructions. If additional makilizations are passed with the state of the st			
	additional mobilizations are necessary due to			
	obstructions, \$650.00 per mob will be charged.			

OnSite Services, Inc. will provide a certificate of insurance meeting the requirements of the Connecticut Department of Transportation Standard Specifications at the date of this proposal. Any additional insurance coverage will be provided at an additional cost.

Jenafer Stephaster

Jennifer Stopkoski, Pres.

Eagle Fence and Guardrail PROPOSAL/CONTRACT

1/15/2024

PAGE 1 OF 2

MATHER CORP

ATTN: MIKE LAWSON

FROM: NICK CASSONE; PROJECT MANAGER

RE: PR#14 - ADDED 4'W GATES

WE HEREBY PROPOSE TO FURNISH AND INSTALL THE FOLLOWING:

ITEM	QUANTITY	UNIT COST	TOTAL
CHAININA FENCE CATES	·	 	
CHAINLINK FENCE GATES			
PER THE FOLLOWING	1	\$ 3,250.00 \$	3,250.00
INCLUDES 2EA 4'W SINGLE SWING GATES			
2" X 9GA KK WIRE MESH			
3" GATE POSTS			
INCLUDES CUTTING IN 1ea NEW GATE IN EXISTING FENCE	LINE		
INCLUDES 1ea NEW GATE IN NEW FUTURE FENCE LINE			
ALL POSTS CONCRETE FOOTINGS			
ALL MATERIAL GALVANIZED FINISH			
INCLUDES STANDARD FORK LATCH			

PLEASE NOTE - GATE INSTALL IN EXISTING FENCE LINE HAS TO BE INSTALLED AT THE SAME TIME THE NEW FENCE IS BEING INSTALLED, PRICE DOES NOT REFLECT A SEPARATE MOBILIZATION

SUBTOTAL:		\$ 3,250.00
SALES TAX:	PLEASE PROVIDE TAX EXEMPT CERT	\$ _
TOTAL COST:		\$ 3,250.00

Eagle Fence and Guardrail

EXCLUSIONS/CLARIFICATIONS

- *GROUNDING & BONDING*
- * SURVEYING/PROPERTY LINE DETERMINATION, BY BUYER. FENCE LINE CLEARING, BY BUYER (IF NEEDED). ALL PERMITS, BY BUYER.
- * NORMAL DIGGING/GRADING CONDITIONS. THIS PROPOSAL DOES NOT INCLUDE ALLOWANCES FOR HAND-WORK OR ADDITIONAL EQUIPMENT
 THAT MAY BE NEEDED DUE TO ROCK LEDGE, CONFLICTS WITH UTILITIES, OR ANY OTHER OBSTRUCTION THAT WOULD PRECLUDE STANDARD
 INSTALLATION PRACTICES. ALL SUCH COSTS WILL BECOME AN ADDITIONAL CHARGE, OVER AND ABOVE THIS PROPOSAL.
- * THIS PROPOSAL EXCLUDES: SURVEY/LAYOUT; PERMITS; ALLOWANCES FOR HAND WORK (ALL POST HOLES TO BE MACHINE-AUGURED);

 ROCK/LEDGE EXCAVATION; CUTTING/PATCHING BLACKTOP; TRAFFIC PROTECTION; MARK-OUT & PROTECTION OF PRIVATELY OWNED UTLITIES

 ANY OTHER WORK NOT SPECIFICALLY STATED ABOVE.
- * PAYMENT TERMS: PAYMENT DUE IN FULL WITHIN 30 DAYS OF INVOICE. A FINANCE CHARGE OF 1.5% PER MONTH (ANNUAL RATE OF 18%) WILL ACCRUE ON ANY BALANCE OVER 30 DAYS. IN THE EVENT IT IS NECESSARY TO ENFORCE COLLECTION, BUYER AGREES TO PAY ALL COSTS OF COLLECTION, INCLUDING REASONABLE ATTORNEY'S FEES.
- * THIS PROPOSAL IS VALID FOR 30 DAYS FROM ABOVE DATE.
- * THIS CONSTITUTES THE FULL AGREEMENT BETWEEN BUYER AND EAGLE FENCE & GUARDRAIL. CHANGES WILL ONLY EXECUTED UPON WRITTEN ORDERS FROM BUYER, AND WILL RESULT IN CHANGES TO COST.

STOMER ACCEPTANCE:	 DATE:



PROPOSAL: 5532910

1/15/24

The Concrete Cutting Professionals

CORE DRILLING - ASPHALT SAWING -SLAB SAWING

DEMOLITION & REMOVAL Page 1 JOB SITE LOCATION

MATHER CORPORATION 21 W. DUDLEY TOWN ROAD BLOOMFIELD ,CT 06002

Killingly Memorial School Danielson, CT

Phn: (860) 242-0743 Fax: (860) 242-1493

Attn:

Mike Lawson

SCOPE OF WORK

QUANTITY DESCRIPTION UNIT PRICE

OUR PROPOSAL INCLUDES ALL LABOR, TOOLS, AND EQUIPMENT NECESSARY TO COMPLETE THE FOLLOWING SCOPE OF $^{\mathrm{WORK:}}$ SAWCUT MINIMUM CHARGE

\$850.00

(1) SAWCUT BITUMINOUS 4" THICK AT NEW PAVEMENT AND A.D.A. RAMP

TOTAL PRICE: \$850.00

Quotation Conditions

IF APPLICABLE, PLEASE ADD 6.35% SALES TAX.

IT IS UNDERSTOOD THAT ALL WORK WILL BE DONE AT CONTINUOUS STRAIGHT TIME WORK SHIFTS OUR ESTIMATE IS BASED ON THE INFORMATION PROVIDED BY YOU. ANY CHANGE IN SCOPE OF WORK, QUANTITIES OR SITE CONDITION MAY EFFECT QUOTED PRICE.

NO PROTECTION, WATER CONTROL, OR COLLECTION REQUIRED.

ALL WORK TO BE DONE ON STRAIGHT TIME.

STAGING, MAN LIFTS OR WORK PLATFORMS REQUIRED ARE NOT INCLUDED.

REMOBILIZATION WILL BE DONE ON A TIME AND MATERIALS BASIS.

PRO CUT RECOMMENDS THE USE OF RADAR SCANNING BEFORE YOU SAWCUT OR CORE HOLES TO TRY TO AVOID UNKNOWNS SUCH AS PIPES, WIRES, OR STRUCTURAL MEMBERS CONCEALED IN THE WORK.

DocuSign Envelope ID: 20B7D687-6D52-4222-A644-B7A76CDFDC78

EXCLUSIONS / CONDITIONS

PRO CUT IS NOT RESPONSIBLE FOR LAYOUT OF CUT LINES OR CORE HOLES, OR THE CUTTING OF UNKNOWN WIRES, PIPES, CONDUITS OR STRUCTURAL MEMBERS. PRO CUT IS NOT RESPONSIBLE FOR THE STRUCTURAL INTEGRITY OF STRUCTURE OR WORK AREA AS A RESULT OF OUR WORK.
PRO CUT IS NOT RESPONSIBLE FOR SAFETY BARRIERS, SAFETY PROTECTION, COVERING OVER HOLES OR OPENINGS AND CREATING A SAFE WORK ZONE. PRICE INCLUDES NOMINAL REINFORCING STEEL ONLY.

IT IS THE CUSTOMER'S RESPONSIBILITY TO OBTAIN A DIG SAFE AUTHORIZATION NUMBER AND ALL PERMITS WHERE APPLICABLE.

UNLESS SPECIFICALLY INCLUDED, PRO CUT IS NOT RESPONSIBLE FOR SLURRY CONTAINMENT, WHEREAS DIRECT OR INDIRECT RUN OFF WOULD VIOLATE STATE OR FEDERAL CLEAN WATER OR WETLAND PROTECTION LAWS,

WE DO NOT ACCEPT RETAINAGE PROVISIONS OR PAY WHEN / IF PAID CLAUSE, PLEASE DO NOT INCLUDE THEM AS PART OF OUR CONTRACT OR PURCHASE ORDER, NOTIFICATION TO PROCEED CONSTITUTES ACCEPTANCE OF THIS PROPOSAL AND ITS TERMS AND CONDITIONS.


THIS PROPOSAL MAY BE WITHDRAWN IF NOT ACCEPTED WITHIN 60 DAYS.

PROPOSAL PREPARED BY: BENJAMIN ULRICH

DATE:

ACCEPTANCE OF PROPOSAL:

DATE:

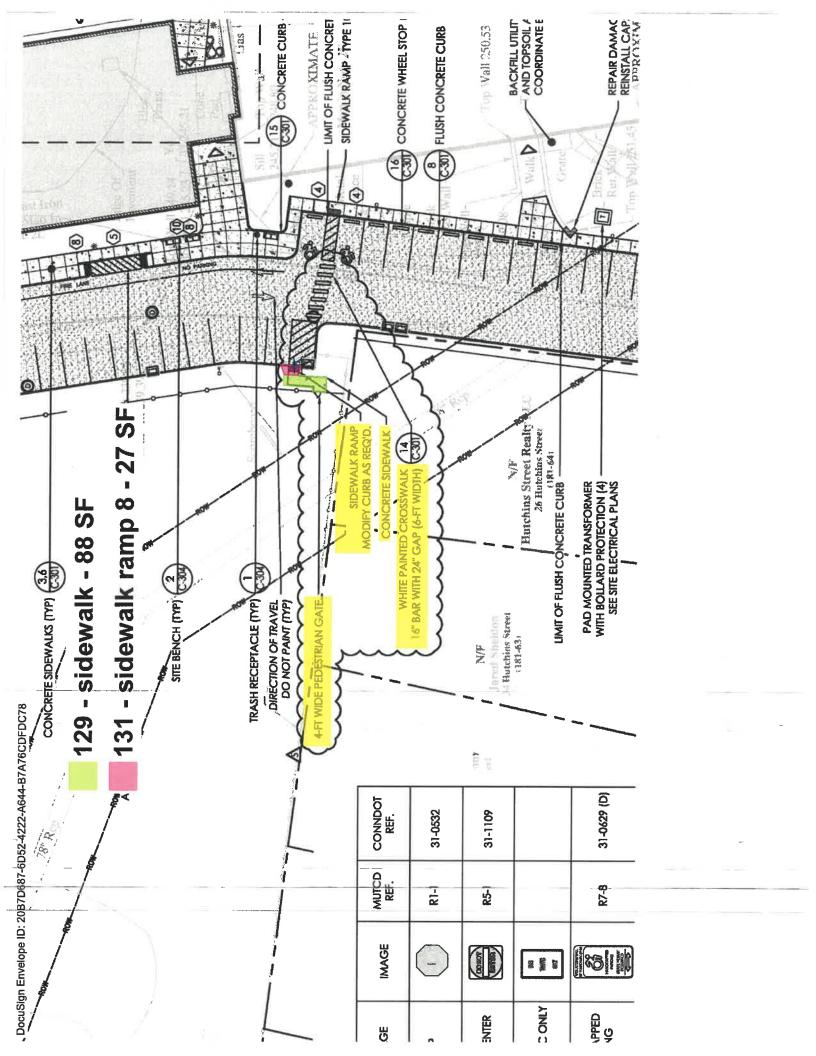





Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 Phone: (860) 229-3755 **Project:** 25-01-0447 - Killingly Memorial School Killingly, Connecticut

Prime Contract Potential Change Order #303: CE #303 - Kitchen Equipment Relocation

то:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	303 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM	:	CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	3/11/2024
REFERENCE:		PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No		
LOCATION:		ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:		PAID IN FULL:	No
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	-
		TOTAL AMOUNT:	\$6,556.00

POTENTIAL CHANGE ORDER TITLE: CE #303 - Kitchen Equipment Relocation

CHANGE REASON: Client Request

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract is Changed As Follows)

CE #303 - Kitchen Equipment Relocation

Labor and material to complete revisions shown in PR #19.

HVAC:

- Labor to revise previously completed & approved coordination drawing.

-Plumbing:

- Extend gas line to new WH location
- F&I additional vent for sink
- F&I additional cast-iron sanitary piping-
- F&I copper water supply piping for sink and washing machine
- F&I pipe insulation
- Credit labor, cast-iron and copper piping materials from original washer / dryer location.

ATTACHMENTS:

#	Budget Code	Description	Amount
1	001.22-100.S Construction.Plumbing System.Subcontractor	Plumbing	\$5,781.00
2	001.23-100.S Construction.HVAC.Subcontractor	HVAC	\$493.00
3	001.60-504.M Construction.CM P&P Bonds.Material (Procore)	Bonds	\$44.00
4	001.60-503.M Construction.General Insurance.Material (Procore)	Insurance	\$47.00
5	001.90-001.M Construction CM Fee Material (Procore)	Fee	\$191.00
	1	Grand Total:	\$6,556.00





Antinozzi Associates
Town of Killingly
Downes Construction Company
271 Fairfield Ave.
172 Main Street
200 Stanley St
Bridgeport Connecticut 06604
Killingly, Connecticut 06239
New Britain, Connecticut 06051

SIGNATURE DATE SIGNATURE DATE DATE



Proposal Request

PROJECT: (name and address)

Killingly Memorial School

Expansion and Renovation Project

339 Main Street Danielson, CT 06239

OWNER: (name and address)

Town of Killingly 172 Main Street

Danielson, CT 06239

CONTRACT INFORMATION:

Contract For: Construction Manager as

Constructor with a GMP

ARCHITECT: (name and address)

Antinozzi Associates, P. C.

271 Fairfield Avenue

Bridgeport, CT 06604

Date: July 06, 2022

Architect's Project Number: 21025 Proposal Request Number: 019

Proposal Request Date: February 20, 2024

CONTRACTOR: (name and address) **Downes Construction Company**

200 Stanley Street

New Britain, CT 06051

The Owner requests an itemized proposal for changes to the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. The Contractor shall submit this proposal within seven (7) days or notify the Architect in writing of the anticipated date of submission.

(Insert a detailed description of the proposed modifications to the Contract Documents and, if applicable, attach or reference specific exhibits.)

Provide a proposal for the following changes as outlined below:

- 1. Relocate the following equipment as outlined in the attached drawings, located in the existing footprint of the Kitchen Renovations (Base Bid) to the Kitchen/Freezer Addition (Alternate Area).
 - A. Mop Sink
 - B. Washer / Dryer
 - C. Hot Water Heater

Please provide a proposal enumerating the changes to your contract as a result of this proposal.

ATTACHMENTS:

Drawings

- 1. E-101.3 PR-019
- 2. M-100.2 PR-019
- 3. P-101.2B PR-019
- 4. SKA-14 PR-019

Specifications

NONE

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE, OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

AIA Document G709 - 2018. Copyright @ 1993, 2001 and 2018. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 12:49:17 ET on 02/20/2024 under Order No.4104244980 which expires on 09/01/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com. User Notes: (3B9ADA4D)

REQUESTED BY THE ARCHITECT:


David C. Ferris, Sr. Associate / Sr. Project


Manager


PRINTED NAME AND TITLE


AIA Document G709 – 2018. Copyright © 1993, 2001 and 2018. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AlA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 12:49:17 ET on 02/20/2024 under Order No.4104244980 which expires on 09/01/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.

(3B9ADA4D)

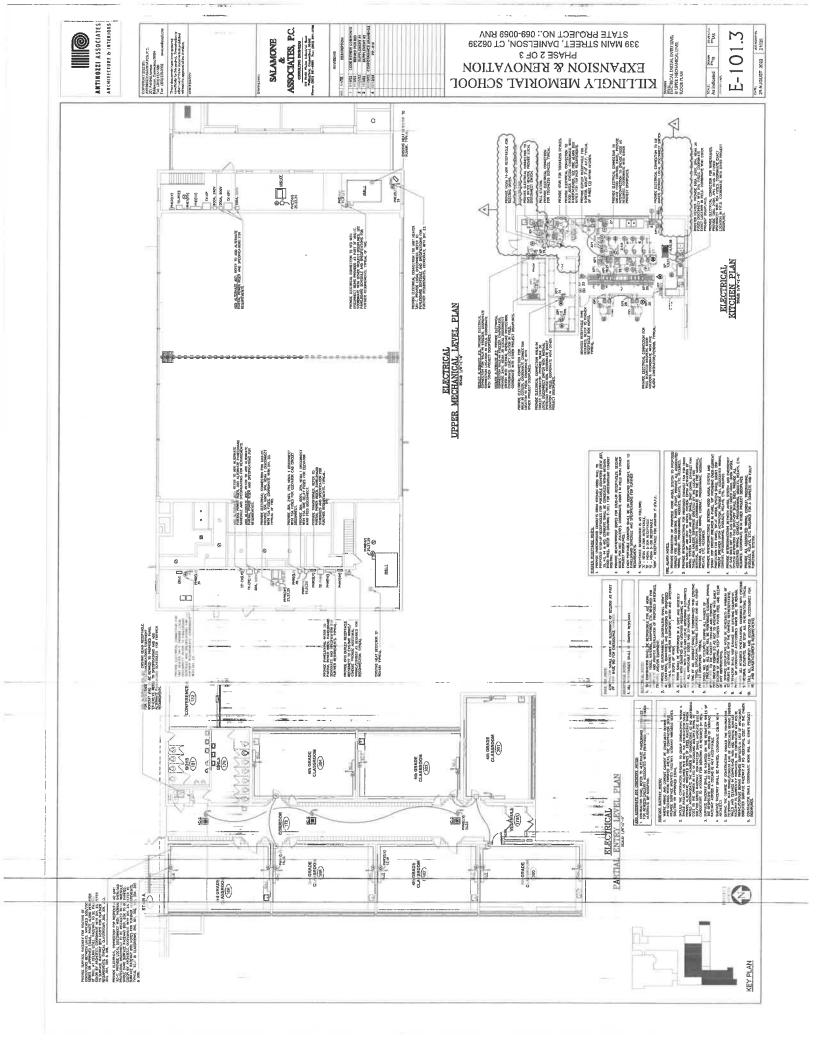

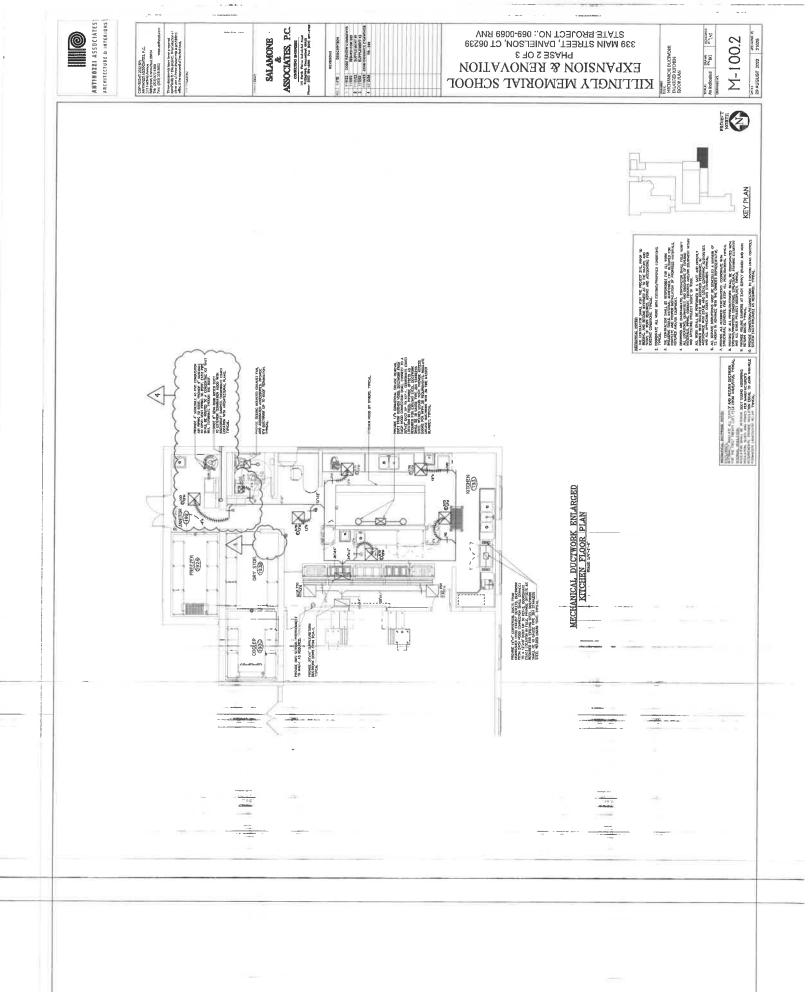

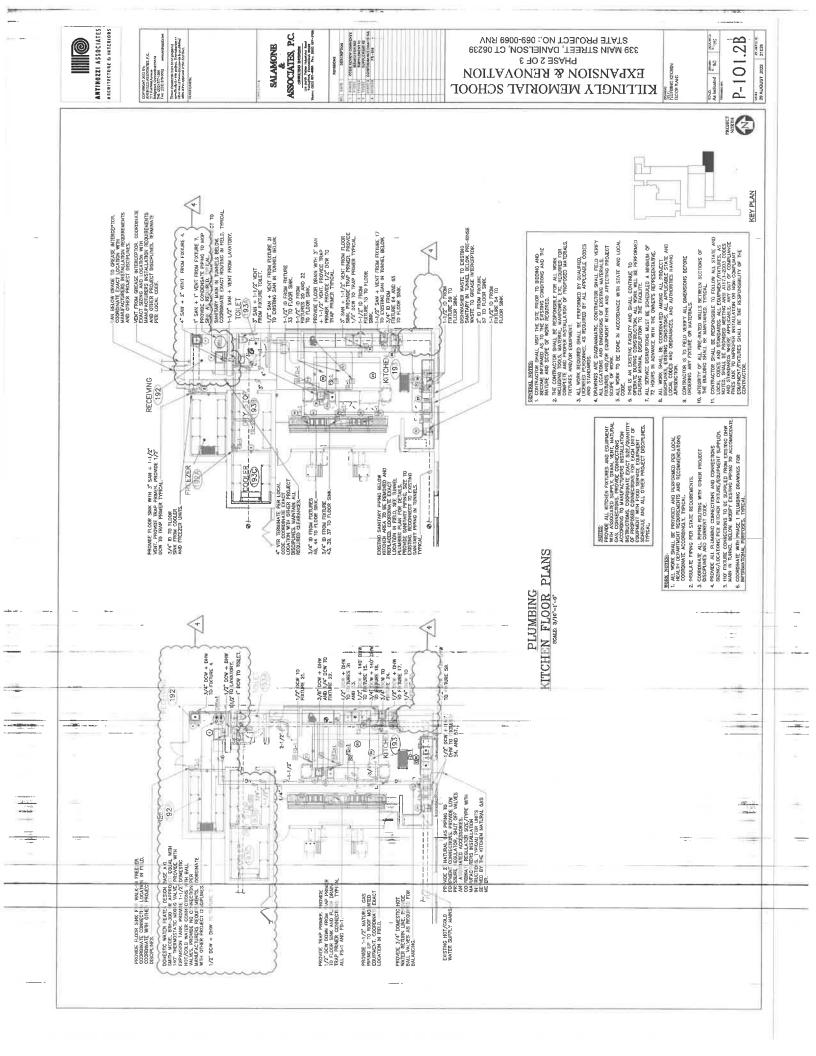

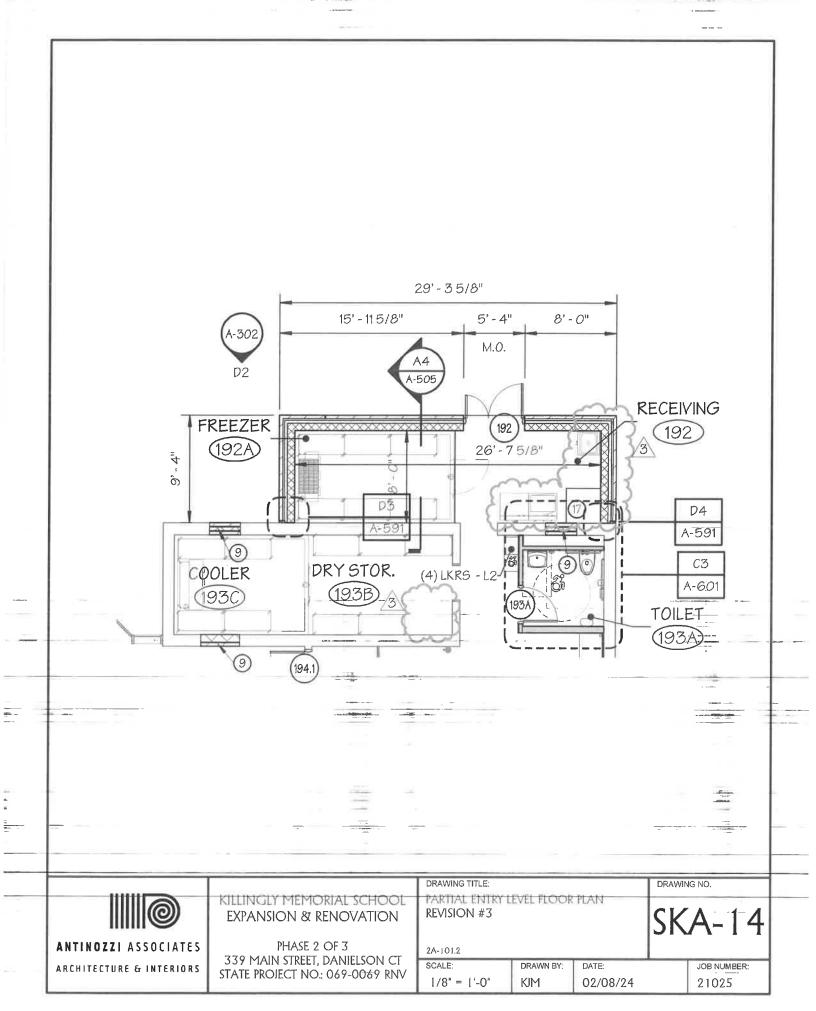

ORIGINAL QUOTE

Killingly Memorial School Change Order Proposal #11

To:

Downes Construction Co.

From:

MJ Daly LLC 2/26/2024

Ref:

PR #019

Date: CM Number:

Trade Contractor COP Number:

11

Description:

Labor & Material to complete scope based on PR #019

					3				/	
Quantity	Unit		Desc	ription of N	aterial and Equi	pment			Uni Cost	Total
1	1	See Material B	reakdown Below						\$ 6,826.00	\$ 6,826.00
										\$ -
								9		\$ -
										\$ -
										\$ -
										\$
										\$ _
										\$ -
										\$
Line 1		1					Mate	rial and Eq	uipment Total	\$ 6,826.00
Crew	Labor	Classification	Hours	Base Rate	FICA & Med	FUTA &	Ø∕L, W/C	Benefits	Total Rate	Total
					Care	SUTA	Ins			
Plumber, Fit	FC	DREMAN	30.50	54.54	\$ 4.17	\$ 4.0	\$ 5.55	\$ 36.15	\$ 104.45	\$ 3,185.73

Crew	Labor Classification	Hours	Base Rate	FICA & Med	FUTA &	JL, W/C	Benefits	Total Rate	Total
				Care	SUTA	Ins		1	
Plumber, Fit	FOREMAN	30.50	\$ 54.54	\$ 4.17	\$ 4.0	\$ 5.55	\$ 36.15	\$ 104.45	\$ 3,185.73
Plumber, Fit	JOURNEYMAN	30.50	\$ 49.58	\$ 3.79	\$ 367	\$ 5.03	\$ 36.15	\$ 98.22	\$ 2,995.71
								\$ -	\$
								\$ -	\$ -
								\$ -	\$ -
								\$ -	\$ -
								\$ -	\$ -
								\$ -	\$ -
		ø		X				\$ -	\$
								\$ -	\$ -
								\$ -	\$ 100
Line 2								Labor Total	\$ 6,181.44

Subcontractor Cost (Attach Proposals	s)				
Trade		Name of Subcontractor	1		Total
Insulation		Axion Sp	ecialty Contra	cting LLC.	\$361.63
			-		
ž	1		1		-2.3.
Line 3				Subcontractor Total	\$ 361.63

Line 4	Total Labor, Material, and Equipm	t		\$ 13,369.07	
--------	-----------------------------------	---	--	--------------	--

Contractor Overhead and Profit		Allow %	1	Amount	-Total-
Net Value of Self Performed Work (Amount = Lir	s 1+2)	10%	\$	13,007.44	\$ - 1,30 0.74
Net Value of Subcontract Work (Amount = Line :		5%	\$	361.63	\$ 18.08
Line 5		Contractor (Overhea	d and Profit Total	\$ 1,318.83

Line 6	Total Proposed Cha	ge Order Amount (Lines 4+5)		\$
			1	

QUOTE REV 1

Killingly Memorial School Change Order Proposal #11

To: **Downes Construction Co.**

From:

MJ Daly LLC

Ref:

PR #019

Date: 3/8/2024

CM Number:

Trade Contractor COP Number:

11

Description:

Labor & Material to complete scope based on PR #019

Quantity	Unit	Description of Material and Equipment	UnitCost	Total
1	1	See Material Breakdown Below	\$ 5,919.00	\$ 5,919.00
				\$ -
			/	\$ -
			-	\$ -
				\$ -
				\$ -
				\$ _
				\$ -
				\$
Line 1		Material and Eq	uipment Total	\$ 5,919.00

									-						
Crew	Labor Classification	Hours	B	ase Rate	FIG	CA & Med	FU	JTA &	15/ l	L, W/C	В	enefits	То	tal Rate	Total
						Care	5	SUTA 🌶		Ins					
Plumber, Fit	FOREMAN	20.1	\$	54.54	\$	4.17	\$	4.04	\$	5.55	\$	36.15	\$	104.45	\$ 2,104.67
Plumber, Fit	JOURNEYMAN	20.1	5 3	49.58	\$	3.79	\$	3.67	\$	5.03	\$	36.15	\$	98.22	\$ 1,979.13
							1						\$	~	\$ -
			L				/				Į.		\$		\$ -
			T										\$		\$ -
													\$	2	\$ -
			Т		1								\$	- 1	\$ _
			Т		1								\$	-81	\$
			Т			X							\$		\$ _
			T		1								\$	-	\$ -
													\$		\$ -
Line 2				,		1					-		La	bor Total	\$ 4,083.80

Subcontractor Cost (Attach Prop	osals)			
Trade		Name of Subcontractor		Total
Insulation		Axion Sp	peculty Contracting LLC.	5361.63
	/	Name of -		
10.5		Appendix A transfer on the second of the sec		
Line 3			Subcontractor Tota	361.63

Line 4	Total Labor, Material, and Equip	ent	\$ 10,364.43

Contractor	Overhead and Profit	/	Allow % Amount				Total
Net Value o	of Self Performed Work (A	mount = Lines 1+2)	10%	5	10,002.80	-\$	1,000.28
Net Value o	of Subcontract Work (Am	unt = Line 3)	5%	\$	361.63	\$	- 18.08
Line 5			Contractor (Over	head and Profit Total	\$	1,018.36

Line 6	Total Proposed @	ange Order Amount (Lines 4+5)	Ś	11,383

QUOTE REV 2

Killingly Memorial School Change Order Proposal #11

To:

Downes Construction Co.

From:

MJ Daly LLC

Date:

3/27/2024

Ref:

PR #019

CM Number:

Trade Contractor COP Number:

11

Description:

Labor & Material to complete scope based on PR #019

Quantity	Unit	Description of Material and Equipment		Upft Cost	Total
1	1	Se Material Breakdown Below		\$ 2,701.00	\$ 2,701.00
					\$ -
			/		\$
					\$ -
Line 1		/Ma	terial and Eq	uipment Total	\$ 2,701.00

Crew	Labor Classification	Hours	Base Rate	FICA & Med	FUTA &	G/L, W/C	Benefits	Total Rate	Total
				Care	SUTA	Ins			
Plumber, Fit	FOREMAN	23.00	\$ 54.54	\$ 4.17	\$ 4/04	\$ 5.55	\$ 36.15	\$ 104.45	\$ 2,402.35
Plumber, Fit	JOURNEYMAN	15.00	49.58	\$ 3.79	\$ /3.67	\$ 5.03	\$ 36.15	\$ 98.22	\$ 1,473.30
	Project Manager	4:00	1		/			\$ 130.00	\$ 520.00
	- AV							\$ -	\$ -
				/				\$ -	\$ -
								\$ -	\$ -
								\$ -	\$ -
								\$ =	\$ -
				X				\$ -	\$ -
								\$ -	\$ -
								\$ -	\$ -
Line 2			/		-			Labor Total	\$ 4,395.65

Line 4 Total Labor, Material, and Eq	ujument				\$ 7,458.28	\$6,576.65
Contractor Overhead and Profit		Allow %	1	Amount-	Total	
Net Value of Self Performed Work (Anou	nt = Lines-1+2)	10%	1	7,096.65	\$ 709.67	\$657.67

Contractor over	ileau allu Front		AllUW 76		AIHOUIIL-		- I-Utai
Net Value of Sel	f Performed Work (🌃	ount = Lines-1+2)	10%	1	7,096.65	Ş	709.67
Net Value of Suk	contract Work (Amou	nt = Line 3)	5%	\$	361.63	\$	18.08
Line 5			Contractor (Overl	nead and Profit Total	\$	727.75
					_		

Line 6 Total Proposed Change Order Amount (Lines 4+5) 5 8,186

\$7,614.00

\$3,875.65

Killingly Memorial School Change Order Proposal #11

To:

Downes Construction Co.

From:

MJ Daly LLC 4/10/2024

Ref:

PR #019

Date: CM Number:

Trade Contractor COP Number:

11

Description:

Labor & Material to complete scope based on PR #019

Quantity	Unit	Description of Material and Equipment	Unit Cost	Total
1	1	See Material Breakdown Below	\$ 1,034.22	\$ 1,034.22
				\$ -
				\$
				\$ -
				\$
				\$ -
ine 1			Material and Equipment Total	\$ 1,034.22

Crew	Labor Classification	Hours	Ва	se Rate	FIC	A & Med	FI	UTA &	G/	/L, W/C	В	enefits	To	tal Rate		Total
						Care	5	SUTA		Ins						
Plumber, Fit	FOREMAN	23.00	\$	54.54	\$	4.17	\$	4.04	\$	5.55	\$	36.15	\$	104.45	\$	2,402.35
Plumber, Fit	JOURNEYMAN	15.00	\$	49.58	\$	3.79	\$	3.67	\$	5.03	\$	36.15	\$	98.22	\$	1,473.30
	Project Manager	4.00	_		-			_	-		_		\$	130.00	\$	520.00
													\$	-	\$	-
													\$	*	\$	
													\$		\$	-
													\$	- 5	\$	
													\$	- :	\$	-
													\$	2	\$	
													\$	-	\$	-
													\$	-	\$	
Line 2							٠.						La	bor Total	S	4,395,65

Subcontractor Cost (Attach Proposals)

Trade Name of Subcontractor Total
Insulation Axion Specialty Contracting LLC. \$361.63

	The state of the s	1718	
Line 4	Total Labor, Material, and Equipment		\$ 5,791.50

Contractor (Overhead and Profit	Allow %		Amount		Total	
Net Value of	f Self Performed Work (Am ount = Lines 1+2)————————————————————————————————————	10%	\$	5,120.07	-5	542.99	\$490.99
Net Value of	f Subcontract Work (Amount = Line 3)	5%	\$	361.63	\$	18.08	
Line 5		Contractor (Overhe	ad and Pröfit Total	5	561.07	

Line 6 Total Proposed Change Order Amount (Lines 4+5)

\$5,781.00

\$3,875.65



Change Request

110 MATTATUCK HEIGHTS WATERBURY, CT 06705-3831 Ph: (203) 753-5131 Fax: (203) 596-9672

To: DOWNES CONSTRUCTION CO., LLC 200 STANLEY STREET NEW BRITAIN, CT 06050 PM: 860-229-3755

Date: 4/10/24 Job: 1385E KILLINGLY MEMORIAL SCI

AEC COR#: 17

Other #: PR #19

Description: PR #19 Source: Other# PR #19

We are pleased to offer the following specifications and pricing to make the following changes:

	Cost Code	Quantity Unit	Unit Price	Labor	Material	Subcontract	Equipment	Other	Price
CAST IRON PIPE	02-0202				662.88				\$662 88
COPPER PIPE	02-0200				693.18				\$603.18
STEEL PIPE	02-0201				173.46				\$173.46
COPPER FITTINGS	02-0210				129.16				\$129.16
CAST IRON FITTINGS	02-0212				648.21				\$648.21
STEEL FITTINGS	02-0211				14.04				\$14.04
HANGERS	02-0230				401.63				\$401.63
P-101.2B DCW&DHW ADD Foreman	11-1102	27.00 Lab	104.44	\$2,819.88					\$2.819.88
P-101.2B DCW&DHW ADD Journeyman	11-1102	27.00 Lab	98.23	\$2,652,21					\$2,652.21
P-101.2B GAS ADD Foreman	11-1101	7.50 Lab	104.44	\$783.30					\$783.30
P-101.2B GAS ADD Journeyman	11-1101	7.50 Lab	98.23	\$736.73					\$736.73
P-101.2B SW-AG ADD Foreman	11-1103		104.44	\$1,462.16					\$1 462 16
P-101.2B SW-AG Journeyman	11-1103	14.00 Lab	98.23	\$1,375.22					\$1.375.22
P-101.2B DCW&DHW Deduct Foreman	11-1102	-27.00 Lab	104.44	\$-2,819.88					\$-2.819.88
P-101.2B DCW&DHW Deduct	11-1102	-27.00 Lab	98.23	\$-2,652,21					\$-2 652 21
Journeyman	=								4-1,000:4-
P-101.2B SW-AG Deduct Foreman	11-1103	-6.50 Lab	104.44	\$-678.86					\$-678.86
P-101.2B SW-AG Deduct Journeyman	11-1103	-6.50 Lab	98.23	\$-638.50					\$-638.50
INSULATION	04-0401	****				361.63			\$36163
CAST IRON PIPE	02-0202				-251.23				\$-251.23
COPPER PIPE	02-0200	***			-592.93				\$-592.93
COPPER FITTINGS	02-0210				-169.07				\$-169.07
CAST IRON FITTINGS	02-0212				-286.89				\$-286.89
HANGERS	02-0230				-388.22				\$-388.22



110 MATTATUCK HEIGHTS WATERBURY, CT 06705-3831 Ph: (203) 753-5131 Fax: (203) 596-9672

Change Request

Date: 4/10/24 Job: 1385E KILLINGLY MEMORIAL SCH \$835.52 \$520.00 \$542.98 \$18.08 \$5,791.42 10.00% 5.00% \$5,429.79 Other #: PR #19 \$361.63 **AEC COR#: 17** \$361.63 Self Performed Subconfractor \$1,034.22 \$835.52 \$520.00 \$4,395.57 130.00 Subtotal: 8.00 Lab 4.00 Lab 01-0003 01-0001 To: DOWNES CONSTRUCTION CO., LLC 200 STANLEY STREET NEW BRITAIN, CT 06050 Ph: 860-229-3755

SUPERVISION PROJECT MANAGER

\$6,352.48

Total:

Change Request

AEC COR#: 17 Date: 4/10/24

110 MATTATUCK HEIGHTS WATERBURY, CT 06705-3831 Ph: (203) 753-5131 Fax: (203) 596-9672

To: DOWNES CONSTRUCTION CO., LLC 200 STANLEY STREET
NEW BRITAIN, CT 06050
Ph. 860-229-3755

Job: 1385E KILLINGLY MEMORIAL SCH

Other #: PR #19

Approved by: Date:

Submitted by:



Corporate Headquarters: 100 North Elm Street • Waterbury, CT 06702 Phone: 203-756-3641 • Fax: 203-753-4317

Quoted By: TORRCO EAST WINDSOR BRANCH L2

10 SOUTH MAIN STREET

EAST WINDSOR, CT 06088-9739 860-627-9677 Fax 860-623-3148

Quotation

QUOTE DATE	GUOTE BUMBER
04/04/24	S7520348
Quoted By	PACE NG
Howard Liebman 860-903-1993 hliebman@torrco.c	com

Quoted To: M.J. DALY, LLC

110 MATTATUCK HEIGHTS RD WATERBURY, CT 06705-3831

Ship To: M.J. DALY, LLC

226 PUTNAM PIKE

KILLINGLY HIGH SCHOOL DAYVILLE, CT 06241

ILLING/PI	R19 ADD RE	V NICK SASS	O 8039-0616	7225: FREIG	TOTAL TRANSPORT AND A STREET AND A STREET AND ASSESSMENT ASSESSMENT AND ASSESSMENT ASSESSMENT AND ASSESSMENT ASS		
	rox, Net 3	0th	04/04/24	Inc	Included		
ORDER DIV	PART NO		DESCRIPTION	Net Pro	Ext Pre		
		*	******				
		* OPEN ADDER					
		* REVISED ON					
			******************	*			
		*	•				
		*					
2lt	64430	1-1/2inchx21:	foot LENGTH S40 DOM	4.13	173.4		
		BLACK STEEL	PIPE T&C				
3ea	20361		LENGTH NH-2 NO-HUB	79.05	237.1		
		PIPE					
3ea	20363		LENGTH NH-2 NO-HUB	141.91	425.7		
		PIPE	-				
1lt			foot LENGTH TYPE L HAI	RD 86.54	86.5		
4 4 2			OPPER TUBING				
1lt	32312		/2inchx20foot LENGTH TYPE L HARD 40.84				
1lt	2222		COPPER TUBING 1/2inchx10foot LENGTH TYPE L HARD 20.42 20.4				
116	32323	COPPER TUBING		20.42	20.4		
31t	32313		ot LENGTH TYPE L HARD	67.00	201.0		
310		COPPER TUBING			201.0		
21t	32316		foot LENGTH TYPE L HAI	RD 172.19	344.3		
	32323	COPPER TUBING			311.3		
2ea	20386		NO-HUB LONG SWEEP	25.46	50.9		
4ea			NO-HUB LONG SWEEP	49.05			
1ea		4x3-1/2inch 1	NH-52S NO HUB TAPPED	41.41	41.4		
	-:		H SOUTHERN RAISED HEAL)			
		BRASS PLUG II					
lea	20496		NO-HUB COMBINATION WY	51.64	51.6		
	****	& 1/8 BEND	***				
lea	20502	4x2inch NH-40 n Next Page *	OA NO-HUB SHORT REDUC	ER 12.69	12.6		
777	mernued of	I Next Page *					
			- 0				



Corporate Headquarters: 100 North Elm Street • Waterbury, CT 06702 Phone: 203-756-3641 • Fax: 203-753-4317

Quoted By: TORRCO EAST WINDSOR BRANCH L2

10 SOUTH MAIN STREET

EAST WINDSOR, CT 06088-9739 860-627-9677 Fax 860-623-3148

Quotation

OUGTE DATE	GUOTE NUMBER
04/04/24	S7520348
Quoted By	PAGE NG.
Howard Liebman 860-903-1993 hliebman@torrco.d	com 2

Quoted To: M.J. DALY, LLC

110 MATTATUCK HEIGHTS RD WATERBURY, CT 06705-3831

Ship To: M.J. DALY, LLC 226 PUTNAM PIKE

KILLINGLY HIGH SCHOOL DAYVILLE, CT 06241

ILLING/P	R19 ADD RE	V NICK SASSO	72252 FRESIGNT	
-			<u> </u>	
% 10th P:	rox, Net 3	Oth 04/04/24	Includ	led
1ea		2x1-1/2inch NH-40A NO-HUB SHORT	8.46	8.4
Ica	20400	REDUCER	0.40	0
1ea	20413	2x1-1/2inch NH-28 NO-HUB TY	16.32	16.3
1ea		4inch NH-20 NO-HUB WYE	34.73	34.7
1ea		3x2inch NH-20 NO-HUB WYE	16.10	16.1
5ea		C200HW MISSION 2inch HEAVY WEIGHT	8.30	41.5
Jea	241333	NO HUB COUPLING BLUE	0.50	41.0
16ea	779534	C400HW MISSION 4inch HEAVY WEIGHT	11.14	178.2
1-000	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	NO HUB COUPLING BLUE 1904119	11.14	1,0.2
1ea	319/5	1-1/2inch 907 COPPER DWV ELBOW	8.88	8.8
6ea		1/2inch 607 COPPER 90 DEGREE ELBOW	0.64	3.8
oea	21242	- 5/8 OD	0.01	5.0
7ea	2.1246	3/4inch 607 COPPER 90 DEGREE ELBOW	1.41	9.8
/ea	21240	= 7/80D	1.41	9.0
3ea	21256	1-1/2inch 607 COPPER ELBOW—	7.97	23.9
2ea		3/4inch 600RS COPPER COUPLING WITH	0.95	1.9
2 e a	31249	STOP 7/80D	0.95	1.3
2ea	31262	1-1/2inch 600 COPPER COUPLING WITH	4.38	8.7
200	31202	STOP 1-5/80D	4.50	0.7
2ea	31265	1-1/2x3/4inch 600 COPPER COUPLING	7.12	14.2
202	<u> </u>	WITH STOP		11.2
1ea	31518	1/2inch 611 COPPER TEE	1.08	1.0
. 2ea		1-1/2inch 611 COPPER TEE	16.10	32.2
lea		1-1/2x1-1/2x1/2inch 611 COPPER TEE	12.24	12.2
1ea		1-1/2x1-1/2x3/4inch 611 COPPER TEE	12.24	12.2
3ea		1-1/2inch BLACK MALLEABLE 90	4.68	14.0
Jea	_ 540000	ELL _	4.00	14.0
	* 7	This is a quotation *	Subtotal	2320.9
		s subject to market	S&H CHGS	0.0
fluct		nd may change without notice.	Sales Tax	147.3
TTUCI		icable taxes extra!		
	ADT) I	LUGULE LAXES EXLIGI	1	



Corporate Headquarters: 100 North Elm Street • Waterbury, CT 06702 Phone: 203-756-3641 • Fex: 203-753-4317

Quoted By: TORRCO EAST WINDSOR BRANCH L2

10 SOUTH MAIN STREET

EAST WINDSOR, CT 06088-9739 860-627-9677 Fax 860-623-3148

Quotation

QUGTE DATE	QUOTE: NUMBER
04/04/24	S7520381
Ray Moussaid	PAGE NG
203-465-4255 rmoussaid@torrco	.com

Quoted To: M.J. DALY, LLC

110 MATTATUCK HEIGHTS RD WATERBURY, CT 06705-3831

Ship To: M.J. DALY, LLC 226 PUTNAM PIKE

KILLINGLY HIGH SCHOOL DAYVILLE, CT 06241

		SESP DATE	FRE 1981T	
10th Pr	ox, Net 3	04/04/24	Inclu	ded
SANTE SELECTION		**	Britis Krieg	Rep.
		*********	**	
		* OPEN DEDUCT REVISION 1		
		*********	*	
		*		
		*		
-lea	20362		109.320	-109.32
		PIPE		
-1ea	20363	4inchx10foot LENGTH NH-2 NO-HUB	141.910	-141.91
774	2020	PIPE	E4 180	E 4 3 E
-1lt	32325	linchx10foot LENGTH TYPE L HARD COPPER TUBING	54.170	-54.17
11t-	32312	1/2inchx20foot LENGTH-TYPE L-HAR	2D 40.840	-40.84
110		COPPER TUBING	40.040	-40.04
11t	32313	3/4inchx20foot LENGTH TYPE L-HAR	D 67,000	-67.00
-		COPPER TUBING		
-21t	32316	1-1/2inchx20foot LENGTH TYPE L H	ARD 172.190	-344.38
	a. 200	COPPER TUBING		
-1lt	32307	1-1/2inchx10foot LENGTH TYPE L H	ARD 86.540	-86.54
	00450	COPPER TUBING		
-4ea		4inch NH-4 NO-HUB 1/4 BEND	23.110	-92.44
-lea	20441	3inch NH-22 NO-HUB COMBINATION W & 1/8 BEND	YE 26.730	-26.73
-lea	20435	3inch NH-42 NO-HUB P TRAP	37.280	-37.28
-lea		4inch NH-20 NO-HUB WYE	33.320	-33.32
-2ea		C300HW MISSION 3inch HEAVY WEIGH		-19.14
		NO HUB COUPLING BLUE		-
-7ea	779534		11.140	-77.98
		NO HUB COUPLING BLUE 1904119		
-1ea		linch 607 COPPER ELBOW	3.450	-3.45
-lea		749 3/4 CXCXC 45 WYE CAST Next Page ***	24.510	-24.51



Corporate Headquarters: 100 North Elm Street • Waterbury, CT 06702 Phone: 203-758-3641 • Fex: 203-753-4317

Quoted By: TORRCO EAST WINDSOR BRANCH L2

10 SOUTH MAIN STREET

EAST WINDSOR, CT 06088-9739 860-627-9677 Fax 860-623-3148

Applicable taxes extra!

Quotation

QUOTE DATE	GUOTE NUMBER
04/04/24	S7520381
Quoted By	PAGE NO
Ray Moussaid 203-465-4255 rmoussaid@torrco	.com 2

Quoted To: M.J. DALY, LLC

110 MATTATUCK HEIGHTS RD WATERBURY, CT 06705-3831

Ship To: M.J. DALY, LLC 226 PUTNAM PIKE

KILLINGLY HIGH SCHOOL DAYVILLE, CT 06241

Amount Due

-1382.69

LLING/PR1	DEDUCT	NICK SASSO		72252	
	TERMS		SHIP DATE	FREIGHT	
10th Pro	c, Net 30	th	04/04/24	Inclu	ded
GROER DEV	PARE NO		DESCRIPTION	Brit Price	Net
-1ea	31331	LEAD FREE 3/4inch 606-2 ELBOW	COPPER STREET 45	1.970	-1.97
-1ea	31255		COPPER COUPLING W	ITH 3.050	-3.05
-5ea	31342	*copper fitti 1/2 inch	ng	0.590	-2.95
7ea		- 7/8OD	OPPER 90-DEGREE ELI		-12.04
-5ea			COPPER ELBOW	7.970	-39.85
-1ea		STOP 1-5/80D			-4.38
lea			/2inch-611 COPPER T		-8.25
-2ea			/4inch 611 COPPER 1		-29.92
<u>lea</u>			11 COPPER TEE	19.350	-19.35
-1ea	31597	2x2x3/4inch 6	11 COPPER TEE	19.350	-19.35
			and the second s	- marz	
			and it desired to a		
					15.00
	* 🗥	hic is a systatic	*	Subtotal	-1300.12
		his is a quotation subject to m		S&H CHGS	0.00



NEFCO CORPORATION - (CT) 411 BURNHAM STREET EAST HARTFORD, CT 06108 Phone 860-289-0285 www.GoNEFCO.com

QUOTE TO:

Quotation

QUOTE DATE QUOTE NUMBER		
04/02/2024	349397	
NEFCO CORPORATION - (0	PAGE NO.	
411 BURNHAM STREET EAST HARTFORD, CT 06108 Phone 860-289-0285 www.GoNEFCO.com		1 of 2

SHIP TO:

M. J. DALY & SONS 110 MATTATUCK HEIGHTS 110 MATTATUCK HEIGHTS WATERBURY, CT 06705

M. J. DALY & SONS 110 MATTATUCK HEIGHTS 110 MATTATUCK HEIGHTS WATERBURY, CT 06705

CUST	OMER NUMBER	CUSTOME	ER PO NUMBER	JOB NAME / RELEAS	SE NUMBER	Si	ALESPERSON	
	1717		bidha c/o	Killingly PR	#19	David	David Palmeri {Davep}	
	WRITER		SHIP VIA	TERMS	OR	DERED BY	FREIGHT ALLOWED	
	Dave Sets	ky	EH TRUCK 5	2% 10th Net 30th	th	Nick	Yes	
INE	ORDER QTY		DESCRIPTIO	N	UNI	T PRICE	EXT PRICE	
		**** MORN	SHIPPING INSTRU IING DELIVERIES *** 11:00					
1	2EA	400DCLHZ 4" CLEVIS F Pn: 29642	HANGER ZN PLTD			389.309/C	7.79	
2	4EA	250DCLHK/ 2-1/2" CLEV EPOXY Pn: 391658	CG 'IS HANGER COPPER	RGARD		863.557/C	14.54	
3	6EA	300DCLHK/	ANGER COPPER GL	JARD		351.048/C	21.06	
4	15EA	400DCLHK/		RD EPOXY		180.637/C	72.10	
5	150FT	{150FT/BD}	THREADED ROD ZN F	PLTD	Ę	52.965/CF	79.45	
6		{48FT/BD}	HREADED ROD ZN F	PLTD		1.941/CF	68.13	
7	4EA	Pn: 40941 250DPSH/12	2L/SAF/5/16HOLE			92.311/C	7.69	
			PIPE SHIELD 12"L W NDED CORNERS	5/16 - =				

^{**} Continued on Next Page **





QUOTE DATE	QUOTE NUMBER	PAGE NO.
04/02/2024	S4849397	2 of 2

NE	ORDER QTY	DESCRIPTION	UNIT PRICE	EXT PRICE
8	6EA	300DPSH/12L/SAF/5/16HOLE 3" SFTY PIPE SHIELD 12"L W 5/16	230.268/C	13.82
		HOLE ROUNDED CORNERS Pn: 734682		
9	15EA	350DPSH/12L/SAF/5/16HOLE 3-1/2 SFTY PIPE SHIELD 12"L W 5/16 HOLE (ROUNDED CORNERS) Pn: 734685	255.572/C	38.34
10		DEW 7416SD1-PWR 3/8 X 5 WEDGE ANCH ZN PWRSTUD+SD1 {50/BX} THUNDER STUD	70.264/C	17.57
11	2EA	Pn: 203384 DEW 7433SD1-PWR 5/8 X 5 WEDGE ANCH ZN PWRSTUD+SD1 {25/BX} Pn: 203394	179.538/C	3.59
12	1BX	37CHFNZ/P100 3/8-16 HEX FIN NUT ZN PLTD PKG 100/BX	5.073/C	5.07
13	1BX	Pn: 27836 62CHFNZ/P25 5/8-11 HEX FIN NUT ZN PLTD PKG 25/BX	44.132/C	11.03
14	- 1BX	Pn: 673373 37DFLWZ/P100 3/8 USS FLAT WSHR ZN PLTD PKG 100/BX	8.059/C	8.06_
15	1BX	Pn: 28472 62DFLWZ/P50 5/8 USS FLAT WSHR ZN PLTD PKG 50/BX Pn: 41660	39.964/C	19.98
		The same of the sa		
		The state of the s		
	S A QUOTAT		Subtotal	388.22
su	bject to chang	days unless otherwise noted and e without notice after 5 days. fective for quantities quoted only. TAXESEXTRA!	S&H Charges	0.00
Ъ	LICABLE	IAXESEXTRA!	Amount Due	388.22



NEFCO CORPORATION - (CT) 411 BURNHAM STREET EAST HARTFORD, CT 06108 Phone 860-289-0285 www.GoNEFCO.com

> M. J. DALY & SONS 110 MATTATUCK HEIGHTS 110 MATTATUCK HEIGHTS WATERBURY, CT 06705

QUOTE TO:

SHIP TO:

Quotation

 QUOTE DATE
 QUOTE NUMBER

 04/02/2024
 \$4849393

 NEFCO CORPORATION - (CT)
411 BURNHAM STREET
EAST HARTFORD, CT 06108
Phone 860-289-0285
www.GoNEFCO.com
 PAGE NO.

 1 of 3

M. J. DALY & SONS 110 MATTATUCK HEIGHTS 110 MATTATUCK HEIGHTS WATERBURY, CT 06705

CUST	OMER NUMBER	сиѕтомі	ER PO NUMBER	JOB NAME / RELEASE NU	MBER	SA	ALESPERSON
	1717		bidha c/o	Killingly PR#19		David	Palmeri (Davep)
	WRITER		SHIP VIA	TERMS	ORDERED BY		FREIGHT ALLOWED
	Dave Sets	ky	EH TRUCK 5	2% 10th Net 30th	1	Nick	Yes
LINE	ORDER QTY		DESCRIPTIO	N	UNIT	PRICE	EXT PRICE
		**** MORN	SHIPPING INSTRU IING DELIVERIES *** 11:00	- 11			
1	2EA	200DCLHZ 2" CLEVIS I Pn: 14509	HANGER ZN PLTD		15	57.558/C	3.15
2	4EA	400DCLHZ	HANGER ZN PLTD		38	9.309/C	15.57
_3	7EA	150DCLHZ 1-1/2" CLE\	/IS HANGER ZN PLTE		13	88.805/C	9.72
4	3E <u>A</u>	250DCLHK/	CG /IS HANGER COPPER	R GARD	36	3.557/C	10.91
5	13EA	300DCLHK/	CG HANGER COPPER GL	JARD	35	1.048/C	45.64
6	8EA	400DCLHK/	CG HANGER COPPER GA	ARD EPOXY	48	0.637/C	38.45
7	150FT-	37C600THF	RZ THREADED ROD ZN F	PLTD	52	.965/CF	79.45
		{150FT/BD} Pn: 27281					

^{**} Continued on Next Page **





QUOTE DATE	QUOTE NUMBER	PAGE NO.
04/02/2024	S4849393	2 of 3

LINE	ORDER QTY	DESCRIPTION	UNIT PRICE	EXT PRICE
8	48FT	62C600THRZ	141.941/CF	68.13
	-	5/8-11 X 6' THREADED ROD ZN PLTD		
		{48FT/BD}		
		Pn: 40941		
9	3EA	250DPSH/12L/SAF/5/16HOLE	192.311/C	5.77
		2-1/2 SFTY PIPE SHIELD 12"L W 5/16		
		HOLE ROUNDED CORNERS		
		Pn: 734680		
10	13EA	300DPSH/12L/SAF/5/16HOLE	230.268/C	29.93
		3" SFTY PIPE SHIELD 12"L W 5/16		
		HOLE ROUNDED CORNERS		
		Pn: 734682		
11	8EA	350DPSH/12L/SAF/5/16HOLE	254.951/C	20.40
		3-1/2 SFTY PIPE SHIELD 12"L W 5/16		
		HOLE (ROUNDED CORNERS)		
		Pn: 734685		
12	33EA	DEW 7416SD1-PWR	70.264/C	23.19
		3/8 X 5 WEDGE ANCH ZN PWRSTUD+SD1		
		{50/BX}		
		THUNDER STUD		
		Pn: 203384		
13	4EA	DEW 7433SD1-PWR	179.538/C	7.18
		5/8 X 5 WEDGE ANCH ZN PWRSTUD+SD1		
- 1		{25/BX}		
		Pn: 203394		
14	- 1BX	37CHFNZ/P100	5.073/C	5.07
		3/8-16 HEX FIN NUT ZN PLTD PKG		
-		100/BX		7 19
		Pn: 27836		
15	1BX	62CHFNZ/P25	44.132/C	11.03
		5/8-11 HEX FIN NUT ZN PLTD PKG		
		25/BX		
		Pn: 673373		
16	1BX	37DFLWZ/P100	8.059/C	_8. 06
		3/8 USS FLAT WSHR ZN PLTD PKG		1 + 2 + 1
		100/BX		Manual A 10 mas
		Pn: 28472		_
				-

^{**} Continued on Next Page **





QUO	TE DATE	QUOTE NUMBER	PAGE NO.
04/0	2/2024	S4849393	3 of 3

ORDER QT		UNIT PRICE	EXT PRICE
7 1	BX 62DFLWZ/P50	39.964/C	19.98
	5/8 USS FLAT WSHR ZN PLTD PKG 50/BX		
	Pn: 41660		
	-		
		1	
	American Marie - Marie		Nillia commissione
	THE PARTY OF THE P		
			Date .
			•
		-	
			- Lancaban
	The second secon	-	11000011
IS A QUOT	ATION		
ces are firm for 30 days unless otherwise noted and subject to change without notice after 5 days. oted prices are effective for quantities quoted only.		Subtotal	401.63
ibject to cha	inge without notice after 5 days.	S&H Charges	0.00
, T I C A B F	ETAXESEXTRA!		
		Amount Due	401.63

Arden Building Companies, LLC

Recap with Total Cost

Project Name: 1385 Killingly Memorial PLG CO

Bid ID: 230327MJD1

Report Time: 3/27/2024 11:11 AM

Profile Name: Standard

Labor Book: Arden MCA

Scoped By: Alternate: PR #19 ADD (A); System: ALL; Material Spec: ALL;

AutoBid Version: 2021 vI

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 1 of 6

Bid ID: 230327MJD1

Report Time: 3/27/24 11:11 AM

Data Calculated: 3/26/2024 12:49:53 PM

Alternate: PR #19 ADD (A); System: ALL; Material Spec: ALL;

pe					
Carbon Steel - Th	readed Black Sch 40 - Thread				
Material Multiplier	: P1000 - Steel Pipe				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
A53 CW					
1-1/2	37	0.12	4	0	485
Carbon Steel - Thre	aded Black Sch 40 - Thread Totals:				
	37		4	0	485
Cast Iron - Soil, N	o-Hub, - NoHub				
Material Multiplier	: CDF00 - Cast Iron No Hub Pipe & Ftg	s - TYL			
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Pipe 10 ft NH					
2	25	0.12	3	0	376
4	30	0.20	6	0	817
Cast Iron - Soil, No-	Hub, - NoHub Totals:				
	55		9	0	1,193
Copper - DWV - 9	25/5	-			
Material Multiplier	: P2000 - Copper Tube - CER				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Hard Tube	<u>Valiety</u>	CARO DED TEL	20000 2215	334001 0000	10111 0001
1-1/2	8	0.08	1		109
Copper - DWV - 95/	'5 Totals:				
copper with ser					
	8		1	-0-	109
Copper - Type L -	95/5				
Material Multiplier	: P2000 - Copper Tube - CER				
Item Size	Omentity	Unit Lab Hr	Total Hrs	-Labor-Cost-	Total Cost
Hard Tube	Country	OHI Dab III	Total IIIs	Danor-Cost	
1/2	24	0.06	1	0	97
3/4	58	0.06	3	0	383
1-1/2	34	0.08	3	0	550
Copper - Type L - 9:	5/5 Totals:			Part of Part of the Control of the C	
J	1116	-	8	0	1,030
e Totals:	year and the a				
	216		22	- 0	2,818

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 2 of 6

Bid ID: 230327MJD1

Report Time: 3/27/24 11:11 AM

1,441

11

Data Calculated: 3/26/2024 12:49:53 PM

35

ples					
Copper - Short Piece -	95/5				
Material Multiplier: N20	000 - Copper Nipples				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Short Piece				, , , , , , , , , , , , , , , , , , ,	
1/2	1	0.05	0	0	4
3/4	1	0.05	0	0	7
1-1/2	2	0.06	0	0	33
Copper - Short Piece - 95	5/5 Totals:				
	4	-	0	0	43
les Totales	4		0		41
ples Totals:	4		0	0	43
tings					
Cast Iron - Soil, No-H	ub, - NoHub				
Material Multiplier: CD	F00 - Cast Iron No Hub Pipe & Ftg	gs - TYL			
<u>Item Size</u>	<u>Ouantity</u>	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
1/4 Bend Long Sweep					
2	2	0.43	1	0	97
4	4	0.84	3	0	374
1/8 Bend					
4	1 1	0.73			34
C/O Ferrule w/Plug					
4	_1_	0.83	1	0	79
Combination	- View View View View View View View View				
4	1	1.19	1	0	98
Combination - Red			197		
4x4x2	1	0.92	1	0	53
Reducer	the state of the s				
2x1-1/2	r =	0.33	0	0	16
San Tee - Red	h.				
2x2x1-1/2	1	0.51	1	0	31
Wye					
4 = "=	The state of the s	1.12	= 1	<u></u>	66
Wye - Reducing					
3x3x2	1	0.72	1	0_	31
	F30 - No Hub Couplings - TYL			_	
tem Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
	<u> </u>	Out Day H	TVLAL III3	Labor Cust	Total Cost
Jo-Hub Coupling					
No-Hub Coupling		0.00	0	- 0	102

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 3 of 6

Bid ID: 230327MJD1

Report Time: 3/27/24 11:11 AM

Data Calculated: 3/26/2024 12:49:53 PM

tings					
Copper - DWV - 95/	5				
Material Multiplier: F	2700 - Copper Fittings - NIB				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
1/4 Bend					
1-1/2	1	0.65	1	0	66
Copper - DWV - 95/5	Γotals:				
	1		1	0	66
Copper - Pressure -	95/5				
Material Multiplier: F.	2700 - Copper Fittings - NIB				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
90 Deg Elbow					
1/2	6	0.40	2	0	29
3/4	7	0.53	4	0	74
1-1/2	3	0.74	2	0	179
Coupling					
3/4	2	0.53	1	0	14
1-1/2	= 2	0.74	-1	- = 0	65
Reducer					
1-1/2x3/4	2	0.68	1	0	91
Tee					
1/2	1	0.57	1	0_	8
1-1/2	2	1.09	2	0	241
Tee-Reducing					
$1-1/2x1-1/2x1/2 - \frac{1}{2}$		0.85			91
1-1/2x1-1/2x3/4	1	0.91	1	0	91
Copper - Pressure - 95	/5=Totals:				
			_17	0	883
Malleable Iron - Thr	eaded, Black Class 150 - Thread				MER *Box
Material Multiplier: F	1400 - Malleable Iron Fittings - WAR		\$111 B		
Item Size	Ouantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
90 Deg Elbow					
1-1/2	3	1.08	3	0	27
Malleable Iron - Threa	ded, Black Class 150 - Thread Totals:				
******	3		3	0	27
ings Totals:	66	-	31	0	2,418

Arden Building Companies, LLC **Recap with Total Cost**

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 4 of 6

Bid ID: 230327MJD1

Report Time: 3/27/24 11:11 AM

Data Calculated: 3/26/2024 12:49:53 PM

nger Components					
- Clevis -					
Material Multiplier: H000	1 - Hanger Materials - GRN				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Fig 260 Clevis					
2	2	0.00	0	0	14
4	4	0.00	0	0	64
Fig 65 Clevis					
1-1/2	7	0.00	0	0	25
Fig CT6 Clevis CU					
2-1/2	3	0.00	0	0	30
3	13	0.00	0	0	144
4	8	0.00	0	0	120
- Clevis - Totals:					
	37		0	0	397
- Rods -					
Material Multiplier: H000	3 - Hanger Materials - C&P				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Allthread - Galv					
3/8	132	0.00	0	0	871
5/8	16	0.00	0	0	263
- Rods - Totals:					
- Annual Control of Control					
	148		0	0	1,134
- Saddles & Shields	**************************************				#
Material Multiplier: H000	1 - Hanger Materials - GRN				
tem Size	Quantity	<u>Unit Lab Hr</u>	Total Hrs	Labor Cost	Total Cost
Fig 167 Insl Shield			-	AMARIA A.	
2-1/2	3	0.00		0	59
3	13	0.00	0	0	287
3-1/2	8	0.00	= 0	- 0	190
- Saddles & Shields - Tota	als:				
		The second second			536
	24		0	0	350
- Struct Attach-Cone -	24		0	- U	330
	-		· · · · · · · · · · · · · · · · · · ·		350
Material Multiplier: H000	1 - Hanger Materials - GRN	Unit Lab Hr	Comments of the comments of th	inequa.	
	-	Unit Lab Hr	Total Hrs	render	
Material Multiplier: H000 tem Size	1 - Hanger Materials - GRN	Unit Lab Hr	Comments of the comments of th	inequa.	Total Cost
Material Multiplier: H000 tem <u>Size</u> Wedge Anchors	1 - Hanger Materials - GRN Quantity		Total Hrs	Labor Cost	Total Cost
Material Multiplier: H000 tem Size Wedge Anchors 3/8	1 - Hanger Materials - GRN Ouantity 33	0.00	Total Hrs	Labor Cost	Total Cost
Material Multiplier: H000 tem Size Wedge Anchors 3/8	1 - Hanger Materials - GRN Ouantity 33	0.00	Total Hrs	Labor Cost	Total Cost

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 5 of 6

Bid ID: 230327MJD1

Report Time: 3/27/24 11:11 AM

Data Calculated: 3/26/2024 12:49:53 PM

Alternate: PR #19 ADD (A); System: ALL; Material Spec: ALL;

bor					
Hangers					
Item Size	<u>Ouantity</u>	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Clevis Hanger(HgrItem		1.05	7	0	
1-1/2 2	7 2	1.05 1.05	7 2	0	0
2-1/2	3	1.11	3	0	0
3	13	1.11	14	0	0
4	12	1.40	17	0	0
Hangers Totals:			-,		v
	37	_	44	0	0
oor Totals:	37		44	0	0
sc. Consumables					
- Copper Joints Em					
Materiai Maitipher: A Item Size	KNET - Net Material Price Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Emory Cloth	· Aller	y to make the second se		2000	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
Emory Gloth	1	0:00	0	0	0
- Copper Joints Emor	v Cloth - Totals:				
	1	-	0		
		The state of the s	0	0	0
- Copper Joints Flu	ж -			a 4	
	NET - Net Material Price				
<u>Item Size</u> Flux	<u>Ouantity</u>	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Sta-Brite Flux -	1	0.00	0	0	3
- Copper Joints Flux -	- Totals:				
100	1	- val		0	1
	1		0 .	0	3
- Copper Joints Sol	der -			÷	
	KNET - Net Material Price	_	_		
Material Multiplier: X	Quantity	<u>Unit Lah Hr</u>	<u> Fotal Hrs</u>	Labor Cost	Total Cost
<u>Item Size</u>					
<u>Item Size</u> Solder	Control of the Contro				
Solder 95/5	1	0.00	0	0	7
<u>Item Size</u> Solder	1	0.00	0	0	7

Arden Building Companies, LLC **Recap with Total Cost**

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 6 of 6

Bid ID: 230327MJD1

Data Calculated: 3/26/2024 12:49:53 PM

Report Time: 3/27/24 11:11 AM

Alternate: PR #19 ADD (A); System: ALL; Material Spec: ALL;

lisc. Consumables					
- CS Joints CS Thread	ed Joint -	-			
Material Multiplier: XNE	T - Net Material Price				
Item Size	Ouantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
CS Threaded Joint					
Cutting Oil	0	0.00	0	0	0
Joint Compound	0	0.00	0	0	0
- CS Joints CS Threaded	Joint - Totals:				
	0	-	0	0	0
- Gases -	· ·	-			
Material Multiplier: XNE	T - Nat Matarial Price				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Gases	Quantity	Ont Dab III	Total IIIs	Labor Cost	1 otal Cost
Propane	35	0,00	0	0	39
- Gases - Totals:		5,455	Ť	· ·	,
- Gases - Totals.		_			
	35		0	0	39
isc. Consumables Totals:	37		0	0	48
isc. Steel Items					
isc. Steel Items - Bolts, Nuts & Washers			Acres 1		
- Bolts, Nuts & Washers		angendante valendigade at	* mar.		
- Bolts, Nuts & Washers Material Multiplier: H000	3 - Hanger Materials - C&P		Total Live	Labor Cost	Total Cost
- Bolts, Nuts&Washers Material Multiplier: H000 Item - Size			- <u>Total-Hrs</u> -	Labor Cost	Total Cost
- Bolts, Nuts & Washers Material Multiplier: H000 Item — Size Nuts - Galvanized	3 - Hanger Materials - C&P Ouantity - ·	Unit-Lab He			
- Bolts, Nuts & Washers Material Multiplier: H000 Item - Size Nuts - Galvanized 3/8	3 - Hanger Materials - C&P Quantity	Unit Lab Hr	0	0	16
- Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8	3 - Hanger Materials - C&P Ouantity - ·	Unit-Lab He			
- Bolts, Nuts & Washers Material Multiplier: H000 Item — Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized	99 12	Unit Lab Hz	- 0	0	16
- Bolts, Nuts&Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 Washers- Galvanized 3/8	99 12	Unit-Lab-Ha 0.00 -0.00	0	0 0	16 5
- Bolts, Nuts&Washers Material Multiplier: H000 Item — Size Nuts - Galvanized 3/8 5/8 Washers - Galvanized 3/8 5/8	99 12	Unit Lab Hz	- 0	0	16
- Bolts, Nuts&Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 Washers- Galvanized 3/8	99 12 599 12 Totals:	Unit-Lab-Ha 0.00 -0.00	0 0	0 0	16 5 95 39
- Bolts, Nuts&Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 - Bolts, Nuts&Washers - 7	99 12	Unit Lab Hr0.00 -0.00 -0.00 -0.00	0 0 0	0 0	16 5 95 39
- Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 - Bolts, Nuts & Washers - 7	99 12	Unit-Lab-Ha 0.00 -0.00	0 0	0 0	16 5 95 39
- Bolts, Nuts & Washers Material Multiplier: H000 Item - Size Nuts - Galvanized 3/8 5/8 - Bolts, Nuts & Washers - 7	99 12 599 12 Totals:	Unit Lab Hr0.00 -0.00 -0.00 -0.00	0 0 0	0 0 0	16 5 95 39
- Bolts, Nuts&Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 - Bolts, Nuts&Washers - 7	99 12	Unit Lab Hr0.00 -0.00 -0.00 -0.00	0 0 0	0 0 0 0	16 5 95 39 155
- Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 - Bolts, Nuts & Washers - 7	99 12	Unit Lab Hr0.00 -0.00 -0.00 -0.00	0 0	0 0 0	16 5 95 39
- Bolts, Nuts&Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers - Galvanized 3/8 5/8 - Bolts, Nuts&Washers - Colors, Nuts&W	99 12	Unit Lab Hr0.00 -0.00 -0.00 -0.00	0 0 0	0 0 0 0	16 5 95 39 155
- Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers - Galvanized 3/8 5/8 - Bolts, Nuts & Washers - D	99 12	Unit Lab Hr0.00 -0.00 -0.00 -0.00	0 0 0	0 0 0 0	16 5 95 39 155

^{*} Items flagged with an asterisk may have their price and labor overwritten in Excel's Rapid Reports

Arden Building Companies, LLC

Recap with Total Cost

Project Name:

1385 Killingly Memorial PLG CO

Bid ID:

230327MJD1

Report Time:

3/27/2024 10:59 AM

Profile Name:

Standard

Labor Book:

Arden MCA

Scoped By:

Alternate: PR #19 Deduct (A); System: ALL; Material Spec: ALL;

AutoBid Version: 2021 v1

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 1 of 5

Bid ID: 230327MJD1

Report Time: 3/27/24 10:59 AM

Data Calculated: 3/26/2024 12:49:53 PM

pe					
Cast Iron - Soil, No-	Hub, - NoHub				
Material Multiplier: (CDF00 - Cast Iron No Hub Pipe	& Ftge - TVI			
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Pipe 10 ft NH	Quantity	Ont Dab III	10tal IIIS	Labor Cost	Total Cost
-	3	0.16	0	0	42
3	2 8		0	0	42
Cast Iron - Soil, No-H	·	0.20	2	0	222
Cast from - Son, No-II		5			
-	10		2	0	264
Copper - DWV - 95/	5				
Material Multiplier: P	2000 - Copper Tube - CER				
<u>Item Size</u>	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Hard Tube	-				
1	3	0.07	0	0	14
Copper - DWV - 95/5					~ ·
	3		0	0	14
Copper - Type L - 9:	5/5				
Material Multiplier: P	2000 - Copper Tube - CER				
Item Size	<u>Ouantity</u>	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Hard Tube				200001	20147 0050
1/2	18	0:06	1	0	71
3/4	24	0.06		0	158
· 1-1/2 =	50	- 0.08	4	0	815
Copper - Type L - 95/5		0:00	Т.	•	913
= appear albertage	-				
	92	- sphinister	7_	0	1,044
ipe Totals:	105	and Garagement	9	0	1,322
			4. 4.	-	,
(1					
ipples ·	0.5/5				
Copper - Short Piece	e - Y5/5				
Material Multiplier: N	2000 - Copper Nipples				
Item Size	Ouantity	Hnit Lab Hr	Total Hrs	Labor Cost	Total Cost
Short Piece					
. 1/2	1	0.05	0	0	4
3/4	-2	0.05	-0		13
	2	0.05	0		19
Copper - Short Piece -	95/5 Totals:				
	5	-	0	0	36
ipples Totals:	5		0	0	36
Elecorit otato.	3		U	<u>U</u>	36
	THE RESERVE OF THE PARTY OF THE				

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 2 of 5

Bid ID: 230327MJD1

Report Time: 3/27/24 10:59 AM

Data Calculated: 3/26/2024 12:49:53 PM

Alternate: PR #19 Deduct (A); System: ALL; Material Spec: ALL;

tings						
Cast Iron - Soil, No-H	lub, - NoHub					
Material Multiplier: CD	OF00 - Cast Iron No Hub Pipe	& Ftgs - TYL				
Item Size 1/4 Bend	<u>Ouantity</u>	Unit La	<u>b Hr</u>	Total Hrs	Labor Cost	Total Cost
4	4		0.78	3	0	184
Combination						
3	1		0.86	1	0	51
P-Trap						
3	1		0.65	1	0	71
Wye						
4	1		1.12	1	0	66
Motorial Multiplian CD	DF30 - No Hub Couplings - TY	T				
-	Ouantity	Unit La	h He	Total Hrs	Labor Cost	Total Cost
<u>Item Size</u> No-Hub Coupling	<u>Vuantity</u>	Omt Da	V 111	1 VIAI 1113	Danoi Cost	1 otal Cust
3	2		0.00	0	0	49
4	7		0.00	0	0	201
Cast Iron - Soil, No-Hub	•				-	
=						
	16			6	0	622
Copper - DWV - 95/5						
D. C	BOO C FILL BIND					
•	700 - Copper Fittings - NIB	T1-14 T	L TT	Tetal II	1 -b C4	T-4-1 C4
<u>Item Size</u> — 1/4 Bend	Quantity	Ont La	D III	Total Hrs	Labor Cost	Total Cost
1/4 Dend	1		0.50	1	0	12
Combination	- '	No.	0,50			12
3/4	1		1.02	1	0	2
Reducing Coupling			1.02	,		
1x3/4	1	emper eyen v	0.97	1	0	7
		- Interior -	.W> (_		v	,
Conners DWV - 05/5 To	Julio.					
Coppers DWV - 95/5 To	<u> </u>					
Copper DWV - 95/5 To	3			2	0	21
	3			2	0	21
Copper - Pressure - 95	5/5			2	0	21
Copper - Pressure - 95 Material Multiplier: F2	5/5 700 - Copper Fittings - NIB	·				
Copper - Pressure - 99 Material Multiplier: F27 Item <u>Size</u>	5/5		b Hr	2 Total Hrs	Labor Cost	21 Total Cost
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow	5/5 700 - Copper Fittings - NIB Quantity	Unit La		Total Hrs	Labor Cost	Total Cost
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2	5/5 700 - Copper Fittings - NIB Quantity 5	Unit La	0.40	Total Hrs	Labor Cost	Total Cost
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2 3/4	5/5 700 - Copper Fittings - NIB Quantity 5	Unit La	0.40	Total Hrs	Labor Cost 0 0	Total Cost
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2 3/4 1-1/2	5/5 700 - Copper Fittings - NIB Quantity 5	Unit La	0.40	Total Hrs	Labor Cost	Total Cost
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2 3/4 1-1/2 Coupling	5/5 700 - Copper Fittings - NIB Quantity 5	Unit La	0.40 0.53 0.74	Total Hrs	Labor Cost 0 0 0	Total Cost 24 74 298
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2 3/4 1-1/2 Coupling - 1-1/2	5/5 700 - Copper Fittings - NIB Quantity 5	Unit La	0.40	Total Hrs	Labor Cost 0 0	Total Cost
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2 3/4 1-1/2 Coupling - 1-1/2 Tee-Reducing	5/5 700 - Copper Fittings - NIB Ouantity 5 7. 5	Unit La	0.40 0.53 0.74	2 4 4 4	0 0 0 0	Total Cost 24 74 298
Copper - Pressure - 95 Material Multiplier: F27 Item Size 90 Deg Elbow 1/2 3/4 1-1/2 Coupling - 1-1/2	5/5 700 - Copper Fittings - NIB Quantity 5	Unit La	0.40 0.53 0.74	Total Hrs	Labor Cost 0 0 0	Total Cost 24 74 298

Arden Building Companies, LLC **Recap with Total Cost**

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 3 of 5

Bid ID: 230327MJD1

Report Time: 3/27/24 10:59 AM

Data Calculated: 3/26/2024 12:49:53 PM

Alternate: PR #19 Deduct (A): System: ALL: Material Spec: ALL:

tings						
Copper - Pressure - 9	5/5					
Material Multiplier: F2	700 - Copper Fittings - NIB					
Item Size	Quantity	<u>, U</u>	nit Lab Hr	Total Hrs	Labor Cost	Total Cost
Tee-Reducing						
2x2x3/4	1		1.00	1	0	145
Copper - Pressure - 95/	5 Totals:					
	23			15	0	991
ings Totals:	42		_	23	0	1,634
nger Components						
- Clevis -						
Material Multiplier: H0	0001 - Hanger Materials - GRN					
Item Size	Quantity	Ţ	nit Lab Hr	Total Hrs	Labor Cost	Total Cost
Fig 260 Clevis						
4	2		0.00	0	0	32
Fig CT6 Clevis CU						
2-1/2	4		0.00	0	0	40
3	6		0.00	0	0	66
4	15		0.00	0	0	225
- Clevis - Totals:	- 8	-	***			
	27			0	0	364
- Rods -	ammet.com		A SHOP IS	, +,		
Material Multiplier: H0	003 - Hanger Materials - C&P					
Item Size	Ouantity	-11	nit Lab Hr	Total Hrs	Labor Cost	Total Cost
Allthread - Galv			-			
3/8	100		0.00	- 0	0	660
5/8	8		0.00	0	0	132
- Rods - Totals:						
	108			0	0	791
- Saddles & Shields -	- v vel	-				
	_	_				
-	001 - Hanger MaterialsGRN					= =
Item Size	<u>Quantity</u>	<u>U</u>	nit Lab Hr	Total Hrs	Labor Cost	Total Cost
Fig 167 Insl Shield	B					
2-1/2	4		0.00	0	0	-79
3 1/2	6		0.00	0	0	132
3-1/2	15		0.00	0	0	356
- Saddles & Shields - T	otals:					
	25			0	0	567
						507

Arden Building Companies, LLC **Recap with Total Cost**

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Bid ID: 230327MJD1

1

Data Calculated: 3/26/2024 12:49:53 PM Alternate: PR #19 Deduct (A); System: ALL; Material Spec: ALL; Page: 4 of 5

Report Time: 3/27/24 10:59 AM

anger Components					
- Struct Attach-Conc -			mak s		
Material Multiplier: H0001	- Hanger Materials - GRN				
<u>Item</u> <u>Size</u>	<u>Ouantity</u>	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Wedge Anchors					
3/8	25	0.00	0	0	22
5/8	2	0.00	0	0	3
- Struct Attach-Conc - Tot	cals:				
	27		0	0	25
anger Components Totals	187				
anger Components Totals:	187		0	0	1,747
abor					
Hangers					
Ti O'	0 "		70 . 177		
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Clevis Hanger(HgrItem Preca					
3	4	1.11	4	0	0
3 4 .	6 17	1.11 1.40	7	0	0
·	17	1.40	24	0	0
Hangers Totals:					
hadana juma juma ,	27		35	_ 0	0
bor Totals:	27		35_	0	0
				Total	
isc. Consumables					
- Copper Joints Emory C	Cloth -			- 100.000	
Material Multiplier: XNET	- Net Material Price		the state of the s	and the second	
<u>Item</u> <u>Size</u>	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Emory Cloth					
Emory Cloth	0	0.00	0	0	0
Emory Cioni	th -: Totals:			-4	
- Copper Joints Emory Clot	on and outside				
		-		0	
- Copper Joints Emory Clot		-	0	0	0
			0	0	0
- Copper Joints Emory Clot - Copper Joints Flux - Material Multiplier: XNET	- Net Material Price	-		0	
- Copper Joints Emory Clot - Copper Joints Flux - Material Multiplier: XNET Item Size	- O.	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
- Copper Joints Emory Clot - Copper Joints Flux - Material Multiplier: XNET	- Net Material Price	Unit Lab Hr	Total Hrs	Labor Cost	

Arden Building Companies, LLC Recap with Total Cost

There were 40 calculation messages.

Project Name: 1385 Killingly Memorial PLG CO

Page: 5 of 5

Bid ID: 230327MJD1

Report Time: 3/27/24 10:59 AM

Data Calculated: 3/26/2024 12:49:53 PM

Alternate: PR #19 Deduct (A); System: ALL; Material Spec: ALL;

isc. Consumables					
- Copper Joints Solder	-				
Material Multiplier: XNE	T - Net Material Price				
<u>Item</u> <u>Size</u>	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Solder					
95/5	1	0.00	0	0	5
- Copper Joints Solder -	Fotals:				
	1		0	0	5
- Gases -					
Material Multiplier: XNE	Γ - Net Material Price				
Item Size	Quantity	Unit Lab Hr	Total Hrs	Labor Cost	Total Cost
Gases					
Propane	27	0.00	0	0	30
- Gases - Totals:					
	27		0	0	30
sc. Consumables Totals:		· ·	0	0	37
			0	0	37
isc. Steel Items - Bolts,Nuts&Washers Material Multiplier: H000				0 (37
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size	-	Unit Lab Hr		Labor Cost	Total Cost
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized	3 - Hanger Materials - C&P Quantity	Militar	Total Hrs	Labor Cost	Total Cost
sc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8	3 - Hanger Materials - C&P Ouantity 75	0.00	Total Hrs	Labor Cost	Total Cost
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8	3 - Hanger Materials - C&P Quantity	Militar	Total Hrs	Labor Cost	Total Cost
sc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized	3 - Hanger Materials - C&P Quantity 75 6	0.00 -	Total Hrs 0 0	Labor Cost 0	Total Cost
sc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8	3 - Hanger Materials - C&P Ouantity 75	0.00 0.00 =	Total Hrs	Labor Cost 0 0	Total Cost 12 2 72
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8	3 - Hanger Materials - C&P Ouantity 75 6	0.00 -	Total Hrs 0 0	Labor Cost 0	Total Cost
sc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8	3 - Hanger Materials - C&P Ouantity 75 6 75 Cotals:	0.00 0.00 =	0 0 0	Labor Cost 0 0 0	Total Cost 12 2 72 19
sc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8 - Bolts, Nuts & Washers - T	3 - Hanger Materials - C&P Ouantity 75 6 75 75 162	0.00 0.00 =	Total Hrs 0 0	Labor Cost 0	Total Cost 12 2 72
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8 - Bolts, Nuts & Washers - Totals:	3 - Hanger Materials - C&P Ouantity 75 6 75 Cotals:	0.00 0.00 =	0 0 0	Labor Cost 0 0 0	Total Cost 12 2 72 19
sc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8 - Bolts, Nuts & Washers - T	3 - Hanger Materials - C&P Ouantity 75 6 75 75 162	0.00 0.00 =	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	0 0 0	Total Cost 12 2 72 19
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8 - Bolts, Nuts & Washers - Totals:	3 - Hanger Materials - C&P Ouantity 75 6 75 75 162	0.00 0.00 =	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	0 0 0	Total Cost 12 2 72 19 106
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8 - Bolts, Nuts & Washers - Totals:	3 - Hanger Materials - C&P Ouantity 75 6 75 75 162	0.00 0.00 =	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	0 0 0	Total Cost 12 2 72 19
isc. Steel Items - Bolts, Nuts & Washers Material Multiplier: H000 Item Size Nuts - Galvanized 3/8 5/8 Washers- Galvanized 3/8 5/8 - Bolts, Nuts & Washers - Totals:	3 - Hanger Materials - C&P Ouantity 75 6 75 75 162	0.00 0.00 =	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	0 0 0	Total Cost 12 2 72 19 106

^{*} Items flagged with an asterisk may have their price and labor overwritten in Excel's Rapid Reports



47 Rogers Street Apt. #3 Branford, Ct. 06405 Phone: 203-710-8017

02/26/2024

COR: No. 5

To: MJ Daly Att: Nick

Re: Killingly Memorial School

Danielson, Ct. Our Job #5053

We are pleased to submit for your review our request for a change order to furnish the necessary Labor, material, tools and equipment for the following work at the above referenced project.

Our add/deduct in regards to proposal request #19 relocate equipment In the kitchen area.

Credit

Material	Hours @ \$91.09	Labor	Tax	Total
(-\$175.08)	8	(-\$728.72)	N/A	(-\$903.80)

Add

Material	Hours @ \$93.84	Labor_	10% O/P	Tax	Total
\$230.17	10	\$938.40	\$116.86	\$N/A	\$1,285.43

Total: ADD \$361.63

NOTICE: THIS PROPOSAL IS CONTINGENT ON A LACK OF IMPACT BY THE CORONAVIRUS NATIONAL EMERGENCY. Given the existence of the coronavirus pandemic, Axion Specialty Contracting LLC will use its best efforts to staff and supply this project to meet the scheduled completion date. However, Axion Specialty Contracting LLC reserves its right to seek an excusable extension of time if Axion Specialty Contracting LLC or its suppliers are unable to maintain planned crew sizes or material due to the illness, supply shortages or governmental restraints on business, travel and/or assembly. To the extent that the project is suspended pursuant to the terms of the proposed Subcontract, we intend to seek additional costs associated with the suspension.

We appreciate the opportunity to quote on your insulation requirements. Should you require any additional information, please feel free to contact me on my cell phone at (203) 710-8017.

Thank You
Axion Specialty Contracting LLC.

David DeMarco



P&D MECHANICAL, INC.

HVAC / Plumbing Contractor CT PLM .0204662-P1 CT HTG .0385878-S1

R1#MP01940

RI#MF00006481

627 Old Hartford Road, Colchester, CT 06415 Phone: (860) 537-0617 Fax: (860) 537-0839

Email: Info@PDMechanical-Inc.com Affirmative Action / Equal Opportunity Employer

February 22, 2024

Doug Triba Downes Construction Company 200 Stanley Street New Britain, CT 06051

RE:

Killingly Memorial School

339 Main Street Danielson, CT 06239 Project No. 069-0069 RNV

SUBJECT:

P&D Mechanical Change Order Proposal No. 026

PR #019 Relocated kitchen equipment. Revise previously completed

coordination drawings.

Dear Mr. Triba,

In regards to the above-captioned project and subject matter, P&D Mechanical Inc. submits its breakdown costs in the amount of **Four Hundred Ninety-Two Dollars and 76/100 (\$492.76)** for the abovementioned work.

This proposal will be reviewed as quickly as possible by all parties and will remain firm for ten (10) days. All items and conditions of our original contract apply except as specifically modified by this proposal. P&D Mechanical reserves the right to modify this proposal should direction on how to proceed not be received in writing, in this office, within ten (10) days from the date of this proposal. No materials will be ordered or work started until an executed change order is received in our office. This work adds **Ten (10)** days to the project schedule after a receipt of an executed change order.

Exclusions are as follows; all electrical work, concrete work, cutting and patching of existing/new structure, no holidays or Sundays. Any additional PPE equipment i.e., exhausts fans, negative air machines, etc. above and beyond our approved AHA. No excavation. Shutdowns will be by others. Should you have any questions or comments, please contact our office at 860-537-0617.

Note: Lost of Bond is NOT included and will be determined at project completion.

Respectfully,

David Warzecha

Project Manager

P&D Mechanical, Inc.

General C	ontractor:	Downes Cons	atruction	Compan	v	Projec	at Name & A	Address:	Job # 262	- Killingly	Memorial Schoo	1 - H	VAC
General 2	Original.	200 Stanley Si New Britain, C	treet		,	110,00	Halle &	339 Main S Danielson,					
Subcor	ntractor:	P&D Mechanic 627 Old Hartfo Colchester, Co	ord Road			Chan	ige Order N	umber:	026	Date:	February 22, 2024		
Descr	ription:	PR #019 R	elocate	d kitcher	equipme	ant. Rev	ise previo	iusly com	pleted co	ordinatio	on drawings.		
Quantity	Unit						nd/or Equip lown Sheets				Unit Cost	g	Total
	EA				P&F	D Materia	als				\$ -	\$	
	EA										\$ -	\$	
	EA										\$ -	\$	-
	EA									$\overline{}$	\$ -	\$	
Line 1	EA				We di				Materi	al and/or	Equipment Total		
	He s	16 37		Base		H		Worker/ Comp.	General Liability				
Crow	Labor	Classification	Hours	Rate	FICA	FUTA	\$UTA	insurance	Insurance	Benefits	Total Rate	100	Total
	Plumber/ Fitter	r		48.28	3.69		3.28				103.60	-	
	Supervisor			53.28	4.08	-	3.62		+			_	
	Project Manag	er	-	76.94	5.89		5.23				135.71	_	- 47.05
	Draftsman		4	59.25	4.53		4.03					_	447.96
	Pimb App. 80%		-	38.62	2.95		2.63 4.92				90.88 131.37	_	=
	Plumber/ Fitter Supervisor 1-1.		-	72.42	5.54 6.11		4.92 5.43					_	-
	Project Manag		_	115.41	8.83		7.85		+				-
	Plumber/ Fitter			96.56	7.39		6.57	2.82		-	159.16		-
	Supervisor Do			106.56	8.15		7.25					_	-
	Project Manag			153.88	11.77	0.92	10.46		1.09			\$	
	Plumber/Fitter	Premium - OT		24.14	1.85		1.64				27.77		•
		% Premium - OT		19.31	1.48		1.31				22.22		-
	Supervisor Pre			26.64	2.04		1.81			\longrightarrow	30.65		-
ine 2	Project Manage	ger.Premium - OT		38,47	2.94	0.23	2.62				44.26 Labor Total:		447.96
	Trade		T				t (Attached	Proposeis		Cast In	apact (YES/NO)		Cost
	Sheet Met	est			14 10 11 100	5 OI SOU	contractor			COSt His	pattites/HO	\$-	COST
	Insulation		_					-	-			\$	
Testing	Adjusting 8											\$	
		ture Controls						100 mil		-	-	\$	-
	Other											1	
								-				\$	-
line 3										Subr	contractor Total:	\$	
					ead & Profi	it				Allow %	Amount		Total
		med Work (Amo								10%		-	44.80
	Subcontrac	ct Work (Amount	t = Line 3	5)					Contractor	5%		\$	## SD
ine 4						-			Contractors	Overhead	and Profit Total:	\$	44.80
Jine 5						Su	n Total Pro	nosed Cha	nee Order	Amount ()	ine 1+2+3+4);	4	492.76
						and the same					A T 60 7 M. P. TARY	100	Towns to
ine 6									THE REAL PROPERTY.		Bond (1.56%)	_	

-





Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 Phone: (860) 229-3755 **Project:** 25-01-0447 - Killingly Memorial School Killingly, Connecticut

Prime Contract Potential Change Order #320: CE #320 - Radon Pit Demolition

TO:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	320 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM:	48 Employable St. And Bed - eggs (4 in a first de this phyllines is a plan in some express of physicisms droughly spills with a sinuscial and a sinuscial a	CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	3/18/2024
REFERENCE:	and the second of	PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No		STREET, SAN OR
LOCATION:	THE W	ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:	And the state of t	PAID IN FULL:	No.
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	
NO CONTROL OF THE CON	- 59 198	TOTAL AMOUNT:	\$0.00

POTENTIAL CHANGE ORDER TITLE: CE #320 - Radon Pit Demolition

CHANGE REASON: Backcharge

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract is Changed As Follows)

CE #320 - Radon Pit Demolition & Excavation

Back-charge concrete contractor (marguerite) to have demolition contractor (AAIS) perform cutting, removal and excavation of the Radon Pit.

ATTACHMENTS:

#	Budget Code	Description	Amount
1_	001.01-200.S Construction.Demolition & Hazmat.Subcontractor		\$2,576.94
2	001.03-300.S Construction.Concrete.Subcontractor		\$(2,576.94)
	·-	Grand Total:	\$0.00

-Antinozzi-Associates

Town of Killingly

271 Fairfield Ave.

172 Main Street

Bridgeport, Connecticut 06604

Killingly, Connecticut 06239

Downes Construction Company

200 Stanley St

New Britain, Connecticut 06051

DocuSigned by:

SIGNATURE

David Ferris

4/8/2024

DATE

SIGNATURE

DATE

0 . . .

4/8/2024

SIGNATURE

DATE

							orial Sch							_			
Affiliation of page	nitra establista			C	hange C	rder	Proposal F	FI		1	reset, s	: '}'	di Kilin			1	THE THE STATE OF
To:	Downes Con			Da			trum Enviro 3/11/24-3										
Ref:	30 STATE	CO 42			i Numbe		COD Numbe				Court Color	1.42	en of contracts	1			
					ket Num		COP Numbe	l:		-	PCC	WINNEY		ł			
D-sadutlana		Taken Provide Graphs	er singer pegnegnese	_			Andrew Tall at the St.		(1.00)	_		_		200	. 20 N L (17 N L	erender.	and Personal
Description:							CE MIS				OIV Kai	10	n				
Quantity	Unit		De	scrip	tion of N	/lateria	al and Equip	men	t					Ų	nit Cost		Total
1	Material 1			-	MI-Se					-				\$		\$	
1	Material 2													\$		\$	-
1	Equip 1													\$	- 3	\$	-
1	Equip 2													\$	-	\$	-
1	Equip 3									_				\$	-	\$	
1	Equip 4											_		\$		\$	
1	Equip 5							303				_		\$	-	\$	"
1						_		_		_		_		\$	-	\$	
ine 1										_	Ma	t-marin	145-	\$	ent Total	\$	
ane 1											IVIG	tena	ar ar iu cy	uihiii	ient rotar	1 3	
Crew	Labor Cl	assification	Hours	Ba	ise Rate	FIC	A & Med		UTA &	G	/L, W/C	8	enefits	То	tal Rate		Total
	For	reman	10.00	\$	42.00	\$	8.40	\$	1.26	\$	11.76	\$	26.37	\$	89.79	\$	897.90
										Т							
		borer	22.00	_	34,00	\$	5.78	\$	1,02	\$	9.52	\$	26.00	\$	76.32	\$	1,679.04
		erator		\$	47.00	\$	9.40	\$	1.41	\$	13.16	\$		\$	97.97	_	
		borer		\$	34.00	\$	5.78	\$	1.02	\$	9.52	\$	26.00	\$	76.32		
	1a	borer		\$	34.00	\$	5.78	\$	1.02	\$	9.52	\$	26.00	\$	76.32	_	
	4			\vdash		_		-		⊢		-		\$		\$	
				_		_		-		⊢		-		\$		\$	
						_		-		-		-		Ś		\$	
	T'			-				\vdash		┢				\$		\$	
										1				Ś	H	Ś	
Line 2										1			1		bor Total	<u> </u>	2,576.94
Subcontractor	Cost (Attach Pro	posals)															
Trade				Naı	me of Su	bcontr	actor										Total
																\$	-
Ü.				_													
												_					
												_		-		4	
Line 3				_				7				_	Subco	ntrae	ctor Total	\	
Line 4	Total Labor,	Material, and Equip	ment													\$	2,576.94
	in elektrokioni	er (Aupenia)				(10)			(1)			7.5		2011	76.74 1971	V. CARDOON	
			7.4				10436 (12)							5 N S			3.5 (4.4.24) 2.14
		n tre							77. A.		151.871.16		116	11	all fall		
0.4	ar Karan	ales ales projections	(4) P. 10 P. 10 P. 10		(0.5)		1.00			COL	0.00		pk.7%		7.7		
Springer Street	Saturdaya .	orania anda	amin's consecution					70.1					90, 77			(1) Y	9786
SOURCE STREET, SECOND CONTRACTORS	A COLUMN TO THE PARTY OF THE PA	Control of the Contro					THE PERSON NAMED IN COLUMN		The same of the sa				ale characteristic con	- Contraction	AND THE PROPERTY OF STREET	The state of the	- AND THE PROPERTY OF THE PARTY



Pco 42

ADDITIONAL WORK AUTHORIZATION

Margarite

	·			ob Ne	me			<u>D</u>	ate	,	Jo	b Numl	er
DOWNES CONSTRUCTION	Kill	Lhso	4.1	(5070	yeiq	(8)	lev!	2-2	2-24	#.	3 kao 9	86	
Job Address:	20	y u:r:	MA	ا ارسالت در درس	,	51. M	: 22		RADON Ropert N. 2.				
Labor	- 7/1		-	20 N	<u> </u>	. [-	7	MEA	ND I	WATE	DIVI	VERI	ICAT!
Employee Name	М	Ť	W	T					-		_		
OSCAR Hermandors	101	7_		-£-	F	S.	3	DO	-C	S C OMP	CNS Any	RUE	TOP
FOREMAN OF								0	. ^			-	
Angel VERA si	-	4					L.,	LXXVIII O	s tion	structio	n Com	pany LL erials uti	Chereb
LABORER OF						-0-4	de	Scribed Scribed	mulk.	Was no	no mai	This v	ized for
ŠT	**			-		-	W	rk perio	rmed	does n	ataria ataria	ve the si	inicatio
or			-				-	from ex	mply	in with	he cor	ract do	Monte
·or	-						t	Joon Tel	YEW.	the we	TK IS NO	Unnd in	PARAG
ST								TUBE CO	uracti	docum	erits a c	hange o	mar will
óu.						-		be is	SUBO	arier ar	levorac	by the C	wher
51	-	-					-		_Arc	illect ar	nd/or E	gineerl	
					Acres and the second	201	0.555	223 (2)	- 1				
or		7		-				- al -		*			·
Description of Work:]					8			2	Ç 23/8	634	
Description of Work: None 5 - Cut CONCR. Pit. 6 X 6 - POWER TO			*************				<u> </u>	ATE:		***************************************	R.A.	ozy DOM FOR	
Description of Work: Nove 5 - Cut concre Pit 6' X 6			*************				<u> </u>	ATE:		***************************************	R.A.	DO.H.	
Description of Work: Now 5 - Cut CONCRI Pit. 6' X 6 - POWER TO SAFETY			*************				<u> </u>	ATE:		Sub T	otal	DO.H.	
Description of Work: Cut concre Pit-6 × 6 Power to SAFETY Power of Customer or Foreman 10 Power to Power to			*************				<u> </u>	ATE:		WN	otal	DO.H.	
Description of Work:		-E	T.A.	5			<u> </u>	ATE:		Sub T	rotal chief	DO.H.	



ADDITIONAL WORK AUTHORIZATION Margaritel

Customer				ob N	me			Date	Jo	b Number
DOWNES CONSTRUC	Tron	K: // 339 DAN:	HA HA	Y M IIN SOM	<i>2600</i> /3	ral Ti	5A	2-21-24	# 3100 Rapor Report	I PTT
Labor					-		1	TIME ALL		
Employee Name		MT	Tw	Ť	F	S	1	TIME AND	MATERIA	VERIFICATI
OSOGA Hernandez	57	***	18			3	1-7-	Total Units	Rate	- listension
_	τΩ						+	DOWN	COMPAN	TRUCTION
Foreman	07					.,.			SO WE AIN	FLLC.
Angel Vena	51		16					Downes Co	Beforetion Con	pany, LLC hereby
LABOREL	70		-							
NILMER PARDO	ST		8			-	- 0	oscribed wor	(Was nerforme	d. This verification
	ori		10				W			
LABORER	TO							from comple	ino with the	ve the subcontrac itract documents.
FRIC CYR	ST		6	-			++			
9 22	OT			-			11			
LABORER	ot						11	be issued	after approval	wanda cadel Ass
	21						T	Arc	hitect and/or E	TOWNS LANGE
	or .					J			المسمد	ightest.
								Hotele Ho		3/3004 3/3004
Backcharge	to	M	alo	<u> </u>		01	۷	Webst bijangin (.esakit .hpp., .		
nature of Customer or Foreman	Ž					Thinkshopse and	7 4 7 414,	Other	Sub Total	



PCO #321

Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 Phone: (860) 229-3755

Project: 25-01-0447 - Killingly Memorial School Killingly, Connecticut

Prime Contract Potential Change Order #321: CE #21G - Drop & Cut MEP Systems into Manageable Sections Batch #07

то:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	321 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM	l:	CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	3/25/2024
REFERENCE:		PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No		displantation of the control of the
LOCATION:		ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:	richinden Erichtes, imperioration autoritation appendus ses vers energias (includentes), independentes i	PAID IN FULL:	No
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	
	And de Barrier ann ann an Barrier an Ann	TOTAL AMOUNT:	\$0.00

POTENTIAL CHANGE ORDER TITLE: CE #21G - Drop & Cut MEP Systems into Manageable Sections Batch #07

CHANGE REASON: Construction Contingency

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract is Changed As Follows)

CE #21G - Drop & Cut MEP Systems into Manageable Sections Batch #07

Furnish all labor, material and equipment to Drop existing MEP systems to floor and cut into manageable sections. This scope item to drop systems to floor and cut into manageable sections was not purchased from HVAC or Demo contractor in base bid. This is associated with all cut & drop operations from 01/10/24 to 02/28/24

Base Bid Scope:

- 1. HVAC subcontractor is responsible to disconnect and make safe
- 2. Demo subcontractor is responsible for removal after its dropped to floor and cut into manageable sections

ATTACHMENTS:

#	Budget Code	Description	Amount
	001.01-200.S Construction.Demolition & Hazmat.Subcontractor	Demolition	\$6,331.00
	001.70-001:M Construction.Contingency.Material (Procore)	CM Contingency	\$(6,331.00)
		Grand Total:	\$0.00

Antinozzi Associates		Town-of-Killingly		Downes Construction (Company
271 Fairfield Ave.		172 Main Street		200 Stanley St	
Bridgeport, Connecticut	06604	Killingly, Connecticut 06239		New Britain, Connecticut	06051
DocuSigned by: David Jerris	4/8/2024			Douglas Triba	4/8/2024
SIGNATURE	DATE	SIGNATURE	DATE	SIGNATURE	DATE

	************			K	Illingly	М	lemorial Sch	pol		AV.							
		-		C	hange C	Ord	ier Proposal R	FI									
To:		nstruction Co.		CN	om: ite: 4 Numbe	ir:	pectrum Enviro 3/22/24		ental	-							
							tor COP Numbe	r:		L							
	i			Tlo	ket Num	bei		_			1/10/24	to 2	/28/24	L			
Description:							MEP Cut I	Dre	op Bat	ch	7						
Quantity	Unit		De	scri	ption of M	dat	terial and Equip	me	nt	_		-		П	Jnit Cost		Total
1	Material 1			TI C	-	-	TAIL T							\$	-	\$	-
1	Material 2											_		\$		\$	•
1	Equip 1													\$		\$	_
1	Equip 2													\$		\$	
1	Equip 3													\$	-	\$	
1	Equip 4													\$		\$	-
1	Equip 5													\$		\$	
1														\$	-	\$	
1						_								\$		\$	
Line 1				_		_				_	Ma	terl	al and Eq	ulpn	rent Total	\$	
Constitution	1.1			-		_				_		_		_			
Crew	Laborci	lassification	Hours	Ba	ise Rate		FICA & Med Care		SUTA &	٩	i/L, W/C Ins	8	enefits	To	otal Rate		Total
	Fo	reman	8.00	\$	42.00	\$	8.40	\$	1.26	\$	11.76	\$	26.37	\$	89.79	\$	718.32
	La	borer	66.00	\$	34.00	\$	5.78	\$	1.02	\$	9.52	\$	26.00	\$	76.32		5,037.12
	Op	erator	5-54-54H-507-15-A	\$	47.00			\$	1.41	\$	13.16	\$			97.97		3,037122
	La	borer		\$	34.00			\$	1.02	\$	9.52	\$		\$	76.32		
	La	borer		\$	34.00			\$	1.02	\$	9.52	Ś		\$	76.32	\$	
						Ė		Ť		Ė		Ť		\$	2	\$	
					See Silve					Г				\$	-	\$	-
= 1.250001180						Г								\$	-	\$	-
												Ĵ.,,		\$		\$	
								_						\$		\$	Welling Street
									water Enversely					\$	eren un t onen	\$	
Line 2														La	bor Total	\$	5,755.44
5. d	-			_													
Subcontractor Co Trade	ST (Attach Pro	posais)		b.L.	. (c.)	_		_		_		_				_	
ilaue				Nar	ne or Sui	000	ontractor	_		_		_		_			Total
					-	-										\$	
			****			-		_		_		_		-		-	
		-		_				0.00				_	_			_	
Line 3		AU-100		_			*			11121		_	Subcor	trac	tor Total	Ś	-
				_				_									
Line 4	Total Labor, N	Vlaterial, and Equ	ipment			_								_		\$	5,755.44
Contractor Overh	ead and Profit					-				ΔII	w %	-	Amo	ne see		_	Total
Net Value of Self			ies 1+2)	_		_		_			10%	\$	Aint		$\overline{}$	ć	Total 575 54
Net Value of Subc						_	h			-	5%	\$				\$	575.54
line S										C		_	rhead an	d Pr	ofit Total	_	575.54
Manager and an artist of the second				_		-		-					TARGETT SITE			<u> </u>	373.34
.ine 6	Total Propose	ed Change Order	Amount (Lines 4+5)													\$	6,331
										_							5,50-



Customer	1		Je	ob Na	me			Date	Job	Number
KMS - DOWNES Job Address:			F/Y M, IE			<u>el</u> 51.	Sca.	1-10-24	# 3100 Cut/Dec Report # 3	786 V #110-A
Labor										
Employee Name	М	Т	W	Т	F	S	S	Total Units	Rate	Extension
Oscar Hernander ST			1							
Foreman on						I	TIME	AND MA	ERIAL VEI	RIFICATION
Vasyl Turetskyy st	_		6			+	DO	OWNES	CONSTRI	ICTION
LABORER OT									IPANY, LL	
Konstantine Uzten enkost			6			H	D.	0	- C	HObasshir
Laborer or									ction Company, e and materials	utilized for the
\$1° OT						+	100.00000			s ventication of
ОТ									W	e subcontractor
ST						\perp	10.00		vith the contrac	
OT OT						+			work is beyon uments a chan	
Description of Work:									er approval by the	
Phase 4									ct and/or Engine	
- RADIATUR DI	EM	0	, C	u	T	4	BV	ROP	ONLY	(E)
									8/2024	
						L	DATE	=:	010001	
+ Refer to So	spes		3	Pha	se	21	3 +	the 6		
MEP Trades do	Lo	+	den	10						
<u>-</u> .										
									Sub Total	
Signature of Customer or Foreman	2	1	7		5			Other	see attached	
rint Name	<u>E</u> 1111	12		For	ta	in-	<	:1	Total	
Date	111	3/6	2020	1						

ķ

Date



Customer			J	ob Na	ame			Date	Jol	Number
KMS - DOWNES	K	H 5						1-17-24	F 3100	786
•	33	H 5	14	AI	H	51.		**	CUT/DR	
Job Address	s: <i>D,</i>	4NI	EL	50	N	0	T		Report #	17-A
Labor										
Employee Name	М	Т	W	Т	F	S	S	Total Units	Rate	Extension
Oscar Hernandez	sr		1							
	ОТ									
Foreman	OT		,							
Gerson Madlado	ST		6							
Latina	TO	-			-	77-15	A C* A	NID MARTI	DIAL VEDI	CICATION
	TC ST		6			137	T.F	IND MAIL	RIAL VERI	FIGATION
	OT		O			-	00	MAILC	ONSTRU	CTION
1 /	от						UU			
	ST							COM	PANY, LLC	
	от									O b - s - b - s
	тс						DOWN	es Construct	on Company, L	LG nereby
	ST					Ve	nties	that the time	and materials u	unzed for the
()T					de	cnbe	d work was f	erformed. This	vernication of
Description of Work:)T					Wo	rk pei	nomed does	not relieve the	subcontractor
						١	rom (complying wi	th the contract o	locuments.
Phase 5 upp	アル					U	pon r	eview, it the	work is beyond	ine scope of
0.0									ments a change	
- Demo Air	\square	uci	5	(=		10	R De		approval by the	
166								Architect	and/or Enginee	<u> </u>
766			_			+		-	-6	
									-	
						D	ATE:		18/2014	
						L			3,7944	
-										
1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1									Sub Total	
		_	المناز الما	4	2					
Signature of Customer or Foreman	8	-)			Other	see attached	
Print Name	E	ic	t	31	tai	e			Total	13 HRS
	111	8/	``	τ.(1	TOTAL
Date	1//	0/	d 02	Y						-

Date





Customer				Jo	ob Na	me			Date	Job Number			
KMS - DOWNES		K,II; 739	ngl	ly M	lenos	1915	Cher	,/	1-31-24	# 310078	6		
		739	M	MIK	1 5	T							
Job Ad	dress:	DAN	T-E	1-50	W	CT.				Report # 131-A			
Labor													
Employee Name		М	Т	W	Т	F	S	S	Total Units	Rate	Extension		
Elliott JONES	ST	141	6	2	1		- 5	5	Total Othis	Tuto	Dittolision		
20001 4013	ОТ		0				Γ	-					
FOREMAN	ОТ						TI	ME/	TAM CAN	RIAL VERI	FICATION		
Gerson MACHADO	ST		6										
	от							DO	WNES C	ONSTRU	CTION		
LABORER	OT								COM	PANY, LLC			
Angel Vera	ST		6				-						
LABORER	ОТ							nwo	es Constructi	on Company, L	C hereby		
LABORER	OT						- 40	nlias	hat the time	and materials u	filized for the		
	ST	\rightarrow					doa	cnbe	d work was p	erformed This	venfication of		
	OT	-	_		-		WO	k per	ormed does	not relieve the s	ubcontractor		
	OT ST	-+						rom c	omplying wit	n the contract d	ocuments.		
	от	+	_				U	on re	view, if the w	ork is beyond th	ne scope of		
	OT							the co	ontract docum	nents a change	order will		
Description of Work:	OII.							be	issued after a	pproval by the	Owner.		
Phase 4 Tuni	nels								Architect a	and/or Engineer	!		
- MEP DEMO	0	F	5	T	EAI	y	AV	TP.	ES.	60			
									,				
						-	-DA	TE:		1000			
vert	_	TV	W	0		SUC	71	7					
70111	1	-	7										
	18	F											
										- Sub Total			
	(-				_	_		OUO IVIAI			
Signature of Customer or Foreman	/				5				Other	see attached			
-0									Other	VCC NITACIIGO			
Pulmi Nome	<	Er:		F	7	Med	0			.			
Print Name	(1	-	1	U	V				Total			






		,		J	ob Na	nie			Date	.fol	Number	
DOWNES CONSTRUCTION		ron	أليود	New	psc/9/	5ok.	w/		226-24	#3/00 76	3:6	
		33	7 14	P.'31	57.	,			-	MEP DI	ंभ ठ	•~
Job Addı	ess:	DA	456	£L.s	ON	4	ġ;			Report #	226-8	
Lahor								ME	AND MAT	ERIAL VER	IFICATION	1
Employee Name		M	Ť	W	TT	F	S	Trec	MARLIET CO.	LONDON		1
OSOAL Hernandez	ST	T					-	LIV.	AAJAEGA	ONSTRU	C. Heatheron	+
-	or						-	-	- CONTRACTOR	PANY, LL		ł
Foreman Francisco Astimbas	07							Down	ac Cancia	Tan Carrent		7
trancised Astimbas	- 8	8					V	Hine	that the time	on Company, I	LC hereby-	t
Laboren	or		-				do	conh	Anak maa	and materials (ulized for the	t
Tosc Horucho	DT.						We	de no	formed does	erformed. This	ventication of	t
hase harveno		8						from	minica nos	not relieve the	subcontractor	T
Laboren	or						-	TVIII 1	Southwhile M	h the contract o	ocuments	ı
	OT Sr	-	-	-				than	onimet den	vork is beyond t	ne scope of	
	or		-				_	ha	teened offer	ments a change	order will	L
	.07	1000						- 40	Architoct	approval by the and/or Enginee	Owner,	L
	51		-		1			-	AUGMECT	and/or Enginee	d	H
	OT						1100		7	(F)		١.
	_OT					1	-8	1		= 19		-
Description of Work:									71/-			
MEP DEMO	2.					- 1	D/	YTE!	<u>~10</u>	8/2024		
						- ا شده د د د د		- Particular		-		-
and and an											وتسمر	
· DENO RAOI	47	OR.	٤	AN	P	HA	#G	ER	S 🕮	Phase	5	
· DEHO RAOI,										Phase		
* DEHO RAOI. RM5.2004, 20										Phase		
										Phase		
RM5.200A, 20										Phase	3	
RM5.200A, 20										Phase	3	- tu
* Cu+,	72	12	64	_ 3						Phase	3	-
* Cu+,	72	12	64	_ 3						Pha se	5	e ha
RM5. 200A, 20	72	12	64	_ 3						Pha se	3	-
* Cu+,	72	12	64	_ 3						Pha se		-
* Cu+,	72	12	64	_ 3						Pha se		
* Cu+,	7,2	, 2 Can	Hrai	/ 3 /-	204	A.				Pha se		
* Cu+, Not in	7,2	, 2 Can	Hrai	/ 3 /-	204	A.						
* Cut, Not in	7,2	, 2 Can	Hrai	/ 3 /-	204	A.						
RMS. 200A, 20	7,2	, 2 Can	Hrai	/ 3 /-	204	A.				Sub Total		
* Cu+, Not in	7,2	, 2 Can	Hrai	/ 3 /-		A.				Sub Total		



Customer	Job Name	Date	Job Number	
OCIUNES CONSTRUCTION	Killingly Memorial School 3.39 HAIH ST.	2-79-20	#3100786 MEP DEHO DAY	
.lob Address:	DANTELSON CT		, .	.
	LETHIFFE SOCI		DATE: STAD	ES
Labor		Ь.	GOG IFIE STAD	2
Employee Name		3 3 Torrit Umrs	Rate Extension	
Oscar Hermandor SI	2		(C)	
Foreman or		Tiporuffy:	Architect and/or	
			svorgge reffis beusal ad	H
Francisco Astmbay ST			s anomico bistinos ed	\vdash
LABORER OF			Upon review, it the work is	\vdash
Jose norocho 51	5	THE RESERVE THE PERSON NAMED IN COLUMN TWO IS NOT THE OWNER, THE PERSON NAMED IN COLUMN TWO IS NOT THE OWNER,	ро эц цим Вијујиро тол	
O.T.		The state of the s	work performed does not reli	
LABORER OF			described work was performe	
ST			em bas emil ert tert zeimev	
OT			Downes Construction Con	
OT .		1 1011		
ST		1 777	COMPANY	_
OT OT	 		DOMNES CONS	_
Description of Work: MEP DEMO DEMO RA	RADIATORS IN			
	EAK Pipes Tha			
* Tunnel JA	Removals o	cut, dup		
	v v v v v v v v v v v v v v v v v v v		Sub Total	
gnature of Eustomer or Foreman	5			
Burners of Opposition of Lottenant.	<u> </u>	Other	see attached	_
rint Name —	Eric Fortaine 3/7/2004	-	Total .	
ale	3/7/anay			

Date



Customer		Job Na	me			Date	Job Number			
DOWNES CONSTRUCTION	Killingly Memored School 339 NATH ST.					2.28-24	28-24 # 3100786			
Yu.5. 4 3.5			-				MET DA	540 		
Job Address:	VANL	P450H	<u>ر</u>		-		Report.#	228-2		
Labor			į	That	EA	ND MATE	RIAL VERIF	ICATION		
Employee Name	M T	WT	F	TS_	\$	Total Units	Kafé	Extension		
OGGAR Hernander st				L	OA		NSTRUC	TION		
Foreman or						COMP	ANY, LLC			
Francisco Astinbay si		2	-	- De		Canalaudia	Comment	A haraba		
or		LAG		vonf	oe th	of the time or	Company, LL0 d materials utili	nereny		
Laborer or							formed. This ve			
Franklin Guallo ST		2		work	nerfo	med does no	at relieve the su	hoontractor		
Laborer							he contract doc			
Liquorus ori			-				k is beyond the			
OT			-1	1	e cor	tract docume	nts a change or	der will		
OT					be is	sued after ap	proval by the O	wner.		
ST						Architect an	d/or Engineerl			
от										
Description of Work:		لـــاــا	+	BY		- E8				
			1			٠١ د	10			
MEP DEMO			\dashv	DAT			12004			
- DEMO HAN	IGER	SA	NO		57	EAM	Pipes			
- DEMO HAN	TUN	nels					1	77		
1.			<u>-</u> -	-				~		
D. O. da D.	1./	/ (S.		-		/ 1 -	0		
A Dup to the	70/	CU	Γ	124	10	man	ugeable	PI RE		

		,,								
							Sub Total			
			-			6101114000				
Signature of Customer or Foreman		***************************************	_			Other	see attached			
		Fort								
rint Name	Sic	Fort	≀- 1-∧	<u></u>			Total			
`	0	5	********	•		L	TOTAL .			





Downes Construction Company 200 Stanley St New Britain, Connecticut 06051 Phone: (860) 229-3755

Project: 25-01-0447 - Killingly Memorial School Killingly, Connecticut

Prime Contract Potential Change Order #324: CE #324 - CMU Wall Infill at H

TO:	Town of Killingly 172 Main Street Killingly, Connecticut 06239	FROM:	Downes Construction Company 200 Stanley St New Britain, Connecticut 06051
PCO NUMBER/REVISION:	324 / 0	CONTRACT:	25-01-0447 - Killingly Memorial School
REQUEST RECEIVED FROM	1-950-6606-660-960-960-960-self-on-desider - draw - unfolk-reprosplassed uses a a.	CREATED BY:	Douglas Triba (Downes Construction Company)
STATUS:	Pending - In Review	CREATED DATE:	4/1/2024
REFERENCE:		PRIME CONTRACT CHANGE ORDER:	None
FIELD CHANGE:	No		
LOCATION:		ACCOUNTING METHOD:	Amount Based
SCHEDULE IMPACT:	THE CONTRACTOR THE CONTRACTOR CONTRACTOR	PAID IN FULL:	No
EXECUTED:	No	SIGNED CHANGE ORDER RECEIVED DATE:	
	Assemblikan purum ny silikh ni digina di sang di nyang kang di nyang di nya	TOTAL AMOUNT:	\$0.00

POTENTIAL CHANGE ORDER TITLE: CE #324 - CMU Wall Infill at H

CHANGE REASON: Backcharge

POTENTIAL CHANGE ORDER DESCRIPTION: (The Contract is Changed As Follows)

CE #324 - CMU Wall Infill at HVAC Duct Opening

Back charge between mason and mechanical contractors.

Labor and materials to patch CMU wall where a HVAC duct opening was laid out in the incorrect location.

ATTACHMENTS:

#	Budget Code	Description	Amount
1	001.04-100.S Construction.MASONRY.Subcontractor	Masonry	\$780.00
2	001.23-100.S Construction.HVAC.Subcontractor	HVAC	\$(780.00)
		Grand Total:	\$0.00

Antinozzi Associates
Town of Killingly
Downes Construction Company
271 Fairfield Ave.
172 Main Street
200 Stanley St
Bridgeport, Connecticut 06604
Killingly, Connecticut 06239
New Britain, Connecticut 06051

-DocuSigned by:

David Ferris 4/8/2024

SIGNATURE DATE SIGNATURE

DATE

Douglas Triba

DocuSigned by:

4/8/2024

F6D69D7786E64F1...
SIGNATURE

DATE

Killingly Memorial School Change Order Proposal # 9

To:

Downes Construction Co.

From:

Dexter Masonry 10/13/2023

Ref:

Patching & Relocate Duct Opening

Date: CM Number:

JOB # 069-0069 RNV

Trade Contractor COP Number:

Masonry CO #9 AWA 254

Description:

Patching & relocate duct opening 2nd fl top of new stairway, setup scaffolding x 2, cut old opening, demo, patch,

Quantity	Unit	Description of Material and Equipment	Unit Cost	Total
				\$ -
4	Ea.	8" CMU	\$ 2.65	\$ 10.60
1	Bags	Mortar	\$ 9.85	\$ 9.85
				\$ -
1		Hammer Drill	\$ 66.00	\$ 66.00
1		Mortar Mixer	\$ 135.00	\$ 135.00
				\$
				\$ -
				\$
ine 1			Material and Equipment Total	\$ 221.45

Crew	Labor Classification	Hours	Ва	se Rate	F	ICA & Med Care	JTA & UTA	G/	L, W/C Ins	В	enefits	То	tal Rate	Total
1	Mason Foreman	3.00	\$	45.63	\$	3.49	 3.51	\$	4.58	\$	36.42	\$	93.63	\$ 280.89
												\$		\$
												\$		\$
1	Laborer	3.00	\$	34.00	\$	2.60	\$ 2.62	\$	3.41	\$	26.19	\$	68.82	\$ 206.46
												\$	-	\$ -
												\$	-	\$
												\$	-	\$
												\$	-	\$
												\$		\$
												\$	-	\$ -
ne 2		*										Lab	or Total	\$ 487.35

Subcontractor Cost (Attach Proposals)								
Trade	Name of Subcontractor	Total						
ine 3	Subcontractor Total	\$ -						

Line 4	Total Labor, Material, and Equipment	1 8	709 90

Contractor Overhead and Profit	Allow % Amount	Tot	tal
Net Value of Self Performed Work (Amount = Lines 1	10% \$ 708.80	\$	70.88
Net Value of Subcontract Work (Amount = Line 3)	5% \$ -	\$	
Line 5	Contractor Overhead and Profit Total	\$	70.88

_		
Line 6	Total Proposed Change Order Amount (Lines 4+5)	\$ 780

Bruce W. Depter 11

Downes Construction Co.

Dexter Masonry

ŧ				Dexter earney Road,		.C				2
	· · · · · · · · · · · · · · · · · · ·			(860	0) 428-9909			ling ly Memoeia	13/	23
stomer h	lame Downes Co	anstru	ction		Job N	ame	Koll	ingly Mampia	1 Sal	ad
one Num	ber			Platte ment const.	Job N	umbe	200	7-01-0447		301
scription	l blad deletion and the selection and the side of the last deletion are deleted to be the selection as deletions as because as because as the selection as the						o C	7-01-0947		
atch es 4	ing and Reloca o scaffolding	4.0	s, Cut o		(1)			top of New 3 Iano again to		
	* Backcharge	40 1	PAD / KI	eeburu	7 In	tot/s	ect L	Location: 1st Time Top of Alew St Olass Room 2	70	oe K
Sentitude personal section of the se	LABOR	Torrersayeess	41.1					Location:	W	42
FIG MEN	CLASSIFICATION	STRAITLE					100	10p of Allew Ol	anur	ag in
7	Mason Foreman	3104001		Partine :	SEMIDA	10,724	uns.	Class Room L'	Ploo	ž
	Mason	1	F(R)	f		-				
	Mason Apprentice					_		1		
-	Labor Foreman		1							
7	Laborer	0	1				TIME	AND MATERIAL V	ERIFIC	OITA
	Lull Driver	7	XEP-			-		100 100 100 100 100 100 100 100 100 100		
	Truck Driver							WNES CONSTI	DILCT	ION
	, mook offer		-		1			·		IOIA_
irenen saetumba	MATERIAL	4						EGGMRANY, I	LU	
	Brick		each	:	019				HRS.	TOT. 9
	Anchor Clips (w/ screws	and (le)	each			Lul	(Incl. free)	vnes Construction Compa	nv LLC	nereby
	Insulation		sq. ft.			Ger	ie Lift (i	nci lively the time and mater	ale utiliza	of for th
_/	Mortar	baa	batch			Sci	SOF	s that the time and mater	TL:	Cation at
	CMU (4")	- /	each			Pro	Danesch	ped work was performed.	mis veni	nçauon
-1-	CMU (6")		each			Pall	HWOOK!	performed does not relieve	the subc	xontract
4	CMU (8")		each			Truc	k from	m complying with the cont	ract docu	ments.
	CMU (10")		each	5		Prin	ie Move	review if the work is held	and the s	cope of
	CMU (12")		each	9		Bug	gy/Bloc	review, if the work is bey carring Packer configet documents a ch	ance on	or will
	CMU Specials (GF SF	BN)	each		ļ,	Dun	pstery	Flaulingur ubuuments a u	ango ora	OI WIN
	Grout		batch					be issued after approval b		nei,
	Rebar	· II um\	If.					(Incl. to Architect and/or En	gineer!	-
	Joint Reinforcement (V Corner Wire	vire)	[[.		- 1		mer Du	ill (w/ chisel or bit)		ļ
	Hit Pins (incl. shots & wast		pieces			Saw		// Blade E'F		
	Epoxy	(ers)	each tube		(es/No			// Blade & F		-
~	Precast		each		(es)/No					
	Field Stone		sq. ft.			DIZU	e (Sìze) DAT	E: 10/16/20	25	-
	Cut Stone		sq. ft./ea.							
	Flashing w/ weeps		sq. ft.	Ī				SCAFFOLDING		
A STATE OF THE STA	Termination Bar w/ pine	s	If.		OTV.	Part of		TEM		· UNIT
	Stainless Steel Drip Ed		II.		86	Fran	re Scaffe	olding (excludes labor)	and the state of t	sq. ft
	Karnak 920 / Mastic		5 gal. can			1772				_ oq
				ſ			V	VINTER PROTECTION		
					OTY)			OTENIA	7 (**):	UNITS
1				Ī		Poly		San and San		rolls
						Pot I	leaters i	Hawk Heaters		each
QTY.	OTHER ITEMS	THE RESERVE	, UNITS			Sala	manders	3		each
į						Prop	ane			100 lb, tai
	herefore and an artist of the second					Wind	Clips	And Andrew Control	20 11 22	each
	And the second s					Plyw	ood			each
						2x4	.cdmill			each
there S	ubcontractor work relate	d to this AV	VA?	Yes / No 3	Sub Name:			TOP TOWN AND AN APP		
are au	thorized to perform this	additional v	vork, which I	3W Dexter v	vill be como	ensat	ed for			
	6/2023 Authorizing Sig				S COMP	-		Name Eric Fort	1	
	ビノ いしとつ Authorizing Sid	mature (Custo	mer!	-			Print t	same Cric Just	11ne	

TOWN OF KILLINGLY WATER POLLUTION CONTROL AUTHORITY

Regular In Person Meeting and Public Hearing Agenda

Wednesday, April 17, 2024 at 5:00 PM

Water Pollution Control Facility 31 Wauregan Road, Killingly CT

PUBLIC HEARING ON SEWER RATE INCREASE ITEM #8d WILL START PROMPTLY AT 5:00 PM

REGULAR MEETING TO START IMMEDIATELY FOLLOWING THE PUBLIC HEARING

- 1. Roll Call
- 2. Citizen Participation (on items not subject to public hearing)
- 3. Town Council Liaison Participation
- 4. Adoption of the Regular Meeting Minutes March 20, 2024
- 5. Finance Report
 - a. Monthly Finance Report
- 6. Report of Plant Superintendent
- 7. Frito-Lay Representation
- 8. Unfinished Business
 - a. North River Lane to Maple Street Sewer Line
 - b. Reynolds Street Improvement Project
 - c. I & I
 - d. Sewer Rate Increase Public hearing (See Attached)
- 9. New Business
- 10.Correspondence
- 11.Other
- 12. Adjournment



Quote # 56771

03 / 26 / 2024

Mary Bromm Town of Killingly 172 Main Street Killingly, CT 06239

Dear Mary,

Thank you for the opportunity to submit a proposal for your upcoming project. Here at Meyer, it is our mission to provide you with an unmatched experience. We are committed to bringing our knowledge and expertise to the project outlined below.

Mary Bromm Via e-mail: mbromm@killinglyct.gov
Town of Killingly State Project: 069-0069 RNV Killingly Memorial School Construction Phase 6 Moves
172 Main Street State of Connecticut Contract: 14PSX0161
Killingly, CT 06239 Due Date and Time: Wednesday March 27, 2024

The estimated cost to complete this project is \$4,836.25.

Please sign the attached quote so we may schedule your work. The project will be subject to the attached Standard Terms.

Should you have any questions concerning this proposal please contact: (860)982-0152 Mobile

isiness Development 2 Mobile lliambmeyer.com

Statement of Work and Pricing for Services

The spaces that will be relocated prior to Construction Phase 6 are floor with half level transitions. Spaces within the addition are accessed via internal accessible ramps. A new elevator located at the south end of the addition WILL NOT be made available to Meyer, Inc. Existing wheelchair lifts at half-level stair transitions in the existing school WILL NOT be made available to Meyer, Inc.

Work performed portal to portal during normal work hours Monday to Friday 8:00 a.m. to 5:00 p.m. April 15 or 16, 2024 Pricing below is based on State of Connecticut contract 14PSX0161.

Final invoicing will only be based on actual time and materials used.

All work-tickets have a four hour minimum.

Any un-used boxes may be returned for full credit.

Moving Services

Labor	Rate	QTY	Hours	Subtotal
PROJECT MANAGER	\$70.00	1	9	\$630.00
STRAIGHT TRUCK & DRIVER	\$89.00	2	9	\$1,602.00
INSTALLER	\$58.00	1	9	\$522.00
MOVER	\$43.00	4	9	\$1,548.00

Subtotal \$4,302.00

Material	Rate	QTY	Subtotal
COMMERCIAL BIN 48 X 24 X 28	\$23.00	12	\$276.00
COMMERCIAL MOVING LABELS ROLL 250	\$9.00	6	\$54.00
STRETCHWRAP 16" X 1500' 63G	\$27.00	1	\$27.00
RAM BOARD FLOOR PROTECTION 38" X 100'	\$117.25	1	\$117.25
BUBBLEWRAP-1/2" 24"X 250' PERF @ 12"	\$60.00		\$60.00

Subtotal **\$534.25**

Equipment Equipment	Subtotal
DOLLIES, HAND-TRUCKS, PANEL CARTS, PADS, LOGISTIC STRAPS, TOOLS @ NO CHARGE	\$0.00

Subtotal \$0.00

Grand Total: \$4,836.25

Payment terms and credit limits are subject to credit approval.

Acceptance - Signature Required For William B. Meyer, Inc. to Perform Services

Signature acknowledges acceptance of this Statement of Work and the attached Standard Terms. A signature transmitted by facsimile or electronic mail in pdf or other electronic format, shall be deemed an original signature for the purpose of this Agreement.

ent's Name	Title	Town of Killingly Company Name	 >
Man Willes	3-27-24 Date		
		MARKA JAN. 4	
		· ·	
		LI DOMEN CONTRACTOR CO	

Standard Terms

The following Standard Terms cover the services as set forth in the above proposal and any future services that William B. Meyer may perform on the customer's (the "Customer") behalf, including but not limited to the loading, transportation, unloading and storage of those items, goods or property ("Property") identified by the Customer.

Section 1: The Services

- 1. The services (the "Services") performed by William B. Meyer, Inc. ("WBM") will be performed according to the specifications agreed to by the parties ("Specifications") and in accordance with standard industry practices.
- 2. Any alterations or deviations from Specifications, including but not limited to extra labor, equipment, or additional time, will be agreed to by both parties in writing and may result in an adjustment to pricing and/or additional charges. Any such additional fees or charges will be due and payable in accordance with the terms hereof.
- 3. At the time of the move, if the Customer requests any additional Services to be performed, charges for such Services will be assessed at WBM's applicable rate schedule in effect at the time.
- 4. The Customer shall ensure the following conditions are met by Customer at both origin(s) and destination(s) for the entire duration of the Services:
 - a. There must be adequate light, heat, air and power.
 - b. WBM must have the exclusive and uninterrupted use of the primary freight elevator.
 - c. Adequate loading and unloading areas must be made available and free of trash, construction equipment, other non-related furniture or other items/materials that would obstruct loading or unloading.
 - d. Construction, renovation, or decorating work must not be in such a state as to impede the move. This includes, but is not limited to carpet laying, tiling, painting, and carpentry work, etc.
 - e. Entrance and exit points to be used for loading and unloading, as agreed upon prior to execution of the contract, must be available.
- 5. All Property shall be placed once at the destination(s) as directed by the Customer or in accordance with the floor plans.
- 6. The Customer or their designate will be present at origin and destination during the actual move. Such personnel shall be authorized to make changes, should changes be necessary, during the actual move.

Section 2: Term and Termination

- 1. This Agreement shall commence on the date signed by both parties, and shall terminate when the Services are completed, as determined by WBM.
- 2. In the event of termination of this Agreement by the Customer for any reason, the full amount due hereunder shall be paid to WBM, unless the parties have mutually agreed otherwise in writing.
 - 3. Any changes to the Services must be agreed to by the parties at least 24 hours prior to the move. Should a crew be dispatched due to the lack of notice by the Customer, the Customer will be charged all Fees set forth herein.

Section 3: Fees and Payment Terms

- 1. The fees and/or charges for the Services (collectively the "Fees") are set forth above, or on a separate statement of work ("SOW") agreed to by the parties. The Fees are exclusive of taxes which will be itemized on the applicable invoice.
- 2. The Fees set forth on the cover page or any applicable SOW only apply to the quantities and/or Services stated. WBM shall invoice for additional billings as set forth above, and for delays that are not caused by WBM.
- 3. All Fees shall be paid upon receipt of invoice, unless otherwise agreed by the parties. Accounts outstanding for more than 30 days will bear interest at the rate of 1 ½ percent per month (18% APR) on the unpaid balance. The Customer agrees to pay all costs and expenses of collection, including attorneys' fees.

Section 4: Insurance and Liability and Property Valuation

a. Storage Services

- 1. WBM carries liability insurance coverage for all Property stored by WBM, provided the damage occurred while the Property was under WBM's complete and total control. As a bailee, WBM exercises that degree of care which a reasonable careful person would exercise in regard to similar goods of his own. Accordingly, we assume no liability whatsoever for the loss or destruction or any damage to goods or property occasioned by fire, theft, water, leakage, shrinkage, breakage, ratage, vermin, heat, cold, frost, chance of weather, or from inherent qualities of the goods from strikes, work stoppages, riot, civil commotion, accident, acts of God, or any other cause whatsoever, unless due to WBM's negligence. WBM assumes no liability for any concealed item, unless caused and accompanied by external damage caused by WBM.
- 2. Claims for damage occurring to stored Property will not be valid unless:
 - a. Noted in writing on the delivery ticket at time of delivery out of storage.
 - b. Payment in full for the Services has been made by the Customer according to the terms of the proposal.
- 3. WBM reserves the right of first refusal to make all repairs to damaged Property.
- 4. WBM shall have a general warehouseman's lien, as set forth in the Uniform Commercial Code as adopted by the Connecticut General Statutes, upon any and all stored Property for Fees or other amounts not paid hereunder by the Customer.

b. Transit Services

- 1. WBM carries liability insurance coverage for all Property handled by us while performing a move and while under our complete and total control. WBM assumes no liability for articles packed or unpacked by anyone other than WBM. WBM assumes no liability for any concealed item, unless caused and accompanied by external damage caused by WBM. Property of value (i.e. electronic equipment, artwork, high-value furniture, etc.) exceeding \$1,000 per piece must be declared prior to being moved or it liability therefore is disclaimed.
- 2. Claims will not be valid unless:
 - a. Presented in writing within five (5) working days after completion of the Services.
 - b. Payment in full for the Services has been made by the Customer according to the terms of the proposal.
- 3. WBM reserves the right of first refusal to make all repairs for any damage that may occur in connection with the performance of Services.

C. LIMITATIONS OF LIABILITY. WBM'S LIABILITY IS LIMITED TO THE SUM OF \$.60 PER POUND PER ITEM ("PROPERTY VALUATION"). EXCEPT AS EXPRESSLY CONTAINED HEREIN TO THE FULLEST EXTENT PERMITTED BY LAW, WBM MAKES NO REPRESENTATIONS OR WARRANTIES REGARDING THE SERVICES. WBM DOES NOT WARRANT THAT THE SERVICES WILL BE ERROR FREE. WBM EXPRESSLY DISCLAIMS ALL WARRANTIES, EXPRESS OR IMPLIED, INCLUDING THE WARRANTIES OF MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. TO THE MAXIMUM EXTENT PERMITTED BY APPLICABLE LAW, IN NO EVENT WILL EITHER PARTY, BE LIABLE FOR ANY INCIDENTAL, INDIRECT, SPECIAL, EXEMPLARY OR CONSEQUENTIAL DAMAGES WHATSOEVER ARISING OUT OF OR RELATING TO THIS AGREEMENT OR ANY SERVICES PERFORMED BY WBM. TO THE EXTENT ALLOWED BY APPLICABLE LAW, WBM'S MAXIMUM CUMULATIVE LIABILITY IN CONNECTION WITH ANY SERVICES PERFORMED BY WBM AND THE EXCLUSIVE REMEDY FOR ANY CLAIMS ARISING OUT OF OR RELATED TO THIS AGREEMENT WILL BE LIMITED TO THE PROPERTY VALUATION. CLIENT SHALL CAUSE ITS INSURERS OF PROPERTY TO WAIVE ANY RIGHT OF SUBROGATION AGAINST WBM.

Section 5: Miscellaneous: This Agreement constitutes the complete and exclusive statement of the agreement between the parties concerning the subject matter hereof and supersedes terms and conditions found in any other documents including click-wrap agreements or POs. The terms of any provision required to give effect thereto shall survive the expiration or termination of this Agreement. A wavier by either party of any breach of this Agreement shall not be considered a waiver of any subsequent or other breach. Customer may not assign this Agreement. This Agreement shall be governed by the laws of the State of Connecticut and jurisdiction shall be exclusively in the courts of the State of Connecticut.

AGENDA ITEM COVER SHEET

ITEM 4(b):

WESTFIELD AVENUE/COMMUNITY CENTER RENOVATION PROJECT

PREPARED BY:

Mary Bromm, CD Administrator

ARCHITECT/ENGINEER:

Antinozzi Associates

CONSTRUCTION MANAGER:

Downes Construction

ITEM SUMMARY:

Downes will review the GMP Amendment #2 for Commission approval. Alternates will be reviewed at a site walk prior to your May 1, 2024 meeting and discussed during the regular meeting.

Antinozzi will review the environmental testing proposal from Pennoni. No work at Westfield can begin until the environmental consultant applies to the State for approval, which may take several weeks.

ACTION REQUESTED AT THE APRIL 16, 2024 MEETING:

Review and if appropriate, approve the GMP, Amendment #2.

Review and if appropriate, approve the Pennoni proposal for Environmental Testing – this is an amendment to the Antinozzi Contract.

SUPPORTING DOCUMENTS:

- GMP Amendment #2
- Pennoni Proposal

Guaranteed Maximum Price Amendment

AMENDMENT NO. 2 - Interiors Renovation Package

This Amendment dated the 12TH day of APRIL in the year TWO THOUSAND AND TWENTY FOUR, is incorporated into the accompanying AIA Document A133TM—2019, Standard Form of Agreement Between Owner and Construction Manager as Constructor where the basis of payment is the Cost of the Work Plus a Fee with a Guaranteed Maximum Price dated the 12th day of APRIL in the year TWO THOUSAND TWENTY FOUR (the "Agreement") (In words, indicate day, month, and year.)

for the following **PROJECT**: (Name and address or location)

KILLINGLY COMMUNITY CENTER WESTFIELD AVENUE RENOVATION 79 WESTFIELD AVENUE KILLINGLY, CT 06239

THE OWNER:

(Name, legal status, and address)

TOWN OF KILLINGLY 172 MAIN STREET KILLINGLY, CT 06239

THE CONSTRUCTION MANAGER:

(Name, legal status, and address)

DOWNES CONSTRUCTION COMPANY, LLC 200 STANLEY STREET NEW BRITAIN, CT 06051

TABLE OF ARTICLES

- A.1 GUARANTEED MAXIMUM PRICE
- A.2 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION
- A.3 INFORMATION UPON WHICH AMENDMENT IS BASED
- A.4 CONSTRUCTION MANAGER'S CONSULTANTS, CONTRACTORS, DESIGN PROFESSIONALS, AND SUPPLIERS

ARTICLE A.1 GUARANTEED MAXIMUM PRICE

§ A.1.1 Guaranteed Maximum Price

Pursuant to Section 3.2.6 of the Agreement, the Owner and Construction Manager hereby amend the Agreement to establish a Guaranteed Maximum Price. As agreed by the Owner and Construction Manager, the Guaranteed Maximum Price is an amount that the Contract

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An Additions and Deletions Report that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

AlA Document A201™–2017, General Conditions of the Contract for Construction, is adopted in this document by reference. Do not use with other general conditions unless this document is modified. Sum shall not exceed. The Contract Sum consists of the Construction Manager's Fee plus the Cost of the Work, as that term is defined in Article 6 of the Agreement.

- § A.1.1.1 The Contract Sum is guaranteed by the Construction Manager not to exceed NINETEEN MILLION ONE HUNDRED FOURTEEN THOUSAND SEVEN HUNDRED TWENTY ONE DOLLARS AND NO CENTS (\$19,114,721.00), subject to additions and deductions by Change Order as provided in the Contract Documents.
- § A.1.1.2 Itemized Statement of the Guaranteed Maximum Price. Provided below is an itemized statement of the Guaranteed Maximum Price organized by trade categories, including allowances; the Construction Manager's contingency; alternates; the Construction Manager's Fee; and other items that comprise the Guaranteed Maximum Price as defined in Section 3.2.1 of the Agreement.

(Provide itemized statement below or reference an attachment.)

REFER TO EXHIBIT A1.1.2, ATTACHMENT #01GUARANTEED MAXIMUM PRICE

- § A.1.1.3 The Construction Manager's Fee is set forth in Section 6.1.2 of the Agreement.
- § A.1.1.4 The method of adjustment of the Construction Manager's Fee for changes in the Work is set forth in Section 6.1.3 of the Agreement.
- § A.1.1.5 Alternates
- § A.1.1.5.1 Alternates, if any, included in the Guaranteed Maximum Price:

Item Price

Refer To Exhibit A1.1.5, Attachment #02 Alternates

§ A.1.1.5.2 Subject to the conditions noted below, the following alternates may be accepted by the Owner following execution of this Exhibit A. Upon acceptance, the Owner shall issue a Modification to the Agreement. (Insert below each alternate and the conditions that must be met for the Owner to accept the alternate.)

Item Price Conditions for Acceptance

Refer To Exhibit A1.1.5, Attachment #02 Alternates

§ A.1.1.6 Unit prices, if any:

(Identify the item and state the unit price and quantity limitations, if any, to which the unit price will be applicable.)

ARTICLE A.2 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION

§ A.2.1 The date of commencement of the Work shall be:

(Check one of the following boxes.)

Init.

- [X] The date of execution of this Amendment.
- [] Established as follows:

 (Insert a date or a means to determine the date of commencement of the Work.)

If a date of commencement of the Work is not selected, then the date of commencement shall be the date of execution of this Amendment.

§ A.2.2 Unless otherwise provided, the Contract Time is the period of time, including authorized adjustments, allotted in the Contract Documents for Substantial Completion of the Work. The Contract Time shall be measured from the date of commencement of the Work.

§ A.2.3 Substantial Completion

§ A.2.3.1 Subject to adjustments of the Contract Time as provided in the Contract Documents, the Construction Manager shall achieve Substantial Completion of the entire Work:

(Check one of the following boxes and complete the necessary information.)

- Not later than () calendar days from the date of commencement of the Work.
- By the following date: SUBSTANTIAL COMPLETION IS PER SCHEDULE [X]

§ A.2.3.2 Subject to adjustments of the Contract Time as provided in the Contract Documents, if portions of the Work are to be completed prior to Substantial Completion of the entire Work, the Construction Manager shall achieve Substantial Completion of such portions by the following dates:

Portion of Work

Substantial Completion Date

See Attachment #3

§ A.2.3.3 If the Construction Manager fails to achieve Substantial Completion as provided in this Section A.2.3, liquidated damages, if any, shall be assessed as set forth in Section 6.1.6 of the Agreement.

INFORMATION UPON WHICH AMENDMENT IS BASED

§ A.3.1 The Guaranteed Maximum Price and Contract Time set forth in this Amendment are based on the Contract Documents and the following:

§ A.3.1.1 The following Supplementary and other Conditions of the Contract:

Document	Title	Date	Pages
Attachment #1	GMP Summary	4/08/24	1
Attachment #2	Alternates	4/08/24	3
Attachment #3	Schedule	4/08/24	7
Attachment #4	Specifications	4/08/24	3
Attachment #5	Drawing Log	4/08/24	4
Attachment #6	Allowances	4/08/24	1
Attachment #7	Assumptions & Clarifications	4/08/24	3

§ A.3.1.2 The following Specifications:

(Either list the Specifications here, or refer to an exhibit attached to this Amendment.)

Refer To Attachment #4, A.3.1.2 - Specifications

Title Section Date **Pages**

§ A.3.1.3 The following Drawings:

Init.

(Either list the Drawings here, or refer to an exhibit attached to this Amendment.)

Refer To Attachment #5, A.3.1.3 - Drawings

Title Number Date

(892429680)

§	A.3.1.4	The	Sustainabilit	y Plan,	if any:
---	---------	-----	---------------	---------	---------

(If the Owner identified a Sustainable Objective in the Owner's Criteria, identify the document or documents that comprise the Sustainability Plan by title, date and number of pages, and include other identifying information. The Sustainability Plan identifies and describes the Sustainable Objective; the targeted Sustainable Measures; implementation strategies selected to achieve the Sustainable Measures; the Owner's and Construction Manager's roles and responsibilities associated with achieving the Sustainable Measures; the specific details about design reviews, testing or metrics to verify achievement of each Sustainable Measure; and the Sustainability Documentation required for the Project, as those terms are defined in Exhibit C to the Agreement.)

Title

Date

Pages

Other identifying information:

§ A.3.1.5 Allowances, if any, included in the Guaranteed Maximum Price: (Identify each allowance.)

ltem

Price

Refer To Attachment #6, A.3.1.5 -Allowances

Refer To Attachment #06 for allowance summary breakdown

§ A.3.1.6 Assumptions and clarifications, if any, upon which the Guaranteed Maximum Price is based: (Identify each assumption and clarification.)

Refer To Attachment #7, A.3.1.6 – Assumptions & Clarifications

§ A.3.1.7 The Guaranteed Maximum Price is based upon the following other documents and information: (List any other documents or information here, or refer to an exhibit attached to this Amendment.)

N/A

ARTICLE A.4 CONSTRUCTION MANAGER'S CONSULTANTS, CONTRACTORS, DESIGN PROFESSIONALS, AND **SUPPLIERS**

§ A.4.1 The Construction Manager shall retain the consultants, contractors, design professionals, and suppliers, identified below:

(List name, discipline, address, and other information.)

N/A

This Amendment to the Agreement entered into as of the day and year first written above.

OWNER (Signature)	CONSTRUCTION MANAGER (Signature)
Mary Bromm	Frank J. Tomcak - Project Executive
(Printed name and title)	(Printed name and title)

A.1.1.2 - GUARANTEED MAXIMUM PRICE

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #01

04/08/24

Provided below is an itemized statement of the Guaranteed Maximum Price organized by trade categories, allowances, contingencies, alternates, the Construction Manager's Fee, and other items that comprise the Guaranteed Maximum Price.

				CIVIL		
NUMBER	DESCRIPTION	CONTRACTOR	CURRENT CONTRACT	This Amendment #1.0	Amendment #2.0	Total Value as of
			Dated 10/19/2021	Total w/Alternates		this Amendment (GMP)
01 00 00	PROJECT REQUIREMENTS	Downes		\$ 180,118	\$ 610,244	\$ 790,362
01 00 00	PROGRESS / FINAL CLEANING	Downes		· ·	\$ 265,793	\$ 265,793
01 00 00	PHASING / TEMP ENCLOSURES	Downes		₹\$	\$ 268,475	\$ 268,475
02 00 00	DEMOLITION & HAZMAT	Spectrum		\$ 819,000.00	\$ 833,874	\$ 1,652,874
04 20 00	MASONRY	Dexter		\$ 936,405.00		\$ 1,083,652
02 00 00	STRUCTURAL STEEL & MISC. METALS	Berlin Steel		45	\$ 45,462	\$ 45,462
06 10 00	GENERAL TRADES	Noble		\$	\$ 343,118	\$ 343,118
06 20 00	CARPENTRY	Downes		\$ 203,722	\$ 683,077	\$ 886,799
07 50 00	ROOFING SYSTEM	Silktown		\$ 2,642,790.00	•	\$ 2,642,790
08 80 00	GLASS & GLAZING	Accurate		\$ 1,522,080.00	\$ 7,600	\$ 1,529,680
00 06 80	DOORS, FRAMES, HARDWARE (FURNISH ONLY)	Tull Brothers			13	
09 20 00	DRYWALL & ACOUSTICAL CEILINGS	Conn Acoustics		43	\$ 856,306	\$ 856,306
00 30 00	TILE	R&B		*	\$ 129,000	\$ 129,000
00 09 60	FLOORING	Higgins		*	\$ 542,000	\$ 542,000
00 06 60	PAINTING	Mackenzie		\$ 72,500.00	S	\$ 72,500
00 06 60	PAINTING	Cross Cup		•	\$ 149,000	\$ 149,000
22 00 00	PLUMBING & HVAC SYSTEM	MJ Daly		\$	3,616,000	\$ 3,616,000
26 00 00	ELECTRICAL SYSTEM	Dicin			\$ 848,288	\$ 848,288
ALLOW	SITEWORK & CONCRETE	Downes		\$ 50,000	\$ 483,060	\$ 533,060
ALLOW	MEP REMOVE / RE-CONNECT / REPAIR EXISTING	Downes		\$ 30,000.00	♦	\$ 30,000
ALLOW	OFF-HOURS WORK / SUPERVISION	Downes		\$	\$ 25,000.00	\$ 25,000
ALLOW	TEMP ENCLOSURES	Downes		\$	\$ 25,000.00	\$ 25,000
ALLOW	MISC. CUT / PATCHING	Downes		\$	\$ 50,000.00	\$ 50,000
ALLOW	SUPPLEMENTAL STEEL / SUPPORTS	Downes		4	\$ 75,000.00	\$ 75,000
ALLOW	MISC. FIREPROOF PATCHING	Downes		· · · ·	\$ 25,000.00	\$ 25,000
ALLOW	TERRAZZO POLISHING / REPAIR	Downes		w.	\$ 150,000.00	\$ 150,000
ALLOW	TEMP ENVIRONMENTAL CONTROLS	Downes		\$	\$ 175,000.00	\$ 175,000
ALLOW	UTILITY FEES	Downes		•	\$ 20,000.00	\$ 20,000
	TRADE PACKAGE W/ALLOWANCES TOTAL			\$ 6,456,615	\$ 10,506,844	\$ 16,963,459
0.026%	STATE EDUCATION FEE			\$ 1,679	\$ 2,732	\$ 4,410.50
	BOILDING PERMIT PEE			ASSUME	ASSUME WAIVED	ASSUME WAIVED
	GENERAL CONDITIONS	Downes	φ.	\$ 422,779	\$ 602,375	\$ 1,025,153.75
0.75%	GENERAL INSURANCE	Downes		\$ 54,178	85,988	\$ 140,165.67
0.86%	CM P & P BONDS	Downes		\$ 60,335	\$ 98,819	\$ 159,154.42
0.00%	BUILDERS RISK	BY OWNER		BY OWNER	BY OWNER	BY OWNER
3.00%	CONTINGENCY - (CM USE)	Downes		\$ 209,868	341,389	\$ 551,256.29
T.15%	CIMIR FEE	Downes		\$ 82,863	\$ 133,839	\$ 216,701.39
	LOIMIP SUIM PRECONSTRUCTION SERVICES	Downes				\$ 54,420.00
		TOTALS:	\$ 54,420	\$ 7,288,316	\$ 11,771,985	\$ 19,114,721



A.1.1.5 - ALTERNATES

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #02 04/08/24



Alternate #3 - FRP Doors

NUMBER	DESCRIPTION	CONTRACTOR			
		l'		Alternate #3	
2.8.1	Glass & Glazing	Accurate	\$	154,660.00	
2.8.2	Doors, Frames, & Hardware	Tull Brothers	\$	48,950	
	TRADE PACKAGE TOTAL		\$	203,610	
0.026%	STATE EDUCATION FEE		\$	53	
	BUILDING PERMIT FEE		1	Waived	
	GENERAL CONDITIONS (Not including Bond & Insurance)		l		
0.75%	GENERAL INSURANCE		\$	1,592	
0.70%	CM P & P BONDS		\$	1,497	
0.00%	BUILDERS RISK		l	BY OWNER	
4%	CONTINGENCY - (CM Construction - GMP)		\$	7,321	
1.15%	CMR FEE		\$	2,462	
			\$		
		TOTALS:	\$	216,536	TBD

Alternate #10 - Abate Existing Tunnel Not Part of Base Bid

NUMBER	DESCRIPTION	CONTRACTOR			
	223.11 11011		Alternate #10		
2.2.1	Demo & HAZMAT	SPECTRUM		28,000.00	
2.22.1	Plumbing	MJ Daly		30,000.00	
2.23.1	HVAC	MJ Daly	\$	138,000	
	TRADE PACKAGE TOTAL		\$	196,000	
0.026%	STATE EDUCATION FEE		\$	51	
	BUILDING PERMIT FEE		l	Waived	
	GENERAL CONDITIONS (Not including Bond & Insurance)		l		
0.75%	GENERAL INSURANCE		\$	1,535	
0.70%	CM P & P BONDS		 \$	1,443	
0.00%	BUILDERS RISK			BY OWNER	
4%	CONTINGENCY - (CM Construction - GMP)		s	7,051	
1.15%	CMR FEE		s	2,370	
		TOTALS:	ė	208,451	TBD

Alternate #11 - Replace Existing Ceilings Not Part of Base Bid

NUMBER	DESCRIPTION	CONTRACTOR		
	DESCRIPTION		Alternate #11	
2.2.1	Demo & HAZMAT	SPECTRUM	11,500	
2.9.3	Acoustical Ceilings	Conn Acoustics	\$ 49,074	
	TRADE PACKAGE TOTAL		\$ 60,574	
0.026%	STATE EDUCATION FEE		\$ 16	
	BUILDING PERMIT FEE		Waived	
	GENERAL CONDITIONS (Not including Bond & Insurance)			
0.75%	GENERAL INSURANCE		\$ 519	
0.70%	CM P & P BONDS		\$ 488	
0.00%	BUILDERS RISK		BY OWNER	l
4%	CONTINGENCY - (CM Construction - GMP)		\$ 2,241	l
1.15%	CMR FEE		\$ 734	
			\$ -	
		TOTALS:	\$ 64,573	TBD

Alternate #12 - Mecho Shades In Lieu of Mini Blinds

NUMBER	DESCRIPTION	CONTRACTOR	Alternate #12	
2.6.1	General Trades	Noble	29,000.00	
	TRADE PACKAGE TOTAL		\$ 29,000	

A.1.1.5 - ALTERNATES

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE.

EXHIBIT A1 - GMP - ATTACHMENT #02

04/08/24



04/00/24						
0.026%	STATE EDUCATION FEE		 \$	8		- 1
1	BUILDING PERMIT FEE		l	Waived		- 1
1	GENERAL CONDITIONS (Not including Bond & Insurance)		l			- 1
0.75%	GENERAL INSURANCE		\$	218		- 1
0.70%	CM P & P BONDS		\$	205		- 1
0.00%	BUILDERS RISK		l	BY OWNER		- 1
4%	CONTINGENCY - (CM Construction - GMP)		\$	1,030		- 1
1.15%	CMR FEE		\$	350		- 1
			\$	-		
		TOTALS:	Ś	30,810	TBD	\neg

Alternate #13 - VRF Split Units At 1st Fl. East Conn West of Gym Corr.

NUMBER	DESCRIPTION	CONTRACTOR	Alternate #13	
2.2.1	Selectrive Demo & Abatement	Spectrum	4,000.00	
2.9.1	Gypsum Drywall	Conn Acoustics	1,800.00	
2.9.3	Acoustical Ceilings	Conn Acoustics	13,595.00	
2.22.1	Plumbing	MJ Daly	3,000.00	
2.23.1	HVAC	MJ Daly	100,000.00	
	TRADE PACKAGE TOTAL		\$ 122,395	
0.026%	STATE EDUCATION FEE		\$ 32	
	BUILDING PERMIT FEE		Waived	
	GENERAL CONDITIONS (Not including Bond & Insurance)			
0.75%	GENERAL INSURANCE		\$ 918	
0.70%	CM P & P BONDS		\$ 863	
0.00%	BUILDERS RISK		BY OWNER	
4%	CONTINGENCY - (CM Construction - GMP)		\$ 4,347	
1.15%	CMR FEE		\$ 1,478	
			\$ _	
		TOTALS:	\$ 130,034	TBD

Alternate #14 - Site Improvements At Comm Ctr Entrance

NUMBER	DESCRIPTION	CONTRACTOR			
				Alternate #7	
3.31.1	Sitework & Concrete	TBD		0.00	
	TRADE PACKAGE TOTAL		\$		
0.026%	STATE EDUCATION FEE		\$	-	
	BUILDING PERMIT FEE			Waived	
	GENERAL CONDITIONS (Not including Bond & Insurance)				
0.75%	GENERAL INSURANCE	ĺ (i	\$	-	
0.70%	CM P & P BONDS		\$	-	
0.00%	BUILDERS RISK			BY OWNER	
4%	CONTINGENCY - (CM Construction - GMP)		\$	-	
1.15%	CMR FEE		\$	**	
		TOTALS:	\$	-	TBD

Alternate #15 - Terrazzo Floor Refinishing

NUMBER	DESCRIPTION	CONTRACTOR	Alternate #8	
2.9.4	Flooring	Higgins	117,200.00	
	TRADE PACKAGE TOTAL		\$ 117,200	
0.026%	STATE EDUCATION FEE		\$ 30	
	BUILDING PERMIT FEE		Waived	
	GENERAL CONDITIONS (Not including Bond & Insurance)			
0.75%	GENERAL INSURANCE		\$ 879	
0.70%	CM P & P BONDS		\$ 827	
0.00%	BUILDERS RISK		BY OWNER	

A.1.1.5 - ALTERNATES

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE.



EXHIBIT A1 - GMP - ATTACHMENT #02 04/08/24

CONTINGENCY - (CM Construction - GMP) CMR FEE		\$ \$	4,163 1,416	
	TOTALS:	\$	124,515	TBD

ALTERNATES INDICATED AS TBD SHALL BE CONSIDERED TO BE DETERMINED WITHIN SIXTY (60) DAYS OF AMENDMENT DATE. SEE ASSUMPTIONS AND QUALIFICATIONS.

MI A MI J J J A S O N D J F M A M J J J A S O N D J F M A M J J J A S O N D J F M A M J J J A S O N D J F M A M J J J A S O N D J F M A M J J J A S O N D D F M A M J J J A S O N D D F M A M D D F M A M D D F M A M D D F M A M D D F M A M D D F M A M D D F M A M D D F M A M D D F M M D D F M M D D M M D M D M M	KILLINGLY COMMUNITY CENTER	ITY CENTER				BASELINE SCHEDULE	EXHIBIT A2.3.2, ATTACHMENT #3 - SCHEDULE
Interior DD Budget/Reconcilation 19 17 19 19 19 19 19 19		ame	Planned	Start		- I -	2025 2026 2026 2026
The chargest of the chargest		illingly Community Center					NO SECTION AND ALCONDATE OF THE PROPERTY OF TH
10.00 Inferior & Discourant Complete 10.00 17-bar-23 17-	Preconstruction	reconstruction					
10.0 Interfect Of Discussive Computer 20.0 17.4 deg 2.3 22.4 deg 2.3 23.4 deg 2.3	PRE100	invelope 100% CDs Rcvd	10	17-Apr-23	17-Apr-23	Finvelope 100% CDs Royd	
	PRE110	rterior SD Documents Complete	10d	17-Apr-23	28-Apr-23	Phyterior SD Documents Complete	
140 Interest ON CROCK Revealed 24 mars	PRE120	nterior DD Documents Complete		01-May-23	23-Jun-23	Interior DD Documents Complete	
15-0 Interfect Deligned Placeardinaries 2-13-12-23 15-14-2	PRE130	nterior 90% CDs Rcvd	p98	26-Jun-23	26-Oct-23	Free Interior 90% CDs Rcvd	
150 City Clarket Particular Compare 154 27-04-23 17-14-2	PRE140	nterior DD Budget/Reconcilation	20d	26-Jun-23	24-Jul-23	Interior DDiBudget/Reconcilation	
Fig. 20 17-00-12 15-00-12 17-00-12	PRE150	arly Release Package Design Compl	PO		16-Aug-23	●◆Early-Release Package Design Complete	
March Marc	PRE160	nterior CD Budget/Reconcilation	20d	27-0ct-23	27-Nov-23	Interior CD Budget / Reconcilation	
Manual Emission Manual Emi	PRE170	00% CDs Rcvd for Bidding	15d	27-0ct-23	17-Nov-23		
100 DCC Charteris for Bild Envelope 141 18-49c-23 20-24c-23 11-40c-24 11-40c	Bid / Award En	iid / Award Envelope					
12.00 CCC Score Review Emergence 154 13-44p-23 11-44p-23	BID1010	ICC Develop Bid Docs Envelope	14d	18-Apr-23		DCC Develop Bid Docs Envelope	
11-10 Calcidade Calcida	BID1020	ICC Advertise For Bids Envelope	30	18-Apr-23	r	PDCC Advertise For Bids Envelope	
DCC Scope Review Enreliene Total 12-May-23 25-May-23 12-May-23 12-Ma	BID1030	ICC Bid Period Envelope	15d	21-Apr-23	11-May-23	The DCC Bid Period Envelope	
200 DCC (AND Development Envelope 10d 19-May-23 09-Jun-23 19-Jun-23 19-Jun-2	BID1040	ICC Scope Review Envelope	10d	12-May-23	25-May-23	Fell-DCC Scope Review Envelope	
17-20 17-2	BID1050	ICC GMP Development Envelope	10d	19-May-23	02-Jun-23	PDCC GMP Development Envelope	
12-Jun-23 13-Jun-23 13-J	BID1060	own GMP Approval Envelope	2d	05-Jun-23	09-Jun-23		
200 DCC (state Contracts 54 19-Jun-23 23-Jun-23 11-Dec-23 11-Dec	BID1070	CC Notice To Proceed To Trades	pS Sd	12-Jun-23	16-Jun-23	T-DCC Notice To Braced To Trades	
11-Dec-23 11-D	BID1080	CC Issue Contracts	PS 2d	19-Jun-23	23-Jun-23	THE COLUMN CONTRACTS	
17.0 DCC Develop Bid Docs Interior 200 27-0et-23 11-Dec-23 11-Dec-23 11-Dec-23 11-Dec-23 11-Dec-23 11-Dec-23 12-Dec-23 11-Dec-23 11-Dec-23 12-Dec-23 12-Dec-	Bid / Award Int	id / Award Interior Renov					
DCC definer(see for Bidst Interior 55d 12-Dec-23 18-Dec-23	BID3010	CC Develop Bid Docs Interior	30d	27-Oct-23	11-Dec-23	F	
Dec Bid Period Interior 356 04-Jan-24 21-Feb-24 15-Aba-24 16-Aba-24 16-Aba-2	BID3020	ICC Advertise for Bids Interior	PS Sd	12-Dec-23	18-Dec-23	Manual Parties for Bids Interior	
DCC Scope Review Interior 15d 22-7eb-24 13-Mar-24 10-Apr-24 13-Mar-24 10-Apr-24 10-Apr	BID3030	CC Bid Period Interior	35d	04-Jan-24	21-Feb-24	-DCC Bid Period Interior	
DCC GMP Development Interior 20d 14-Mar-24 10-Agn-24 15-Agn-24 15-Agn-23 15-Agn-24 15-	BID3050	CC Scope Review Interior	15d	22-Feb-24	13-Mar-24	Tem-DCC Scope Review Interior	
Town GMP Approval Interior 2d 11-Apr-24 15-Apr-24 15-Apr	BID3060	CC GMP Development Interior	D02	14-Mar-24	10-Apr-24	Cem-DCC GMP Development Interior	
DCC Notice D Proceed To Trades 3d 16-Apr-24 18-Apr-24 19-Apr-24	BID3070	own GMP Approval Interior	Zd	11-Apr-24	15-Apr-24		
Decrement	BID3080	CC Notice To Proceed To Trades	2d	16-Apr-24	18-Apr-24	Lat-DCC Notice To Proceed To Trades	
Submit/Approve/ Release Long Lea 30d 17-Apr-23 26-May-23 26-May-2		ACC Issue Contracts		03-May-24	03-May-24	The DCC Issue Contracts	
280 Submit/Approve/Release Long Lea. 30d 17-Apr-23 26-May-23 27-Jun-23 23-Jun-23 30-Jun-23	Procurement	rocurement					
290 Mechanical Curb Procurement 50d 30-May-23 11-Dec-23 11-Dec-24 Mechanical Equipment Procurement 175d 30-May-23 07-Feb-24 Per Helical Tie Submittals Per Helical Tie Submitta		ubmit/Approve/ Release Long Lea	20d	17-Apr-23	26-May-23	-Submit/Approve/ Release Long Lead MEP	
Sign Mechanical Equipment Procurement 155d 30-May-23 11-Dec-23 11-Dec-24 Feb-24		fechanical Curb Procurement	P05	30-May-23	08-Aug-23	Mechanical Curb-Procurement	
Electrical Gear & Panel Procurement 175d 30-May-23 07-Feb-24 Feb-14 Feb-	PRO300	lechanical Equipment Procurement	135d	30-May-23	11-Dec-23		
Helical Tie Submittals / Approvals	PR0310	lectrical Gear & Panel Procurement	175d	30-May-23	07-Feb-24		
10 Roofing Submittals 5d 19-Jun-23 23-Jun-23 23-Jun-23 30-Jun-23	PRO100	elical Tie Submittals / Approvals	10d	12-Jun-23	23-Jun-23	Helical Tie Submittals / Approvals	
20 Caulking Submittals 10d 19-Jun-23 30-Jun-23 30-Jun-23 30-Jun-23 30-Jun-23 30-Jun-23 30-Jun-23 17-Jul-23 17-Jul-	PR0110	oofing Submittals	2d	19-Jun-23	23-Jun-23	September Submittals	
30 Brick Submittals	PR0120	aulking Submittals	10d	19-Jun-23	30-11m-23	Legisland Calmarks	
Window Submittals 20d 19-Jun-23 17-Jul-23 Emphindow Submittals Parked	PR0130	rick Submittals	10d	19-Jun-23	30-Jun-23	Sauring Judillings	
KILLINGLY COMMUNITY CENTER Revision Checked		findow Submittals	70g	19-Jun-23	17-Jul-23	- Mindow Alibmittale	
	8				KILLING		
// 11/2 1/1/	NNES FRON COMPANY				27	79 WESTFIELD AVE.	
TO A SUPERING IN						+ > > > > > > > > > > > > > > > > > > >	

1								PRELIMINARY BASELINE SCHEDULE
190 Roof Perimyter Coping Submittals 156 19-Jun-23 10-Jul-23 10-Ju	9	-	Name	Planned Duration	Start	Finish	2023	2025 2026 D 1 E M A M 1 1 1 A S C B W 1 A M 2 1 1 A S C B W 1 A W 2 W 3 W 3 W 3 W 3 W 3 W 3 W 3 W 3 W 3
19.00 Approve British Submittable 10.0 2.0 ± Jan. 23 10.3 Jan. 23 10.			Roof Perimeter Coping Submittals	15d	19-Jun-23	10-Jul-23	Roof	U J F M A M J J A S O N B J F M A M J J A S O N D
Petring Schmidter 15 26-3u-23 17-3u-23 17-3u-			Approve Roofing Submittals	2d	26-Jun-23	30-Jun-23	CTA prove Roofing Submittals	
15 22-3m-23 17-3a-23 17-3			Painting Submittals	10d	26-Jun-23	10-Jul-23	Painting Submittals	
22.00 Cauling Agenomia 15 a. 2-Jun-23 17-Jul-23 17-Jul-2			Helical Tie Pull Test	2d	26-Jun-23	30-Jun-23	1	
200 Calculate Approve Berk Submittable Controlling Approver Berk Submittable C			Prep/Submit Exterior HMDF/Hardware	15d	26-Jun-23	17-Jul-23	Prep/Submit Exterior HMDF/Hardware	
Protection Pro	_		Caulking Approvals	10d	03-Jul-23	17-Jul-23	Gaulking Approvals	
240 Approve Potentiere Copies Solution (19 do 23, 23, 23 17, 284, 23 2			Approve Brick Submittals	10d	03-Jul-23	17-Jul-23	Approve Brick Submittals	
11-24-12 11-24-12			Roofing Material Procurement	10d	03-Jul-23	17-Jul-23	Roofing-Material-Procurement 1	
24.0 Approve Roof Perimeter Coping Sub 104 11-Jul-23 12-Jul-23 11-Dut-23			Approve Painting Submittals	2q	11-Jul-23	17-Jul-23	Approve-Painting-Submittals - 1	
230 September 130 Sept			Approve Roof Perimeter Coping Sub	10d	11-Jul-23	24-Jul-23		
Agrone Window Submittaby Agrone Window Submittaby	_		Brick Procurement	P09	18-Jul-23	11-0ct-23	Brick Procurement - C. J	
Peap State Pea			Approve Window Submittals	15d	18-Jul-23	07-Aug-23	Approve Window Submittals	
Rolew/kporoe Euricin Holicy Hanner 10d 18-Jul-23 19-Sep-23 19-Sep-23			Prep/Submit Interior HMDF/Wood D	PS	18-Jul-23	24-Jul-23	Call Prep/Submit Interior HMDF/Wood Doors/Hardware	
2500 Roof Perimeter Copine Procurement 40d 25-Jul-23 19-Sep-23 19-			Review/Approve Exterior HMDF/Har	10d	18-Jul-23	31-Jul-23	Cell-Review/Approve-Exterior HMDF/Plardware	
Septiment Propose interior HMDF/Wood Donzy-Handware			Roof Perimeter Coping Procurement	40d	25-Jul-23	19-Sep-23		
San			Review/Approve Interior HMDF/Woo	10d	25-Jul-23	07-Aug-23	Review/Approve Interior HMDF/Wood Doors/Hardware	
Window & GVV Procurement (Openine Gold OB-Alug-233 11-Nov-233 18-Oct-233 18-Oct-234			Fabricate/Deliver/Available Exterior	20d	01-Aug-23	12-Sep-23	Fabricate/Beliver/Available Exterior HMDF/Hardwar	ga
Septicate Checker Sold OB-Aug-23 18-Oct-23 Septicate Septicate Checker Sold OB-Aug-23 Septicate Septicate Checker Septicate			Window & CW Procurement (Openin	p09	08-Aug-23	01-Nov-23	Figure	Laranteed
1020 State these occupancy 17-Apr-23 25-Feb-25 1920 16-Jun-23 26-Feb-25 1920 16-Jun-23 28-Jul-23 1920 16-Jun-23 16-Jun			Fabricate/Deliver/Available Interior	P05	08-Aug-23	18-Oct-23	Fabricate/Deliver/Available Interior HMDE/Woor	Doors/Hardware
17-40-23 25-Feb-25 17-40-23 25-Feb-25 17-40-23 25-Feb-25 17-40-23 25-Feb-25 17-40-23 25-Feb-25 17-40-23 17-40-23 18-40 18-40 1			Occupant Critical Dates					
1020 KMS 4th Grade Last Day of School 16-Jun-23 18d 16-Jun-23 18d 16-Jun-23 18d 16-Jun-24 18d 18d			BOE Central Office Occupancy	470d	17-Apr-23	25-Feb-25		BOF Central Office Occupancy
1900 ECSU Summer Classes 2023 18d 05-Jul-23 28-Jul-23 18d 05-Jul-24 20 30-Aug-23 4 4-Jun-24 20 14-Jun-24 20 15-Jul-24 20 15-Jul-24 20 15-Jul-24 20 15-Jul-24 20 15-Jul-24 20 20-Jul-24 20 20-J	L		KMS 4th Grade Last Day of School	Po	16-Jun-23 💽		◆ KMS 4th Grade Last Day of Schoell W	
1930 KMS 4th Gride First Day of School 30-Aug-23 14-Jun-24 14-Jun-25 14-Jun-24 14-Jun-25 14-Jun-24 14-Jun-24			ECSU Summer Classes 2023	18d	05-Jul-23	28-Juf-23	ECSU Summer Classes 2023	
14-Jun-24 14-J			KMS 4th Grade First Day of School	ро				
10500 ECSU Summer Classes 2024 20d 05-Jul-24 01-Aug-24 01-Aug-24 01-Aug-24 01-Aug-24 01-Aug-24 01-Aug-24 01-Aug-24 01-Aug-24 02-Jul-24 02-Jul-25 02-Jul-24 02-Jul-25			KMS 4th Grade Last Day of School	PO		14-Jun-24 C	en 11	sst Day of School
Milestones Mil			ECSU Summer Classes 2024	50d	05-Jul-24 C	01-Aug-24	File ECSU Summer	r Classes 2024
Start Phase 14 Construction (Area V Od 06-May-24G			Construction					
Phase 1A Construction (Area V Od O6-May-24 G			Milestones					
10 Phase 14 Occupancy Obtained 0d 02-Jul-24 19 19 19 19 19 19 19 1			Start Phase 1A Construction (Area V	PO	06-May-24 C		H with the base 1A Construction	uction (Area Vacated by Owner)
20 Start Phase, 1B Construction (Area V Odd 08-Jul-24 09-Sep-24		İ	Phase 1A Occupancy Obtained	В		02-Jul-24	I I Phase 1A Occupa	ancy Obtained
20 Phase 18 Occupancy Obtained 004 11-Sep-24 15-Nov-24			Start Phase, 1B Construction (Area V	PO	08-Jul-24		Start Phase 1B C	Construction (Area Vacated by Owner)
40 Start Phase 2A Construction (Area V 0d 11-Sep-24 15-Nov-24 1			Phase 1B Occupancy Obtained	PO		09-Sep-24	- Phase 18	B Occupancy Obtained
50 Phase 2A Occupancy Obtained 0d 15-Nov-24 15-Nov-25 15-Nov-25 15-Nov-25 15-Nov-25 15-Nov-25 15-Nov-25 15-Nov-24 15-Nov-25			Start Phase 2A Construction (Area V	p0	11-Sep-24		Start Ph	ase 2A Construction (Area Vacated by Owner)
Start Phase 2B Construction (Area V od 20-Nov-24 13-Feb-25	- 1		Phase 2A Occupancy Obtained	PO		15-Nov-24		Phase 2A Occupancy Obtained
13-Feb-25	d		Start Phase 2B Construction (Area V	PO	20-Nov-24		\$ 15 h	Start Phase 2B Construction (Area Vacated by Owner)
80 Start Phase 3 Cocupancy Obtained/Proje 0d 18-Feb-25 90 Phase 3 Occupancy Obtained/Proje 0d 06-Jun-25 G KILLINGLY COMMUNITY CENTER 24-May-23 Deart Phase 3 Occupancy Obtained/Proje 0d 06-Jun-25 G KILLINGLY COMMUNITY CENTER 24-May-23 Deart Phase 3 Occupancy Obtained/Proje 0d 06-Jun-25 G Revision			Phase 2B Occupancy Obtained	PO		13-Feb-25		◆→Phase 2B Occupancy Obtained
90 Phase 3 Occupancy Obtained/Proje 0d 06-Jun-25 © Community Center Bate Revision KILLINGLY COMMUNITY CENTER Date Revision 79 WESTFIELD AVE.			Start Phase 3 Construction (Area Va	РО	18-Feb-25			Start Phase 3 Construction (Area Variated by Owner)
KILLINGLY COMMUNITY CENTER Date Revision 79 WESTFIELD AVE.			Phase 3 Occupancy Obtained/Proje	PO				◆ Phase 3 Occupancy Obtained / Project Substantial Completion
79 WESTFIELD AVE.						KILLING		Revision
	OWNES							DRAFT
TO VISINITIES	RUCTION COMPAN	*				7	WESTFIELD AVE.	
							KILLINGLY, CT	

	1				
Name	ion Start	Finish	AM 3 3 A S O N D 3 F M A M 3 3 A S O	2024 2026 M	2026 A M 3 1 1 A S D N
Relocations Relocations			11		
	2d 03-Jul-24	05-Jul-24	III FI + East Conn Fa	T East Conn Faculty Occupies Refurbished Phase 1A	
P1B.105 Owner Occupies Refurbished Phase 1B	1d 10-Sep-24	10-Sep-24	LE STEEL STE	Towner Occupies Refurbished Phase 18	
P2A.105 East Conn Facility Occupies Refurbis	2d 18-Nov-24	19-Nov-24	=======================================	TEast Conn Eacility Occupies Refurbished Phase 24	
P2B.105 Owner Occupies Refurbished Phase 2B	2d 14-Feb-25	17-Feb-25	==	T-Owner Occupies Refurbished Dhase 28	
Phase 1A Phase 1A					
Envelope Envelope					
2					
P1A.100 Courtyard Helical Ties - Courtyard N	5d 06-May-24	10-May-24	Tit I'I	ourtvard Helical Ties - Courtvard North & West Flevations	
P1A.115 Exterior Brick Repairs & Restoration	10d 04-Jun-24	17-Jun-24	III STEELING Brick R	Figure 1 - Control of the Floration - Control of the Florations	
P1A.195 Sawcut/Dema New Door Opening @	3d 05-Jun-24	07-Jun-24	III	P. Sawrit/Demo New Door Opening @ Furrhard	
P1A.205 Prep New Opening for HM Frame @	2d 10-Jun-24	11-Jun-24	THE STATE OF THE S	rep New Opening for HM Frame ® Courtward	
P1A.215 Install New HM Door Frame @ Court	1d 12-Jun-24	12-Jun-24	MH wew Hart	nstall New HM Door Frame ® Countrierd	
P1A.225 Hang New Door/Install Hardware @	_	13-Jun-24	H Hang Naw Doo	Hans Naw Door/Install Hardware & Countrard	
P1A,120 Replace Windows - Courtyard North	_	24-Jun-24	The Paris of Minds	Pitteniare Windows - Courtward North & West Flevations	
Permeter Permetter					
P1A.130 Exterior Brick Repairs & Restoration	10d 06-Mav-24	17-May-24	The state of the s	- Exterior Brick Bonsire & Destruction - Mosthwood Society	
Exterior Brick Repairs & Restoration	1	03- Jun-24	III MARINE BIRL DO	Exterior Dirth Nepalls & Nestalation - 140f timest Sector	
Replace Windows - Northwest Sector	1	11-Jun-24	III	Extension brack nepality or restoration - Southwest Sector Dailbre Windows - Morthward Sector	
T	1	06 Jun 24	III	- NOT LINES SECTOR	
T	1	10 Jun 24		awout, perior new boor Opening @ Southwest Perimeter	
t	1	11 1 24	THE COMMENT OF THE CO	The new Opening for him Frame (a) Southwest Perimeter	
Ť	4	11-Jun-24	III. The HM	Trinstall New HM Door Frame @ Southwest Perimeter	
t	4	17-Jun-24	III alkebiace windo	Theplace Windows - Southwest Sector	
Ť	4	12-Jun-24	OOO Men Den Doo	lang New Door/Install Hardware @ Phase 1A Perimeter	
T	5d 20-Jun-24	26-Jun-24	III Meplace Curta	Replace Curtainwall - Phase 1A Perimeter	
/st					
P1A.155 Install Roofing System Failed Area TBD	5d 06-May-24	10-May-24	III III Noofing System Failed Area TBD	m Failed Area TBD	
P1A.175 Final Roof Perimeter Terms TBD		17-May-24	The Final Roof Perimeter Terms TRD	r Terms TBD	
P1A.170 Install Roofing Copings / Terminations		24-Mav-24	Thorsall Boofing Co	Install Roofing Conings / Terminations	
Interior Reno Interior Renovation					
P1A.185 Temp Protection/Abatement/Selecti	10d 06-May-24	17-May-24	Figure Protection/A	Temp Protection/Abatement/Selective Demolition - Phase 14	
П	7d 06-May-24	14-May-24		Phase 1A	
	5d 20-May-24	24-May-24	i e Electrical Modifica	ions - Phase 1A	
	5d 20-May-24	24-May-24	Think C Modifications - Phase 1A	s - Phase 1A	
	7d 20-May-24	29-May-24	Thinterior CMU Infil	/Demising Wall - Phase 1A	
P1A.335 Plumbing Modifications - Phase 1A	5d 20-May-24	24-May-24	- Humbing Modifica	tions - Phase 14	
	_	03-Jun-24	The Party for N	Prent Parch for New Toilet 8ms - Dhase 1A	
P1A.285 Blockfill New CMU - Phase 1A		05-Jun-24	THE CALL - Phase 18	- Phase 14	
			GIV COMMINITY CENTED	Date Revision Checked	Approved
DOWNER				24-May 23 DRAFT	3
ANEGH		7	79 WESTEIELD AVE		

Y COMM	KILLINGLY COMMUNITY CENTER	Planned			PRELIMINARY BASELINE SCHEDULE	ASELIN
	Name	Duration	Start	t Finish	AIM 3 3 A S S O N D 3 F M A M	2026
P1A.305	Waterproof/Install Tile @ New Toilet	29	04-Jun-24	10-Jun-24		
P1A.385	Rehang Existing/Hang New Doors/	29	06-Jun-24	12-Jun-24	Holley Basting/Hang New Doors/Hardware - Phase 1A	
P1A.365	Rework ACT Ceiling Grid/Fixtures/Ti	2d	11-Jun-24	17-Jun-24	Philework ACT Ceiling Grid/Fixtures/Tiles as Needed - Phase 1A	
P1A.315	Install Plumbing Fixtures @ New Toil	2d	11-Jun-24	12-Jun-24	This property of the Property	
P1A.325	Install Toilet Accessories @ New Toil	рL	13-Jun-24	13-Jun-24	The first of the f	
P1A,375	Apply Paint/Wall Coverings - Phase 1A	54	14-Jun-24	20-Jun-24	HADIN Paint Wall Coverings - Phase 1a	
P1A.395	Polish/Seal Existing Terrazzo Floor	34	21-Jun-24	25-Jun-24	Politic Name Control of Control o	
P1A.405	New VCT Flooring/Base - Phase 1A	24	26-Jun-24	27-Jun-24	Highwy VCT Floring Rases, Dasses 14	
P1A.415	Final Clean/Punchout/Final Inspecti	3d	28-Jun-24	02-Jul-24	At Enail Class / Director (Final Inserting Make Dough on Community	Dhass 1A
Phase 1B	Phase 1B				יייני מינית איני מונית ויייני אינית ויייני אינית ויייני אינית ויייני אינית ויייני אינית אות אינית אות אינית אינית אינית אינית אינית אות אינית אות אינית אות אינית אות אות אינית אינית אינית אינית אות אינית	riase D
Envelope	Envelape					
Courtyand	Courtyard				_	
P1B.100	Courtyard Helical Ties - Courtyard S	3d	08-Jul-24	10-Jul-24	- Ar Courthard Haliral Thas . Courthard Court Elanceine	
P18,115	Exterior Brick Repairs & Restoration	P\$	11-3ul-24	17-Jul-24		
P1B,195	Sawcut/Demo New Door Opening @	3d	18-Jul-24	22-Jul-24	Participation of the property	
P1B,120	Replace Windows - Courtyard East El	2d	18-Jul-24	24-Jul-24	A Soulise Million Control Test Florestone	
P1B,205	Prep New Opening for HM Frame @	2d	23-101-24	24-Jul-24	- Chinara State of the Control of th	
P1B.215	Install New HM Door Frame @ Court	14	25-Jul-24	25-114-24	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	
P1B.225	Hang New Door/Install Hardware @	10,	26-Jul-24	26-114-24	A lives in the transfer of the	
Permeter	Portmetter				India grew Door/Itstall naturate (p. Couryard	
P18.130	Exterior Brick Repairs & Restoration	10d	08-Jul-24	19-3ul-24	11 - Illinoiscopor Doraire C. Dorbowsian Nacht Darissobar	
P1B,135	Exterior Brick Repairs & Restoration	10d	22-Jul-24	02-Aug-24	Lyterior Brick Repairs & Restoration - 1901 (1 Per little)	
P1B.140	Replace Windows - North Perimeter	10d	05-Aug-24	16-Aug-24	Replace Windows - North Perimeter	
P1B,235	Sawcut/Demo New Door Opening @	3d	05-Aug-24	07-Aug-24	The state of the s	
P18,245	Prep New Opening for HM Frame @	2d	08-Aug-24	09-Aug-24	Physical Desirable Programs of Physical Berinders	
P1B.255	Install New HM Door Frame @ Phas	10	12-Aug-24	12-Aug-24	Anstall New HM Door Frame @ Phase IB Perimeter	
P1B.265	Hang New Door/Install Hardware @	1d	13-Aug-24	13-Aug-24	Hardware @ Dhase RD Derinotes	
P1B.145	Replace Windows - East Perimeter	2d	19-Aug-24	23-Aug-24	MReplace Windows - East Perimeter	
P1B.150	Replace Curtainwall - Phase 1B	ps	26-Aug-24	30-Aug-24	Feblace Curtainwall - Phase IB	
Roofing Syst	. Roofing System - Phased Sensitive T					
P1B,155	Install Roofing System Failed Area TBD	2d	08-Jul-24	12-Jul-24	Philistophia System Failed Area TBD	
P1B,175	Final Roof Perimeter Terms TBD	PS 24	15-Jul-24	19-Jul-24	P-Hall Roof Perimeter Terms TBD	
P18,170	Install Roofing Copings / Terminations	29	22-Jul-24	26-Jul-24	10 Terminations (1997)	
Interior Reno						
P1B.180	MEP Coordination - Phase 1B	29	08-Jul-24	12-Jul-24		
P18,185	Temp Protection/Abatement/Selecti	50	08-Jul-24	12-Jul-24	Properties Observed Calactics Downstition 10	
P18.355	Electrical Modifications - Phase 1B	PS	15-Jul-24	19-Jul-24	The control of the co	
P1B,345	HVAC Modifications - Phase 1B	P5	15-Jul-24	19-Jul-24	Modifications - Dhase 18	
				KILLING	KILLINGLY COMMUNITY CENTER Date Revision Checked	Approved
DOWNES			-		24-May-23 DRAFT JSA	
È				7	79 WESTFIELD AVE.	

KILLINGLY COMMUNITY CENTER	:R						PRELIMINAR	PRELIMINARY BASELINE SCHEDULE
ID Name		Planned Duration	Start	Finish	2023 A M D 1 J A S O N D J E M A M J	OINID JIEIMIAIMIT	24 2025 2026 2026 2026 2026 2026 2026 2026	2026 A May 21 3 1 A 15 10 10 10
153 Plumbing Modiffic	Plumbing Modifications - Phase 1B	2d	15-Jul-24	19-Jul-24		Plumbing Modifications - Phase 1B		AMESIA
P1B.295	Prep/Patch for New Toilet Rms - Pha	2d	22-Jul-24	26-Jul-24	20.00	Frierp/Patch for New Toilet Rms - Phase 1B	e 18	
P1B.305	Waterproof/Install Tile @ New Toilet	2d	29-Jul-24	02-Aug-24	- All Materia	proof/Install Tile @ New Toilet	Rooms - Phase 1B	
156 P1B.385 Rehang Existing/	Rehang Existing/Hang New Doors/	2d	29-Jul-24	30-Jul-24	and	Existing/Hang New Doors/H	lardware - Phase 18	
157 P1B.365 Rework ACT Ceilin	Rework ACT Ceiling Grid/Fixtures/Ti	ps 2d	05-Aug-24	09-Aug-24	D. C. Sewor	Pework ACT Ceiling Grid/Fixtures/Tiles as Needed - Phase 1B	iles as Needed - Phase 1B	
158 P1B.315 Install Plumbing F	Install Plumbing Fixtures @ New Toil	Zd	05-Aug-24	06-Aug-24	ets	Stall Plumbing Fixtures @ New Toilet Rooms - Phase 18	let Rooms - Phase 18	
159 P1B.325 Install Toilet Acce	Install Toilet Accessories @ New Toil	10	07-Aug-24	07-Aug-24	lets	Thinstall Toilet Arressories @ New Toilet Rooms - Dhase 18	let Rooms - Phase 18	
160 P1B.375 Apply Paint/Wall	Apply Paint/Wall Coverings - Phase 1B	50	14-Aug-24	20-Aug-24	Cu y	Proposition (Wall Coverings - Disea 18	1100000	
161 P1B,405 New VCT Flooring	New VCT Flooring/Base - Phase 1B	2d	21-Aug-24	22-Aug-24	No.	Me New VCT Flooring / Bace - Dhace 18	11 11	
162 P1B.415 Final Clean/Punc	Final Clean/Punchout/Final Inspecti	PS Sd	03-Sep-24	09-Sep-24		nal Clean/Princhort/Final Inco	# Final Clean (Directory / Final Instructions (Make Deads for Owner Occurrence Observed)	Orange Ohnes 10
163 Phase 2A Phase 2A						dem min change of the same	certain many later than a series	occupanty - rijase ip
164 Envelope Envelope								
P								
P2A,115	Exterior Brick Repairs & Restoration	50	11-Sen-24	17-Sen-24		Separation Design Description C. Deschares	Participate Drive Described Committee C. Denska making of constitution of the contract of the	
167 P2A.195 Sawcut/Demo Ne	Sawcut/Demo New Door Opening @	34	18-Sep-24	20-Sep-24		Saucrat /Domo New Door Operator @ Control	inor - courtyaid south Elevation	_
168 P2A,120 Replace Windows	Replace Windows - Courtyard South	89	18-Sen-24	27-Sen-24		The state of the s	Court Daniel	
169 P2A.205 Prep New Openin	Prep New Opening for HM Frame @	24	23-Sep-24	24-Sen-24	13	The Bran Naw Opening for UNI Come @ Construction		
t	Install New SF Door Frame @ Courty	19	30-Sep-24	30-Sep-24	4	Alectrical Name SE Door Erams & Countries	THE GOOD TABLE	
P2A.225	Hang New SF Door/Install Hardware	PL	01 Oct 24	01 Oct 24		install New SP LOOP Flatter (9)	Courtyard	
Roofing Syst	Roofing Switem - Phased Sensitive T		17-170-10	10010		Finang New 3r Door/Install Hardware (@ Courtyard	raware (a Countyard	
D2A 155	Install Desting System Collect Ann TDD	3	4	0 10		-		
72A, 133	Stein railed Area I DD	DO I	11-5ep-24	17-Sep-24	1	Install Roofing System Failed Area TBD	ea TBD	
P2A,173	ster terms IBU	20	18-Sep-24	24-Sep-24	# 1	Final Roof Perimeter Terms TBD	۵	
PZA,T70	Install Roofing Copings / Terminations	29	25-Sep-24	01-0ct-24	<u>.</u>	Latelia Roofing Copings / Terminations	ninations	
no.	uc							
P2A.180	n - Phase 2A	74	11-Sep-24	19-Sep-24	N. d.	II-MEP Coordination - Phase 2A		
P2A.185	Temp Protection/Abatement/Selecti	10d	11-Sep-24	24-Sep-24		 Temp Protection/Abatement/S		
179 P2A.355 Electrical Modifica	Electrical Modifications - Phase 2A	2d	25-Sep-24	01-0ct-24	1	Felectrical Modifications - Phase 20	2A	
P2A.345 HVAC Modifications - Phase 2A	ins - Phase 2A	Şq	25-Sep-24	01-0ct-24		Par HVAC Modifications - Phase 2A		
P2A.335 Plumbing Modific	Plumbing Modifications - Phase 2A	54	25-Sep-24	01-0ct-24		Of Plumbing Modifications - Phase 2A		
P2A.295 Prep/Patch for Ne	Prep/Patch for New Gang Toilet Rms	29	02-0ct-24	08-Oct-24		- Heren/Patch for New Gans Toilet Rms - Phase 24	let Rms - Phase 24	
P2A,310 Install New Lightin	Install New Lighting @ Kitchen - Pha	29	02-Oct-24	08-Ort-24		AC	- Dhare 38	
T	Waterproof/Install Tile @ New Gang	89	09-Oct-24	21-Oct-24		Illistali Ivew Lightling & Nitchel	in - Fridoe ZA	
T	Apply Paint/Wall Coverings - Phase 2A	100	00-004-24	22 Oct 24	Li	The water proof in Island I like to the	A vacel proof/litistail lile to thew daring lotter rooms - Priese ZA	đ
T	Rehang Existing / Hang New Doors /	2	09 Oct 24	14 Oct 24		Coverings - Phase 2A	- Phase ZA	
Ť	Control Name Country of Control College	7 0	07-OCL-24	10-00-Z		The nang Existing/Hang New	Doors/Hardware - Phase ZA	
P.2A.303	Control Cellings	80	11-0ct-24	23-Oct-24	£.1	Thistall New Sound Control Ceilings - Phase 2A	eilings - Phase 2A	
P2A.190	Install New LVT Flooring/Base - Pha	POL	18-Oct-24	31-0ct-24	=1	Install New LVT Flooring/Base - Phase 2A	lase - Phase 2A	
	Install Plumbing Fixtures @ New Ga	2d	22-Oct-24	28-Oct-24		Frinstall Plumbing Fixtures @	Frinstall Plumbing Fixtures @ New Gang Toilet Rooms - Phase 2A	22A
190 P2A.320 Install Toilet Partit	Install Toilet Partitions @ New Gang	20	29-Oct-24	30-Oct-24		Frinstall Toilet Partitions @ N	Thinstall Toilet Partitions @ New Gang Toilet Rooms - Phase 2A	ZA.
•				KILLING	KILLINGLY COMMUNITY CENTER	Date Revision	Checked	Approved
DOWNES			_			24-May-23 DRAFT	JSA	
REPLECOMPANY				7	79 WESTFIELD AVE.			
					KILINGIN CT			

KILLINGLY COMMUNITY CENTER		PRELIMINARY BASELINE SCHEDULE
ID Name Planned Start Finish	2023 2024 2025 2024 2025 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2026	2025 M 1 1 1 4 6 1 0 1 N 1 0 1 1 1 1 1 1 1 1 1 1 1 1 1 1
31-0ct-24 31-0ct		Thinstall Toilet Accessories @ New Toilet Rooms - Phase 24
P2A.395 Polish/Seal Existing Terrazzo Floor 5d 01-Nov-24	Polish/Seal Existing	Polish/Seal Existing Terrazzo Floor - Phase 2A
5	Tel Final Clean/Punch	** Final Clean/Punchout/Final Inspections/Make Ready for Owner Occupancy - Phase 24
194 Phase 2B Phase 2B		עם פרובים ביות ביית ביית ביית ביית ביית ביית ביית
195 Envelope Envelope		
196 P2B.130 Exterior Brick Repairs & Restoration 12d 20-Nov-24 06-Dec-24	Texterior Brick Re	-Exterior Brick Repairs & Restoration - Dhase 28 Courth Derimeter
	The Carlotte	New Door Opening @ Phase 28 Doubleton
-	POSM CONTROL OF THE POSM C	Donlare Windows - Dhace 28 South Darimotes
. 2d 12-Dec-24	Parity New Charlet	Approx Millows - Friese 25 Journ Fellineter
H	AH may lietsuff	The I New HW Occ Frame @ Dage 28 Berimeter
1d 17-Dec-24	July wow Now Dor	Hang New Dong Install Hardware @ Dhace 2B Dorimeter
		מיני ומיני ומיני מיני מיני מיני ומיני לקי ו מיני לקי ו
	O Bullion III	Hostall Roofing System Eailed Area TRD
	Paris Box Dari	Manual Roof Darimeter Terms TRD
205 P2B.170 Install Roofing Copings / Terminations 10d 19-Dec-24 03-Jan-25	all control leaves and an arrangement of the control of the contro	-Install Roofing Conings / Terminations
207 P2B.180 MEP Coordination - Phase 2B 10d 20-Nov-24 04-Dec24	The Contribution Disco 2D	in Dhace 2D
P2B.185 Temp Protection/Abatement/Selecti 15d 20-Nov-24	City and Care III	emp Protection/Abatement / Selective Demolition - Dhace 28
-	Meritian Ma	Pertrical Modifications - Phase 2R
P2B.345 HVAC Modifications - Phase 2B 12d	STEP WAC Modifie	-HVAC Modifications - Phase 2B
P2B.335 Plumbing Modifications - Phase 2B 7d 12-Dec-24	Par lumping Mod	odifications - Phase 28
P28.375 Apply Paint/Wall Coverings - Phase 2B	Com Apply Paint	Apply Paint/Wall Coverings - Phase 2B
P2B.295 Prep/Patch for New Toilet Rms - Pha 5d 23-Dec-24	Parch fe	for New Toilet Rms - Phase 2B
P2B.385 Rehang Existing/Hang New Doors/ 8d 31-Dec-24	Rehang Exis	kehang Existing/Hang New Doors/Hardware - Phase 2B
P2B.305 Waterproof/Install Tile @ New Tollet		Paragraphoof/Install Tile @ New Toilet Rooms - Phase 2B
P28,365 Install New Sound Control Ceilings	Finistall New	w Sound Control Ceilings - Phase 2B
P2B.315 Install Plumbing Fixtures @ New Toil 2d 08-Jan-25	H- ustall Plum	4- Install Plumbing Fixtures @ New Toilet Rooms - Phase 2B
P28.325 Install Toilet Accessories @ New Toil 1d 10-Jan-25	Left-Install Toilet	nstall Toilet Accessories @ New Toilet Rooms - Phase 2B
P.28.405 New VCT Flooring/Base - Phase 2B 15d 17-Jan-25	LDA MAN LOS	New VCT Flooring/Base - Phase 2B
728.415	(sa-Final Cle	® Final Clean/Punchout/Final Inspections/Make Ready for Owner Occupancy - Phase
221 Phase 5 Phase 5		
Eliverope English		
P3.135 Exterior Brick Repairs & Restoration 10d 18-Feb-25	- E-E-Exteri	即手xterior Brick Repairs & Restoration - Phase 3 Perimeter
	The same	Sawcut/Demo New Door Opening @ Phase 3 Perimeter
P3.145		Replace Windows - Phase 3 Perimeter
226 P3.245 Prep New Opening for HM Frame @ 2d 07-Mar-25 10-Mar-25		Prep New Opening for HM Frame @ Phase 3 Derimeter
P3.255 Install New HM Door Frame @ Phas 1d 11-Mar-25	tsulf.	Hustall New HM Door Frame @ Dhace 2 Derimater
H	THAIR	+ Hang New Door/Install Hardware @ Phase 3 Perimeter
KIFTIN	GLY COMMUNITY CENTER	Revision Checked Approved
DOWNES SUSSIDICITIES OF THE PROPERTY OF THE PR	24-May-23	DRAFT
	79 WESTFIELD AVE.	

							PRELIMINARY BASELINE SCHEDULE
	D	Nаme	Planned Duration	Start	Finish	2025 2025 2026 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2026 2025 2025	2026
229	Roofing Syst	Roofing System - Phased Sensitive T					A W O S W C W D
230	P3.155	Install Roofing System Failed Area TBD	10d	18-Feb-25	03-Mar-25		
231	P3.175	Final Roof Perimeter Terms TBD	10d	04-Mar-25	17-Mar-25	The Final Roof Darimeter Tarms TRD	
232	P3.170	Install Roofing Copings / Terminations	10d	18-Mar-25	31-Mar-25	Install Brofing Counce / Terminations	
233	Interior Reno	Interior Renovation					
234	P3.180	MEP Coordination - Phase 3	PL PL	18-Feb-25	26-Feb-25	1 Phase 3	
235	P3.185	Temp Protection/Abatement/Selecti	20d	18-Feb-25	17-Mar-25	1 1 Journal of Public of P	Z usefile and itiom
236	P3.355	Electrical Modifications - Phase 3	20d	18-Mar-25	15-Apr-25	Security S	C Deally - London
237	P3.345	HVAC Modifications - Phase 3	30d	18-Mar-25	29-Apr-25		
238	P3.335	Plumbing Modifications - Phase 3	20d	18-Mar-25	15-Apr-25	Plimhing Modifications - Dhace 3	
239	P3.375	Apply Paint/Wall Coverings - Phase 3	50d	18-Mar-25	15-Apr-25	- The state of the	
240	P3.295	Prep/Patch for New Toilet Rms - Pha	29	16-Apr-25	22-Apr-25	There is a second of the secon	F.
241	P3.305	Waterproof/Install Tile @ New Toilet	29	23-Apr-25	29-Apr-25	Myterinord Install Tile Romes - Dhase Z	Pooms - Dhase Z
242	P3.385	Rehang Existing/Hang New Doors/	10d	23-Apr-25	06-May-25	Description of Manch and Manch (Manch and Manch Albrace Albrac	Harriwara Dhaca Z
243	P3,365	Rework ACT Ceiling Grid/Fixtures/Ti	15d	23-Apr-25	13-May-25	Period Control of the	Tiles as Needed - Dhase X
244	P3,315	Install Plumbing Fixtures @ New Toil	p2	30-Apr-25	01-May-25	Install Plumbing Fixtures @ New Triller Rooms. Phase & Pha	let Rooms - Phase 3
. 245	P3.325	Install Toile! Accessories @ New Toil	1d	02-May-25	02-May-25	Left Install Toilet Acrescories @ New Triels Rooms. Debes 2	et Rooms - Dhase 3
246	P3.405	New VCT Flooring/Base - Phase 3	70d	02-May-25	30-May-25	- Figure New VCT Flooring /Base - Phase 3	
247	P3.415	Final Clean/Punchout/Final Inspecti	P8	28-May-25	06-Jun-25	19 Final Clean/Plint Final Instructions (Make Bearly for Dumor Down	pertions (Make Boady for Owner Or

KILLINGLY COMMUNITY CENTER
79 WESTFIELD AVE.
KILLINGLY, CT

Pare	Kevision	Checked	Approved	_
				$\overline{}$
24-May-23	DRAFT	JSA		$\overline{}$
				_
				_



A.3.1.2 - SPECIFICATIONS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #04 04/08/24



The guaranteed Maximum Price is based upon the following Specifications:

Division / Spec	Title	Janua Data	Dougt	Cat
Section Division 00	Introductory Information	Issue Date	Rev#	Set
000001	Project Manual Cover	40/4/0000		
	•	12/1/2023		
000107	Seals Page	12/1/2023		
010000	Table of Contents	12/1/2023		
Division 01	General Requirements			
011000	Summary	12/1/2023		
12100	Allowances	12/1/2023		
012200	Unit Prices	12/1/2023		
012300	Alternates	2/2/2024	2	Addendum 3
012500	Substitution Process	12/1/2023		
012500.A	CSI Substitution Request Form	12/1/2023		
012600	Contract Modification Procedures	12/1/2023		
012900	Payment Procedures	12/1/2023		
013100	Project Management and Coordination	12/1/2023		
013200	Construction Progress Documentation	12/1/2023		
013233	Photographic Documentation	12/1/2023		
013300	Submittal Procedures	12/1/2023		
013516	Alteration Project Procedures	12/1/2023		
014000	Quality Requirements	12/1/2023		
014200	References	12/1/2023		
014339	Mockups	12/1/2023		
015000	Temporary Facilities and Controls	12/1/2023		
016000	Product Requirements	12/1/2023		
017300	Execution	12/1/2023		
017419	Construction Waste Management and Disposal	12/1/2023		
017719	Closeout Procedures			
017700		12/1/2023		
017823	Operation & Maintenance Data Project Record Documents	12/1/2023 12/1/2023		
017839	•			
017900	Demonstration & Training	12/1/2023		
018113	Volatile Organic Compound (VOC) Limits for Adhesives,	12/1/2023		
040440	Sealants, Paints and Coatings	12/1/2023		
018119	Construction IAQ Management	12/1/2023		
Division 02	Existing Conditions			
024119	Selective Demolition	12/1/2023		
028213	Hazardous Materials Specification	12/1/2023		
028433	PCB Specification	12/1/2023		
Division 03	Concrete			
030559	Penetrating Colloidal Silica Concrete Treatment	12/1/2023		
033000	Cast-In Place Concrete	12/1/2023		
035416	Self Leveling Cement Underlayment	12/1/2023		
Dhelalan A4	Manager			
Division 04	Masonry	40/4/0000		
042000	Unit Masonry Assemblies	12/1/2023		
Division 05	Metals			
051200	Steel Framing	12/1/2023		
Division 06	Wood, Plastics, and Composites			
061053	Miscellaneous Rough Carpentry	12/1/2023		
061600	Sheathing	12/1/2023		
064023	Interior Architectural Woodwork	12/1/2023		

A.3.1.2 - SPECIFICATIONS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #04 04/08/24



The guaranteed Maximum Price is based upon the following Specifications:

Division / Spec Section	Title	Issue Date	Rev#	Set
Division 07	Thermal & Moisture Protection			
078100	Applied Fireproofing	12/1/2023		
078413	Penetration Firestopping System	12/1/2023		
078446	Fire Resistive Joint Systems	12/1/2023		
079200	Joint Sealants	12/1/2023		
079500	Expansion Control	12/1/2023		
Division 08	Openings			
	· · · · · · · · · · · · · · · · · · ·	0/0/0004		Addresdon o
081113	Hollow Metal Doors & Frames	2/2/2024	2	Addendum 3
081416	Flush Wood Doors	12/1/2023		
081743	Fiberglass-Reinforced Polyester (FRP) Flush Doors	12/1/2023		
083113	Access Doors & Frames	12/1/2023		
083326	Overhead Colling Grilles	12/1/2023		
083483	Floor Doors	2/2/2024	0	Addendum 3
084113	Aluminum-Framed Entrances & Storefronts	12/1/2023		
087100	Door Hardware	2/2/2024	2	Addendum 3
088000	Glazing	2/2/2024	2	Addendum 3
088300	Mirrors	12/1/2023	_	Addendam o
000300	MIITOIS	12/1/2023		
Division 09	Finishes			
092216	Non-structural Metal Framing	12/1/2023		
092900	Gypsum Board Assemblies	12/1/2023		
093000	Tiling	12/1/2023		
			•	4.11 1 0
095113	Acoustical Panel Ceilings	2/2/2024	2	Addendum 3
096519	Resilient Tile Flooring	1/26/2024	1	Addendum 2
096566	Resilient Athletic Surfacing	1/26/2024	1	Addendum 2
096613	Terrazzo Flooring Replacement & Repair	1/26/2024	0	Addendum 2
096723			v	Addendam 2
•	Resinous Flooring	12/1/2023		
096813	Tile Carpeting	1/26/2024	1	Addendum 2
098413	Acoustical Panels	12/1/2023	1	Addendum 2
099123	Painting (Professional Line Product)	12/1/2023		
Division 10	Specialties			
		4014/0000		
101100	Visual Display Surfaces	12/1/2023		
101400	Signage	12/1/2023		
102113	Toilet Compartments	12/1/2023		
102800	Toilet, Bath & Laundry Accessories	12/1/2023		
102000	Tollet, Datif & Eddinary Accessories	12/1/2023		
Division 12	Furnishings			
122113	Horizontal Louver Blinds	12/1/2023		
122413	Roller Window Shades	12/1/2023		
123400	Manufactured Plastic Laminate Clad Casework	12/1/2023		
Division 22	Plumbing			
220500		12/1/2022		
	Common Work Results For Plumbing	12/1/2023		
220519	General Duty Valves For HVAC Piping	12/1/2023		
220523	Hangers & Supports For HVAC Piping & Equipment	12/1/2023		
220548	Vibration / Selsmi Controls For HVAC Piping & Equipment	12/1/2023		
220553	Identification For Plumbing Piping & Equipment	12/1/2023		
220719	Plumbing Pipe Insulation	12/1/2023		
220800	Plumbing Systems Commissioning	12/1/2023		
221113	Water Distribution Piping	12/1/2023		
221316	Sanitary Waste & Vent Piping	12/1/2023		
224200	Plumbing Fixtures	12/1/2023		
District CO	Hashing Vandilading 9 Alm Occultations			
Division 23 230500	Heating Ventilating & Air Conditioning Common Work Results For HVAC	12/1/2023		
230523	General Duty Valves For HVAC Piping	12/1/2023		
230529	Hangers & Supports For HVAC Pipe & Equipment	12/1/2023		
	Vibration / Seismic Controls For HVAC Piping & Equipment	12/1/2023		

A.3.1.2 - SPECIFICATIONS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #04 04/08/24



The guaranteed Maximum Price is based upon the following Specifications:

Division / Spec				
Section	Title	Issue Date	Rev#	Set
230553	Identification For HVAC Piping & Equipment	12/1/2023	*	
230593	Testing Adjusting & Balancing For HVAC	12/1/2023		
230700	Duct Insulation	12/1/2023		
230719	HVAC Piping Insulation	12/1/2023		
230923	BAS Direct Digital Control System	12/1/2023		
230933	Variable Frequency Drive	12/1/2023		
230993	Sequence of Operation	12/1/2023		
231123	Natural Gas Piping	12/1/2023		
232000	HVAC Pumps	12/1/2023		
232113	Hydronic Piping	12/1/2023		
232300	Refrigerant Piping	12/1/2023		
233100	HVAC Ducts & Casing	12/1/2023		
233300	Ductwork Accessories	12/1/2023		
233700	Air Outlets & Inlets	12/1/2023		
236413	Air Cooled Chiller	12/1/2023		
237113	Central Station Air Handler	12/1/2023		
238100	Unitary HVAC Equipment	12/1/2023		
238129	Variable Refrigerant Flow	12/1/2023		
238224	Power Ventilators	12/1/2023		
Division 26	Electrical			
260500	Common Work Results For Electrical	12/1/2023		
260501	Common Work Results For Electrical Materials & Methods	12/1/2023		
260519	Low Voltage Electrical Power Conductors & Cables	12/1/2023		
260526	Grounding & Bonding For Electrical Systems	12/1/2023		
260529	Hangers & Supports For Electrical Systems	12/1/2023		
260533	Raceway & Boxes For Electrical Systems	12/1/2023		
260553	Electrical Identification	12/1/2023		
262213	Low Voltage Distribution Transformers	12/1/2023		
262416	Panelboards	12/1/2023		
262726	Wiring Devices	12/1/2023		
262800	Overcurrent Protective Devices	12/1/2023		
262816	Enclosed Switches & Circuit Breakers	12/1/2023		
265100	Interior Lighting	12/1/2023		
265200	Emergency Lighting	12/1/2023		

A.3.1.3 - DRAWINGS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #05 04/08/24



The Guaranteed Maximum Price is based upon the following Drawings:

Drawing No.	Drawing Title	Drawing Date	Revision
2INFO-1	GENERAL INFORMATION, DRAWING LIST, ABBREVIA	12/1/2023	
2INFO-2	WALL TYPES & SCHEDULES	12/1/2023	
CODE-101	FIRST FLOOR CODE PLAN	12/1/2023	
CODE-102	SECOND FLOOR CODE PLAN	12/1/2023	
HZ-104	FIRST FLOOR REMEDIATION PLAN	12/1/2023	
HZ-105	SECOND FLOOR REMEDIATION PLAN	12/1/2023	
HZ-106	TUNNEL LEVEL REMEDIATION PLAN	12/1/2023	
D-101.A	PARTIAL FIRST FLOOR UNIT A DEMOLITION PLAN	12/1/2023	
D-101.B	PARTIAL FIRST FLOOR UNIT B DEMOLITION PLAN	2/2/2024	1
D-101.C	PARTIAL FIRST FLOOR UNIT C1 DEMOLITION PLAN	12/1/2023	
D-101.D	PARTIAL FIRST FLOOR UNIT D DEMOLITION PLAN	5/4/2023	
2A-101.A	PARTIAL FIRST FLOOR PLAN - UNIT 'A'	2/2/2024	1
2A-101.B	PARTIAL FIRST FLOOR PLAN - UNIT 'B'	2/2/2024	1
2A-101.C	PARTIAL FIRST FLOOR PLAN - UNIT C	5/10/2023	
2A-101.D	PARTIAL FIRST FLOOR PLAN - UNIT 'D'	5/10/2023	
D-100	TUNNEL DEMOLITION PLAN	1/26/2024	1
D-101.A	PARTIAL FIRST FLOOR UNIT A DEMOLITION PLAN	12/1/2023	
D-101.B	PARTIAL FIRST FLOOR UNIT B DEMOLITION PLAN	12/1/2023	
D-101.C1	PARTIAL FIRST FLOOR UNIT C1 DEMOLITION PLAN	12/1/2023	
D-101.D	PARTIAL FIRST FLOOR UNIT D DEMOLITION PLAN	12/1/2023	
D-101	FIRST FLOOR WINDOW TREATMENT OVERALL DEMOLITIO	12/1/2023	
D-102	SECOND FLOOR WINDOW TREATMENT OVERALL DEMOLIT	12/1/2023	
D-102.B	SECOND FLOOR UNIT B DEMOLITION PLAN	12/1/2023	
D-102.C1	PARTIAL SECIOND FLOOR UNIT C1 & D DEMOLITION PLAN	12/1/2023	
D-102C2	PARTIAL SECOND FLOOR UNIT C2 DEMOLITION PLAN	12/1/2023	
2A-101.A	PARTIAL FIRST FLOOR PLAN - UNIT A	12/1/2023	
2A-101.B	PARTIAL FIRST FLOOR PLAN - UNIT B	12/1/2023	
2A-101.C1	PARTIAL FIRST FLOOR PLAN - UNIT C	1/26/2024	1
2A-1-1.D	PARTIAL FIRST FLOOR PLAN - UNIT D	12/1/2023	
2A-102.B/C	PARTIAL SECOND FLOOR PLAN - UNIT B/C & PARTIAL ROOI	2/2/2024	1
2A-102.D	PARTIAL SECOND FLOOR PLAN - UNIT D	12/1/2023	

A.3.1.3 - DRAWINGS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #05 04/08/24



The Guaranteed Maximum Price is based upon the following Drawings:

Drawing No.	. Drawing Title	Drawing Date	Revision
2A-201.A	PARTIAL FIRST FLOOR REFLECTED CEILING PLAN - UNIT A	12/1/2023	
2A-201.B	PARTIAL FIRST FLOOR REFLECTED CEILING PLAN - UNIT B	2/2/2024	1
2A-201.C1	PARTIAL FIRST & SECOND FLOOR REFLECTED CEILING PLAN	12/1/2023	
2A-201.D	PARTIAL FIRST FLOOR REFLECTED CEILING PLAN - UNIT D	12/1/2023	
A-250	DETAILS	12/1/2023	
A-601	ENLARGED TOILET ROOM PLANS, ELEVATIONS AND DETAIL	12/1/2023	
A-602	TOILET ROOM ELEVATIONS	12/1/2023	
A-801	INTERIOR ELEVATIONS	12/1/2023	
2A-901	DOOR SCHEDULES AND ELEVATIONS	2/2/2024	2
2A-950	DOOR DETAILS	12/1/2023	
A-990	WINDOW TREATMENT, NUMBERS & SIGNAGE FIRST FLOO	12/1/2023	
A-991	WINDOW TREATMENT, NUMBERS & SIGNAGE SECOND FLO	12/1/2023	
A-992	BUILDING SIGNAGE DETAILS	12/1/2023	
FI-101.A	PARTIAL FIRST FLOOR UNIT A FINISH PLAN	1/26/2024	1
FI-101.B	PARTIAL FIRST FLOOR UNIT B FINISH PLAN	2/2/2024	2
FI-101.C1	PARTIAL FIRST & SECOND FLOOR UNIT C FINISH PLAN	1/26/2024	1
FI-101.D	PARTIAL FIRST FLOOR UNIT D FINISH PLAN	1/26/2024	1
FI-901	FINISH LEGEND	2/2/2024	2
S-000	GENERAL NOTES	12/1/2023	
S-101.A	PARTIAL FOUNDATION AND ROOF FRAINING PLAN	2/2/2024	1
S-200	SECTIONS AND TYPICAL DETAILS	2/2/2024	1
DM-101-A	PARTIAL FIRST FLOOR A MECHANICAL DEMLITION PLAN	12/1/2023	
DM-101-B	PARTIAL FIRST & SECOND FLOOR B MECHANICAL DEMOLIT	2/2/2024	1
DM-101-C1	PARTIAL FIRST FLOOR C1 MECHANICAL DEMOLITION PLAN	12/1/2023	
DM-101-D	PARTIAL LEVEL D MECHANICAL DEMOLITION PLANS	1/26/2024	1
DM-201	ROOF MECHANICAL DEMOLITION PLAN	12/1/2023	
M-101-A	-PARTIAL-FIRST-FLOOR-A MECHANICAL PLAN	12/1/2023	
M-101-B	PARTIAL FIRST & SECOND FLOOR B MECHANICAL PLANS	2/2/2024	1
M-101-C1	PARTIAL FIRST FLOOR C1 MECHANICAL PLAN	2/2/2024	1
M-101-C2	PARTIAL FIRST FLOOR C2 MECHANICAL PLAN	2/2/2024	1
M-101-D	PARTIAL FIRST FLOOR D MECHANICAL PLANS	1/26/2024	1

A.3.1.3 - DRAWINGS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #05 04/08/24



The Guaranteed Maximum Price is based upon the following Drawings:

Drawing No.	Drawing Title	Drawing Date	Revision
M-201	ROOF MECHANICAL PLAN	2/2/2024	1
M-202	TUNNEL MECHANICAL PLAN	2/2/2024	1
M-203	TUNNEL MECHANICAL PLAN	1/26/2024	1
M-300.1	MECHANICAL VRF DIAGRAMS	2/2/2024	1
M-300.2	MECHANICAL DETAILS	1/26/2024	1
M-300.3	MECHANICAL SYMBOLS, NOTES, SCHEDULES AND ABBREV	2/2/2024	1
DP-101-A	PARTIAL FIRST FLOOR A PLUMBING DEMOLITION PLAN	12/1/2023	
DP-101-B	PARTIAL FIRST FLOOR B PLUMBING DEMOLITION PLAN	12/1/2023	
DP-101-C1	PARTIAL FIRST FLOOR C1 PLUMBING DEMOLITION PLAN	12/1/2023	
DP-101-D	PARTIAL FIRST FLOOR D PLUMBING DEMOLITION PLAN	12/1/2023	
P-101-A	PARTIAL FIRST FLOOR A PLUMBING PLANS	12/1/2023	
P-101-B	PARTIAL FIRST FLOOR PLUMBING PLANS	1/26/2024	1
P-101-C1	PARTIAL FIRST FLOOR C1 PLUMBING PLAN	1/26/2024	1
P-101-C2	PARTIAL FIRST FLOOR AREA C2 PLUMBING PLAN	2/2/2024	1
P-101-D	PARTIAL FIRST FLOOR D PLUMBING PLAN	12/1/2023	
P-200	PLUMBING SCHEDULES NOTES AND DETAILS	12/1/2023	
P-201	TUNNEL PLUMBING PLAN	1/26/2024	1
DE-101-A	PARTIAL FIRST FLOOR A ELECTRICAL DEMOLITION PLAN	12/1/2023	
DE-101-B	PARTIAL FIRST FLOOR B ELECTRICAL DEMOLITION PLAN	2/2/2024	2
DE-101-C1	PARTIAL FIRST FLOOR ELECTRICAL DEMOLITION PLAN	12/1/2023	
DE-101-D	PARTIAL FIRST FLOOR D ELECTRICAL DEMLITION PLAN	12/1/2023	
DE-201	ROOF ELECTRICAL DEMOLITION PLAN	12/1/2023	
E-101-A	PARTIAL FIRST FLOOR A ELECTRICAL PLAN	2/2/2024	2
E-101-B	PARTIAL FIRST & SECOND FLOORS B ELECTRICAL PLANS	2/2/2024	
E-101-C1	PARTIAL FIRST FLOOR C1 ELECTRICAL PLAN	2/2/2024	
E-101-C2	PARTIAL FIRST FLOOR AREA C2 ELECTRICAL PLAN	2/2/2024	
E-101-D	-PARTIAL-FIRST FLOOR D ELECTRICAL PLAN	12/1/2023	
E-201	ROOF ELECTRICAL PLAN	12/1/2023	
E-301-A	PARTIAL FIRST FLOOR A LIGHTING PLAN	12/1/2023	
E-301-B	PARTIAL FIRST FLOOR B LIGHTING PLAN	2/2/2024	1
E-301-C1	PARTIAL FIRST FLOOR C1 LIGHTING PLAN	12/1/2023	

A.3.1.3 - DRAWINGS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #05 04/08/24



The Guaranteed Maximum Price is based upon the following Drawings:

Drawing No.	Drawing Title	Drawing Date	Revision
E-301-D	PARTIAL FIRST FLOOR D LIGHTING PLAN	12/1/2023	
E-400	ELECTRICAL PANELBOARD	12/1/2023	
E-401	ELECTRICAL PANELBOARD & PARTIAL POWER RISER DIAGR	2/2/2024	1
E-500	ELECTRICAL SCHEDULES, DETAILS, SYMBOLS, NOTES AND	12/1/2023	

A.3.1.5 - ALLOWANCES

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #06 4/8/2024



Allowances Included in the Guaranteed Maximum Price, if any:

ALLOW BY BP	Description	QTY	UNIT	RATE	UNIT COST	TOTAL	ALLOWANCE NOTES
Project	Sitework & Concrete	1	LS		\$ 483,060.00	\$ 483,060	On GMP Summary
Project	Off-Hours Work / Supervision	1	LS		\$ 25,000.00	\$ 25,000	On GMP Summary
Project	Temp Enclosures	1	LS		\$ 25,000.00	\$ 25,000	On GMP Summary
Project	Misc. Cutting / Patching	1	LS		\$ 50,000.00	\$ 50,000	On GMP Summary
Project	Supplemental Steel / Supports	1	LŞ		\$ 75,000.00	\$ 75,000	On GMP Summary
Project	Misc. Fireproof Patching	1	LS		\$ 25,000.00	\$ 25,000	On GMP Summary
Project	Terrazzo Polishing / Repair	1	LS		\$ 150,000.00	\$ 150,000	On GMP Summary
Project	Temp Environmental Controls	1	LS		\$ 175,000.00	\$ 175,000	On GMP Summary
Project	Utility Fees	1	LS		\$ 20,000.00	\$ 20,000	On GMP Summary
2.4.1	Interior Masonry Wall Patching / Repair	150	Hrs.	\$ 112.00	\$ 10,000.00	\$ 26,800.00	In Trade Package
2.4.1	Crack Repair On Existing Masonry	80	Hrs.	\$ 112.00	\$ 6,000.00	\$ 14,960.00	In Trade Package

A.3.1.6 - ASSUMPTIONS AND CLARIFICATIONS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #07 04/08/24



Assumptions, if any, on which the Guaranteed Maximum Price is based:

ASSUMPTIONS/QUALIFICATIONS

- The GMP value is contingent upon our ability to execute contracts with the recommended Trade Contractors listed in A.1.1.2 GUARANTEED MAXIMUM PRICE. In the event of withdrawal of a bid by a trade contractor listed in A.1.1.2 GUARANTEED MAXIMUM PRICE an adjustment to the GMP value will be required to accommodate the next lowest responsible bidder.
- 2 General Notes & Key Notes on the Drawings are superseded by these assumptions & qualifications.
- 3 Not used
- 4 It is assumed that the supports and structures specified are suitable and compatible for all systems and components.
- 5 Not used.
- Retainage will be held on Subcontractor trade contract line items and shall not be held on the Construction Manager items, ie Insurance, Bond, General Conditions, CM Fee, etc.. CM Self Performance Trade line items will also have retainage witheld
- 7 Warranties shall begin on the date of Substantial Completion.
- **8** Allowance relocations within the GMP may be permitted. Any additional funding that is required for allowances will be from the Owner's contingency. Any remaining funds within allowances at project conclusion will be credited to the Owner.
- Where there is a conflict with Division 1 and the Downes Project Manual and Supplemental Instructions, the Downes Project Manual & Supplemental Instructions shall prevail.
- All permanent & temporary energy and fuel utility consumption fees and metering (electric, water, propane, gas, etc.) will be paid by Owner.
- Working Hours are 7:00am to 3:30pm Monday through Friday only.
- The Construction Manager assumes they will be able to perform allowance work as they deem necessary without hinderance. Proper notification will be provided to the project team prior to start of work for any allowance and accounting of allowance expenditures on a monthly basis.
- If the Construction Manager is delayed by supply chain shortages, significant price increases for materials, tarrifs, unusual delay in deliveries or other causes related to the COVID-19 Pandemic, the Construction manager shall be entitled to an equitable adjustment in contract time and sum.
- Project Schedule and Cost is subject to adjustment based on approvals form the Town, State, Utility and all Authorities Having Jurisdiction.
- It is assumed the existing structure has been evaluated by the EOR to support and / or attach new construction. No additional engineering analysis of the existing structure has been included in the GMP.
- The existing buildings systems may be used for and to support temporary power, domestic water, heating and cooling at no cost to the Construction Manager.
- 17 Not used.
- 18 -- It-is-assumed all design documents have been coordinated-with the Town's-Standards and requirements.
 - The Owner is responsible to remove, relocate and/or reinstall all loose furnishings from the interior and exterior of the buildings in coordination with the Contruction Manager's schedule. The Construction Manager will endeavor to provide advanced notice and coordinate directly with the appropriate personnel on timing.
 - 20 Salvaging of items are per the Contract Documents only.

A.3.1.6 - ASSUMPTIONS AND CLARIFICATIONS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE. EXHIBIT A1 - GMP - ATTACHMENT #07 04/08/24



- Coordination of the Division 26, 27 and 28 Design & Engineering Responsibilities is assumed to be completed by the Design Team. Conflicts, errors or ommissions in the design leaving a system non-functional or incomplete shall be funded from the owners contingency.
- 22 Project Management software will be Procore. GC Pay will be used for Applications for Payment.
- 23 Certified payrolls will be accepted by the Town electronically.
- Payment applications will be accepted electronically with one Construction Manager original. All backup will be scanned copies.

25

Not used.

- 26 It is assumed that IAQ testing will be performed and monitored by the owner's consultant during construction.
- 27 Not used.
- PH1 Amendment remaining/unspent contingencies and allowances will be merged with this PH2 Amendment.
- The cleaning of the roof will consist of a blower and sweep of the roof, no scrubbing or washing of the roofing system is included. Lighter color PVC or EPDM roofs if specified will result in staining that cannot be removed.
- 30 Not used.
- 31 Not used.
- 32 Due to material cost escalation, any alternate prices listed as TBD are subject to change.
- Phases established in the construction schedule may change.
- The sitework and concrete portions of work including but not limited to interior trenching, concrete infills, interior footings, underpinning, asphalt patching, line striping, site prep has been carried as an allowance within the GMP. Execution of this work is dependent upon trades available to perform the work and may result in a change order to a specific trade already awarded a contract for other portions of work unrelated to sitework and concrete activities.
- The base bid work associated with terrazzo polishing and repair has been carried as an allowance within the GMP due to this scope not being included in a trade package following scope review with the low bid flooring subcontractor.
- The base bid work associated with terrazzo polishing and repair has been carried as an allowance within the GMP due to this scope not being included in a trade package following scope review with the low bid flooring subcontractor.
- The base bid work associated with structural steel & misc metal being awarded to Berlin Steel is limited to furnishing and installing new steel beam/columns associated with new steel reinforcement work within the proposed wrestling room. All other work related to steel / misc. metals has been carried as an allowance within the GMP.
- Any existing condition within the tunnels that may require repair such as loose/broken pipe fittings, missing hangars, missing /rotted piping, etc. is not part of any base bid work awarded to any subcontractor. It is anticipated that the repairs can be addressed within the GMP allowance for "MEP Relocations / Repairs".
- 39 Manufactured casework is being provided for rooms 187A & 237 only. Custom cabinetry is not being provided at these locations.
- Fireproofing that may be required is unknown at this time given the fact that locations can not be clearly identified until removal—/ demo has taken place. It is assumed that any fireproof patching that will be required is covered by the GMP—allowance carried for fireproof patching.
- Painting is limited to rooms identified within the finish schedule only and does not include every room in the building.

EXCLUSIONS

1 Handling, Transportation and Disposal of unsuitable, contaminated or polluted soils are excluded.

A.3.1.6 - ASSUMPTIONS AND CLARIFICATIONS

KILLINGLY COMMUNITY CENTER - 79 WESTFIELD AVE.

EXHIBIT A1 - GMP - ATTACHMENT #07

- 04/08/24
 - 2 Not used.
 - FF&E or owner furnished items called to be installed by the contractor, GC or CM in the documents that are not clearly indicated on the drawings are excluded.
 - 4 Not used.
 - 5 Not used.
 - Work stoppage and its potential effect on contract time and cost due to neighbor/community disagreements or disputes not caused by the Construction Manager are excluded.
 - 7 Materials Testing and Inspection and Special Inspection services are excluded.
 - 8 RFI Questions/Answers not included in Addenda are excluded.
 - 9 Resource loaded and/or man-loaded schedules are excluded.
 - Builders Risk is excluded. It is assumed the Town will provide a Builders Risk policy and is recommended to do so.
 - 11 Not used.
 - 12 Professional photography services are excluded. Photos by Superintendent.
 - 13 Legal council fees associated with review of town resolution, and any associated revisions necessary for GMP approval.
 - 14 Connecticut Sales and Use Tax excluded.
 - 15 Professional services for High Performance or LEED management are excluded.
 - 16 Off-Hours security personnel are excluded.
 - 17 Not used.
 - 18 Not used.
 - Moving services and storage requirements to accommodate phased construction are excluded. All furniture, loose items and technology items will be relocated and re-installed as required by others. The Construction Manager will endeavor to provide advanced notice and coordinate directly with the appropriate personnel on timing.
 - 20 Rock removal is excluded.
 - 21 Liquidated Damages are excluded for this Amendment.
 - 22 AISC certification has been excluded.
 - 23 Fire protection installation, repair, relocation, etc. is excluded.
 - Visual display of any type has been excluded.
 - 25 Fire extinguisher cabinets / fire extinguishers are excluded.
 - Locker installation, removal, relocation, repair is excluded.
 - 27 ACM monitoring is excluded (by owner).





March 20, 2024

ANTIA22005 (CO#01)

ANTINOZZI ASSOCIATES

ARCHITECTURE & INTERIORS
Michael Losasso, AIA, LEEDI AP BD+C
Principal
MLosasso@Antinozzi.com

RE:

Abatement Monitoring - Change Order Westfield Ave. Community Center 79 Westfield Avenue Killingly, CT 06239

The estimated cost for the abatement time frame, based on the attached email and phase drawings, is as follows:

School-in-Session Application for All Phases (Assumes State will allow one application)
School in Session Application & Visit w/ State = \$1,800.00

Phase 1A (Estimated 3 weeks for interior & 2 weeks for exterior abatement, no weekends)

25 weekdays of monitoring @ 700.00/8-hour day =	\$17,500.00
6 project management site visits at \$600/visit =	\$3,600.00
8 perimeter PCM samples per day @ \$15/sample =	\$3,000.00
2 TEM Clearances @ \$800/clearance =	\$1,600.00
Estimated Total for Phase 1A	\$25,700.00

Phase 1B (Estimated 3 weeks for interior & 2 weeks for exterior abatement, no weekends)

25 weekdays of monitoring @ 700.00/8-hour day =	\$17,500.00
6 project management site visits at \$600/visit =	\$3,600.00
8 perimeter PCM samples per day @ \$15/sample =	\$3,000.00
2 TEM Clearances @ \$800/clearance =	\$1,600.00
Estimated Total for Phase 1B	\$25,700.00

Phase 2A (Estimated 4 weeks for interior & 2 weeks for exterior abatement, no weekends)

30 weekdays of monitoring @ 700.00/8-hour day =	\$21,000.00
7 project management site visits at \$600/visit =	\$4,200.00
8 perimeter PCM samples per day @ \$15/sample =	\$3,600.00
2 TEM Clearances @ \$800/clearance =	\$1,600.00
Estimated Total for Phase 2A	\$30,400.00

ANTIA22005 (CO#01)
Antinozzi Associates

March 20, 2024

Westfield Ave Community Center, Killingly, CT

Page 2 Project Monitoring

Phase 2B (Estimated 4 weeks for interior & 2 weeks for exterior about 30 weekdays of monitoring @ 700.00/8-hour day =	\$21,000.00		
7 project management site visits at \$600/visit =	\$4,200.00		
8 perimeter PCM samples per day @ \$15/sample =	\$3,600.00		
2 TEM Clearances @ \$800/clearance =	\$1,600.00		
Estimated Total for Phase 2B	\$30,400.00		
Phase 3 (Estimated 2 weeks for interior & 2 weeks for exterior abat	ement, no weekends)		

Phase 3 (Estimated 2 weeks for interior & 2 weeks for exterior abatement	t, no weekends)
20 weekdays of monitoring @ 700.00/8-hour day =	\$14,000.00
4 project management site visits at \$600/visit =	\$2,400.00
8 perimeter PCM samples per day @ \$15/sample =	\$2,400.00
O TENA Olegania de O O O O O O O O O O O O O O O O O O	01 600 00

<u>2 TEM Clearances @ \$800/clearance = \$1,600.00</u> Estimated Total for Phase 3 \$20,400.00

Final Closeout Report

Final Closeout Report for Remaining Phases \$3,500.00

Unit Rates for Miscellaneous Item

a. Day rate is based on an 8-hour shift. Overtime will be billed at time and a half.

b. Overnight Saturday Shipping Unit Price \$50.00/package

c. Courier of Samples Unit Price Cost + 20%

d. TEM Air Sample Analysis (NIOSH 7402) \$240.00/sample

(Only needed for an elevated perimeter air sample, includes FedEx Delivery + Rush TAT)

Project Monitoring

PROVIDED SCHEDULING INFORMATION

From: Doug Triba
To: Michael Losasso

Cc: David Ferris; James Twitchell; Frank Tomcak
Subject: RE: Westfield Ave. Abatement Monitoring
Date: Wednesday, March 20, 2024 1:20:57 PM

Attachments: image001.png

Killingly Westfield Ave Phasing Plan 2023-08-24.pdf

Of course. Jim can call Joe anytime.

I have attached out latest phasing plan that was developed back in August 23. We will be revising this shortly to reflect more accurate dates, but the durations should remain.

Douglas Triba
Project Manager
DOWNES CONSTRUCTION COMPANY
An Employee Owned Company **Building Excellence Since 1934**

New Britain, CT | Providence, RI | Warwick, RI

p. 860.229.3755 | m. 860.682.2997 | www.downesco.com

Check us out on Linked in

The information contained in this transmission is intended only for the person(s) or entity to which it is addressed and may contain confidential and/or privileged material. If you are not the intended recipient of this information, do not review, retransmit, disclose, disseminate, use, or take any action in reliance upon this information. If you received this transmission in error, please contact the sender, destroy all printed copies, and delete the material from all computers. Views of individuals herein do not necessarily reflect those of the Downes Companies. This email does not constitute a binding offer, acceptance, amendment, waiver, or other agreement, unless such intention is clearly stated in the email. As good computing practice you should conduct your own virus checking. Please note that we may monitor, in accordance with applicable law, emails we receive. Downes Construction Company, LLC is an Affirmative Action/Equal Opportunity Employer.

From: Michael Losasso < Mlosasso @antinozzi.com>

Sent: Wednesday, March 20, 2024 1:08 PM **To:** Doug Triba <dtriba@downesco.com>

Cc: David Ferris < DFerris@antinozzi.com>; James Twitchell < jtwitchell@pennoni.com>; Frank

Tomcak <ftomcak@downesco.com>

Subject: RE: Westfield Ave. Abatement Monitoring

Hi Doug,

Would it be acceptable to Downes if Jim Twitchell contacted Spectrum for additional details on the abatement schedule? I have attached the latest copy of the latest version of the Phasing Plan that

we have on file. Is there a more recent version?

Thank you, Michael

Michael LoSasso, AIA, LEED AP BD+C Principal

ANTINOZZI ASSOCIATES

ARCHITECTURE + INTERIORS MAIN (203) 377-1300 x2436 DIRECT (203) 551-2436

From: James Twitchell < <u>ITwitchell@Pennoni.com</u>>
Sent: Wednesday, March 20, 2024 12:24 PM
To: Michael Losasso < <u>Mlosasso@antinozzi.com</u>>

Cc: David Ferris < <u>DFerris@antinozzi.com</u>>

Subject: RE: Westfield Ave. Abatement Monitoring

CAUTION. This email originated from outside of the organization.

Is it ok to reach out to Spectrum to clarify this with them? I need to figure out if it is 5 weeks for Phase 1A or 3 and the exterior overlaps. Also will need to ask about weekends.

Is there are drawing that shows the phases?

James Twitchell

Senior Industrial Hygienist/ Office Director

Pennoni

49 Woodside Street | Stamford, CT 06902

Direct: +1 203-487-8665 | **Mobile:** +1 203-554-1249 www.pennoni.com | JTwitchell@Pennoni.com

From: Michael Losasso < Mlosasso@antinozzi.com > Sent: Wednesday, March 20, 2024 11:46 AM

To: James Twitchell < JTwitchell@Pennoni.com > Cc: David Ferris < DFerris@antinozzi.com >

Subject: FW: Westfield Ave. Abatement Monitoring

Jim,

Downes has provided the following durations for abatement listed at the bottom of this email chain. It is not as detained as what was provided for KMS. Can you develop your monitoring fee proposal for Westfield Ave. based on these amounts?

Thanks, Michael

Michael LoSasso, AIA, LEED AP BD+C

Principal

ANTINOZZI ASSOCIATES

ARCHITECTURE + INTERIORS
MAIN (203) 377-1300 x2436
DIRECT (203) 551-2436

From: Doug Triba < dtriba@downesco.com
Sent: Wednesday, March 20, 2024 10:50 AM
To: Michael Losasso < Mlosasso@antinozzi.com
Subject: FW: Westfield Ave. Abatement Monitoring

CAUTION. This email originated from outside of the organization.

Mike,

Please see durations below from the abatement contractor.

Douglas Triba
Project Manager
DOWNES CONSTRUCTION COMPANY
An Employee Owned Company

Building Excellence Since 1934
New Britain, CT | Providence, RI | Warwick, RI

p. 860.229.3755 | m. 860.682,2997 | <u>www.downesco.com</u>

Check us out on Linked in

The information contained in this transmission is intended only for the person(s) or entity to which it is addressed and may contain confidential and/or privileged material. If you are not the intended recipient of this information, do not review, retransmit, disclose, disseminate, use, or take any action in reliance upon this information. If you received this transmission in error, please contact the sender, destroy all printed copies, and delete the material from all computers. Views of individuals herein do not necessarily reflect those of the Downes Companies. This email does not constitute a binding offer, acceptance, amendment, waiver, or other agreement, unless such intention is clearly stated in the email. As good computing practice you should conduct your own virus checking. Please note that we may monitor, in accordance with applicable law, emails we receive. Downes Construction Company, LLC is an Affirmative Action/Equal Opportunity Employer.

From: Doug Triba

Sent: Friday, March 1, 2024 2:42 PM

To: Frank Tomcak <ftomcak@downesco.com>

Subject: RE: Westfield Ave. Abatement Monitoring

I got the following durations from Joe Villano

Phase 1A

Interior 3 weeks
Exterior 2 weeks

Phase 1B

Interior 3 weeks
Exterior 2 weeks

Phase 2A

Interior 4 weeks Exterior 2 weeks

Phase 2B

Interior 4 weeks Exterior 2 weeks

Phase 3

Interior 2 weeks
Exterior 2 weeks

Douglas Triba
Project Manager
DOWNES CONSTRUCTION COMPANY
An Employee Owned Company

Building Excellence Since 1934New Britain, CT | Providence, RI | Warwick, RI
p. 860.229.3755 | m. 860.682.2997 | www.downesco.com

Check us out on Linked in

The information contained in this transmission is intended only for the person(s) or entity to which it is addressed and may contain confidential and/or privileged material. If you are not the intended recipient of this information, do not review, retransmit, disclose, disseminate, use, or take any action in reliance upon this information. If you received this transmission in error, please contact the sender, destroy all printed copies, and delete the material from all computers. Views of individuals herein do not necessarily reflect those of the Downes Companies. This email does not constitute a binding offer, acceptance, amendment, waiver, or other agreement, unless such intention is clearly stated in the email. As good computing practice you should conduct your own virus checking. Please

note that we may monitor, in accordance with applicable law, emails we receive. Downes Construction Company, LLC is an Affirmative Action/Equal Opportunity Employer.

From: Frank Tomcak <ftomcak@downesco.com Sent: Thursday, February 29, 2024 7:50 AM

To: Doug Triba dtriba@downesco.com

Subject: FW: Westfield Ave. Abatement Monitoring

FYI – I thought Joe Vilano had commented on this a while ago. Can you touch base with him and see if he has tentative durations? As long as scope checks out for phase 2 we will be using Spectrum for all abatement work.

Frank J. Tomcak, Project Executive DOWNES CONSTRUCTION COMPANY An Employee Owned Company

Building Excellence Since 1934 New Britain, CT | Providence, RI | Warwick, RI

p. 860.229.3755 | f. 860.225.3617 | m. 860.681.9413 | <u>www.downesco.com</u>

Check us out on Linked in

From: Michael Losasso < Mlosasso@antinozzi.com >

Sent: Tuesday, January 30, 2024 11:21 AM **To:** Frank Tomcak ftomcak@downesco.com

Cc: 'Mary Bromm (MBromm@killinglyct.gov)' <MBromm@killinglyct.gov>; Doug Triba

dtriba@downesco.com">dtriba@downesco.com; David Ferris DFerris@antinozzi.com>

Subject: Westfield Ave. Abatement Monitoring

Frank,

As we approach abatement at 79 Westfield Ave., Killingly will need to decide who will provide abatement monitoring. Because the building is occupied by EASTCONN throughout most of the year, the KMS 4th grade for the regular school year, and the BoE Offices, this facility will need to be treated as an abatement while school is in session. Whether the PBC choses to consult Hygenix's services as an extension of our agreement or bid the work competitively, we will need a current construction schedule and, ideally, the Abatement Contractor's anticipated durations.

We understand that the Phase 1 abatement was awarded to Spectrum. According to the attached schedule included with the DD Estimate, Phase 2 and Phase 3 abatement will follow without interruption. Please confirm this represents the most current project schedule for 79 Westfield Ave. Please also request Spectrum's abatement schedule for Phase 1 in order that we might budget for these activities.

Thank you, Michael

Michael LoSasso, AIA, LEED AP BD+C Principal

ANTINOZZI ASSOCIATES

ARCHITECTURE + INTERIORS
271 Fairfield Avenue
Bridgeport, Connecticut 06604
MAIN (203) 377-1300 x2436
DIRECT (203) 551-2436
FAX (203) 378-3002
www.antinozzi.com

The information contained in this transmission is intended only for the person(s) or entity to which it is addressed and may contain confidential and/or privileged material. If you are not the intended recipient of this information, do not review, retransmit, disclose, disseminate, use, or take any action in reliance upon this information. If you received this transmission in error, please contact the sender, destroy all printed copies, and delete the material from all computers. Views of individuals herein do not necessarily reflect those of the Downes Companies. This email does not constitute a binding offer, acceptance, amendment, waiver, or other agreement, unless such intention is clearly stated in the email. As good computing practice you should conduct your own virus checking. Please note that we may monitor, in accordance with applicable law, emails we receive. Downes Construction Company, LLC is an Affirmative Action/Equal Opportunity Employer.

The information contained in this transmission is intended only for the person(s) or entity to which it is addressed and may contain confidential and/or privileged material. If you are not the intended recipient of this information, do not review, retransmit, disclose, disseminate, use, or take any action in reliance upon this information. If you received this transmission in error, please contact the sender, destroy all printed copies, and delete the material from all computers. Views of individuals herein do not necessarily reflect those of the Downes Companies. This email does not constitute a binding offer, acceptance, amendment, waiver, or other agreement, unless such intention is clearly stated in the email. As good computing practice you should conduct your own virus checking. Please note that we may monitor, in accordance with applicable law, emails we receive. Downes Construction Company, LLC is an Affirmative Action/Equal Opportunity Employer.

The information contained in this transmission is intended only for the person(s) or entity to which it is addressed and may contain confidential and/or privileged material. If you are not the intended recipient of this information, do not review, retransmit, disclose, disseminate, use,

or take any action in reliance upon this information. If you received this transmission in error, please contact the sender, destroy all printed copies, and delete the material from all computers. Views of individuals herein do not necessarily reflect those of the Downes Companies. This email does not constitute a binding offer, acceptance, amendment, waiver, or other agreement, unless such intention is clearly stated in the email. As good computing practice you should conduct your own virus checking. Please note that we may monitor, in accordance with applicable law, emails we receive. Downes Construction Company, LLC is an Affirmative Action/Equal Opportunity Employer.

